
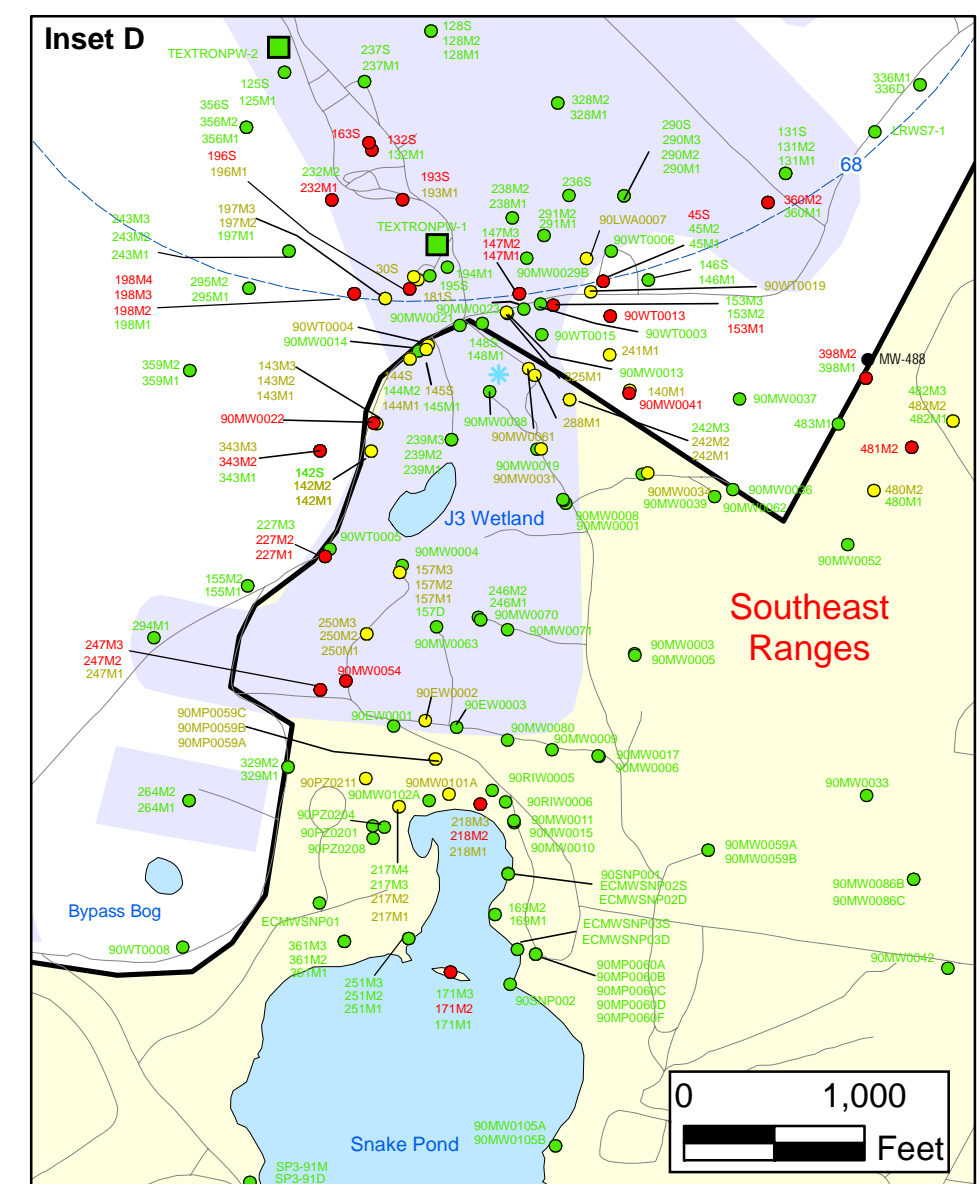
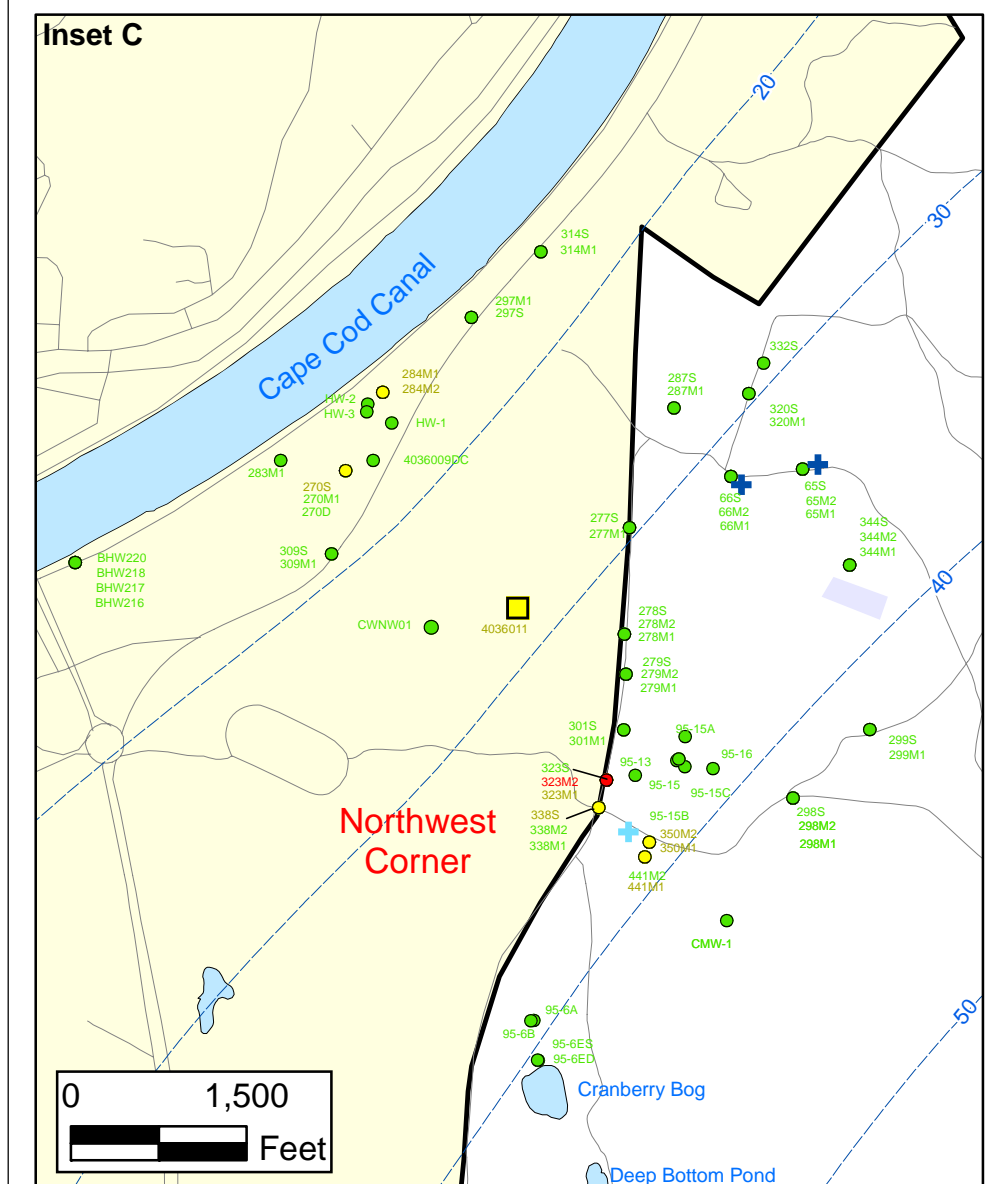


Explosives in Groundwater Compared to Maximum Contaminant Level/Health Advisories
Validated Data as of 5/25/07

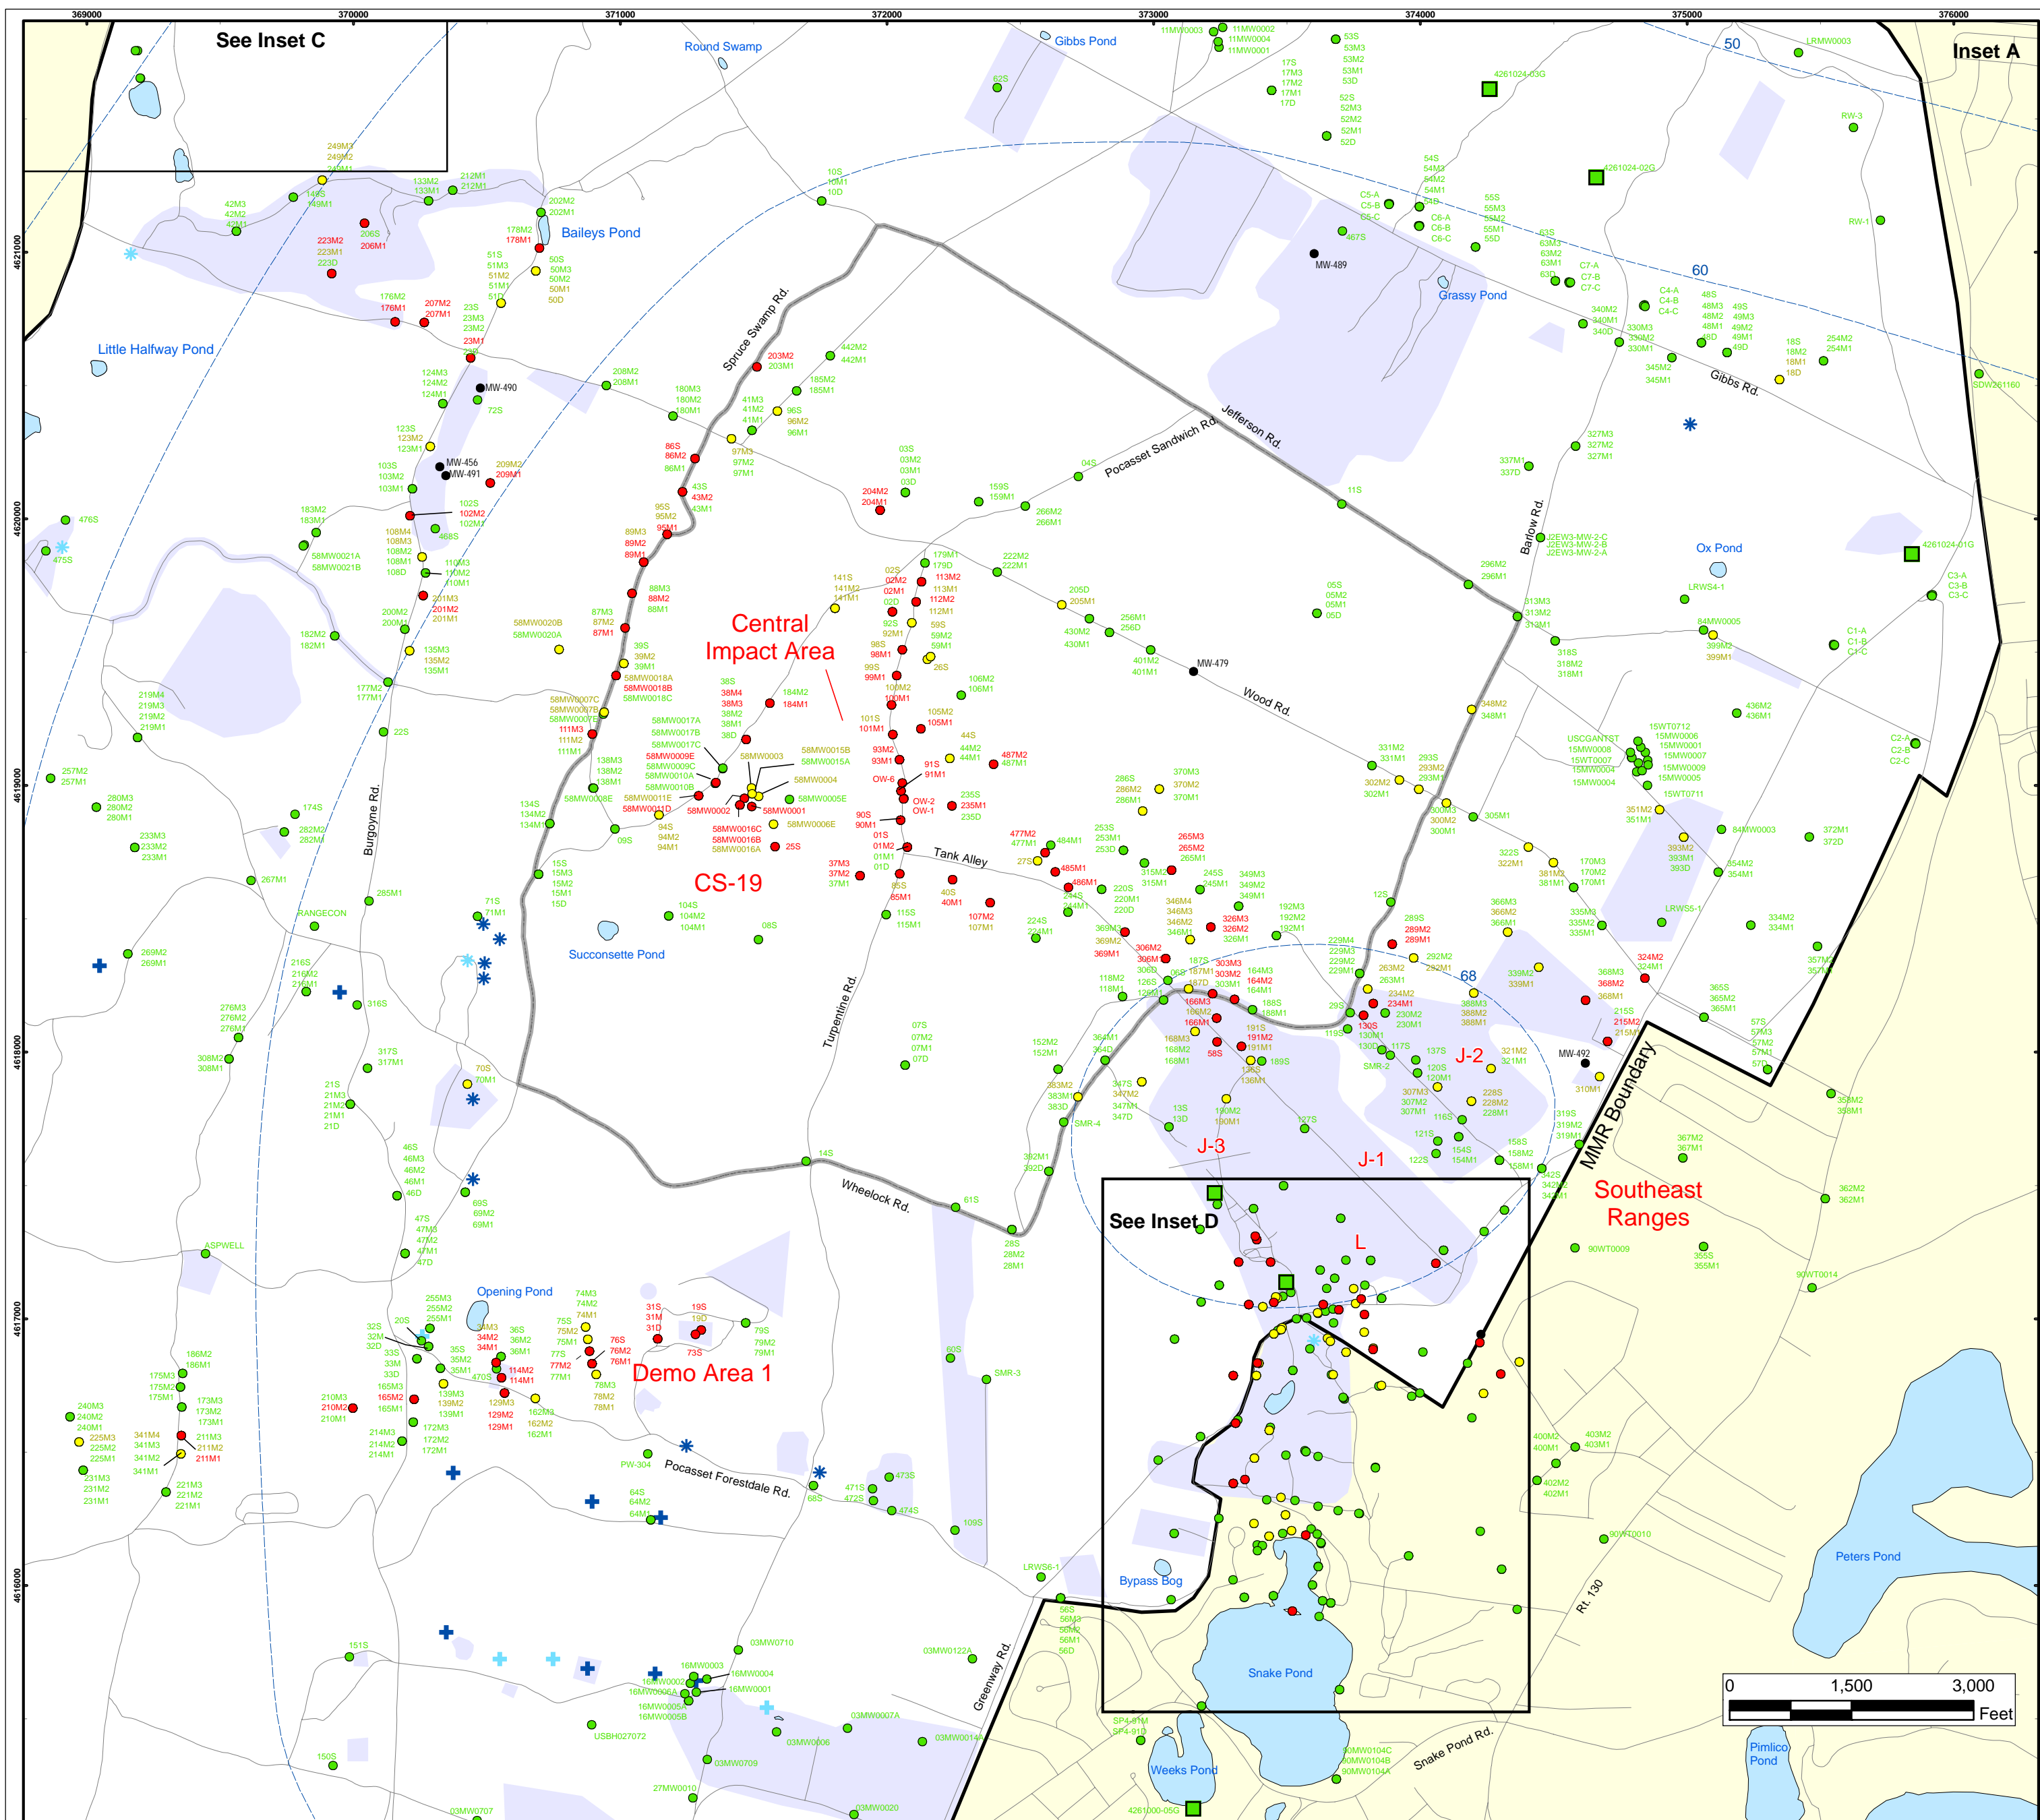

Explosives in Groundwater Compared to Maximum Contaminant Level/Health Advisories

Validated Data as of 5/25/07

- Validated Detection Greater than or Equal to Maximum Contaminant Level/Health Advisories
- Validated Detection Less than Maximum Contaminant Level/Health Advisories
- Validated Non-Detect
- Data Pending
- Proposed Monitoring Well
- Military Range Areas
- + Current Gun Position
- * Current Mortar Position
- + Old Gun Position
- * Old Mortar Position
- Validated Non-Detect Water Supply Well
- Validated Detection Less than Maximum Contaminant Level/Health Advisories Water Supply Well
- Water Table Contour (Feet NGVD), AMEC, September 2003

Note: Map dot colors are representative of the highest historical concentration at each well and not the current concentration level. Historical data presented on this figure range from November 1996 through 2007.


**Impact Area
Groundwater Study Program**

AMEC Earth & Environmental, Inc.
Westford, Massachusetts

**FIGURE
1**

Inset Map

Sources & Notes
Base map data from US Geological Survey
7 1/2 minute Topographic Maps
Source: Office of Geographic and
Environmental Information (MassGIS)
Commonwealth of Massachusetts
Executive Office of Environmental Affairs

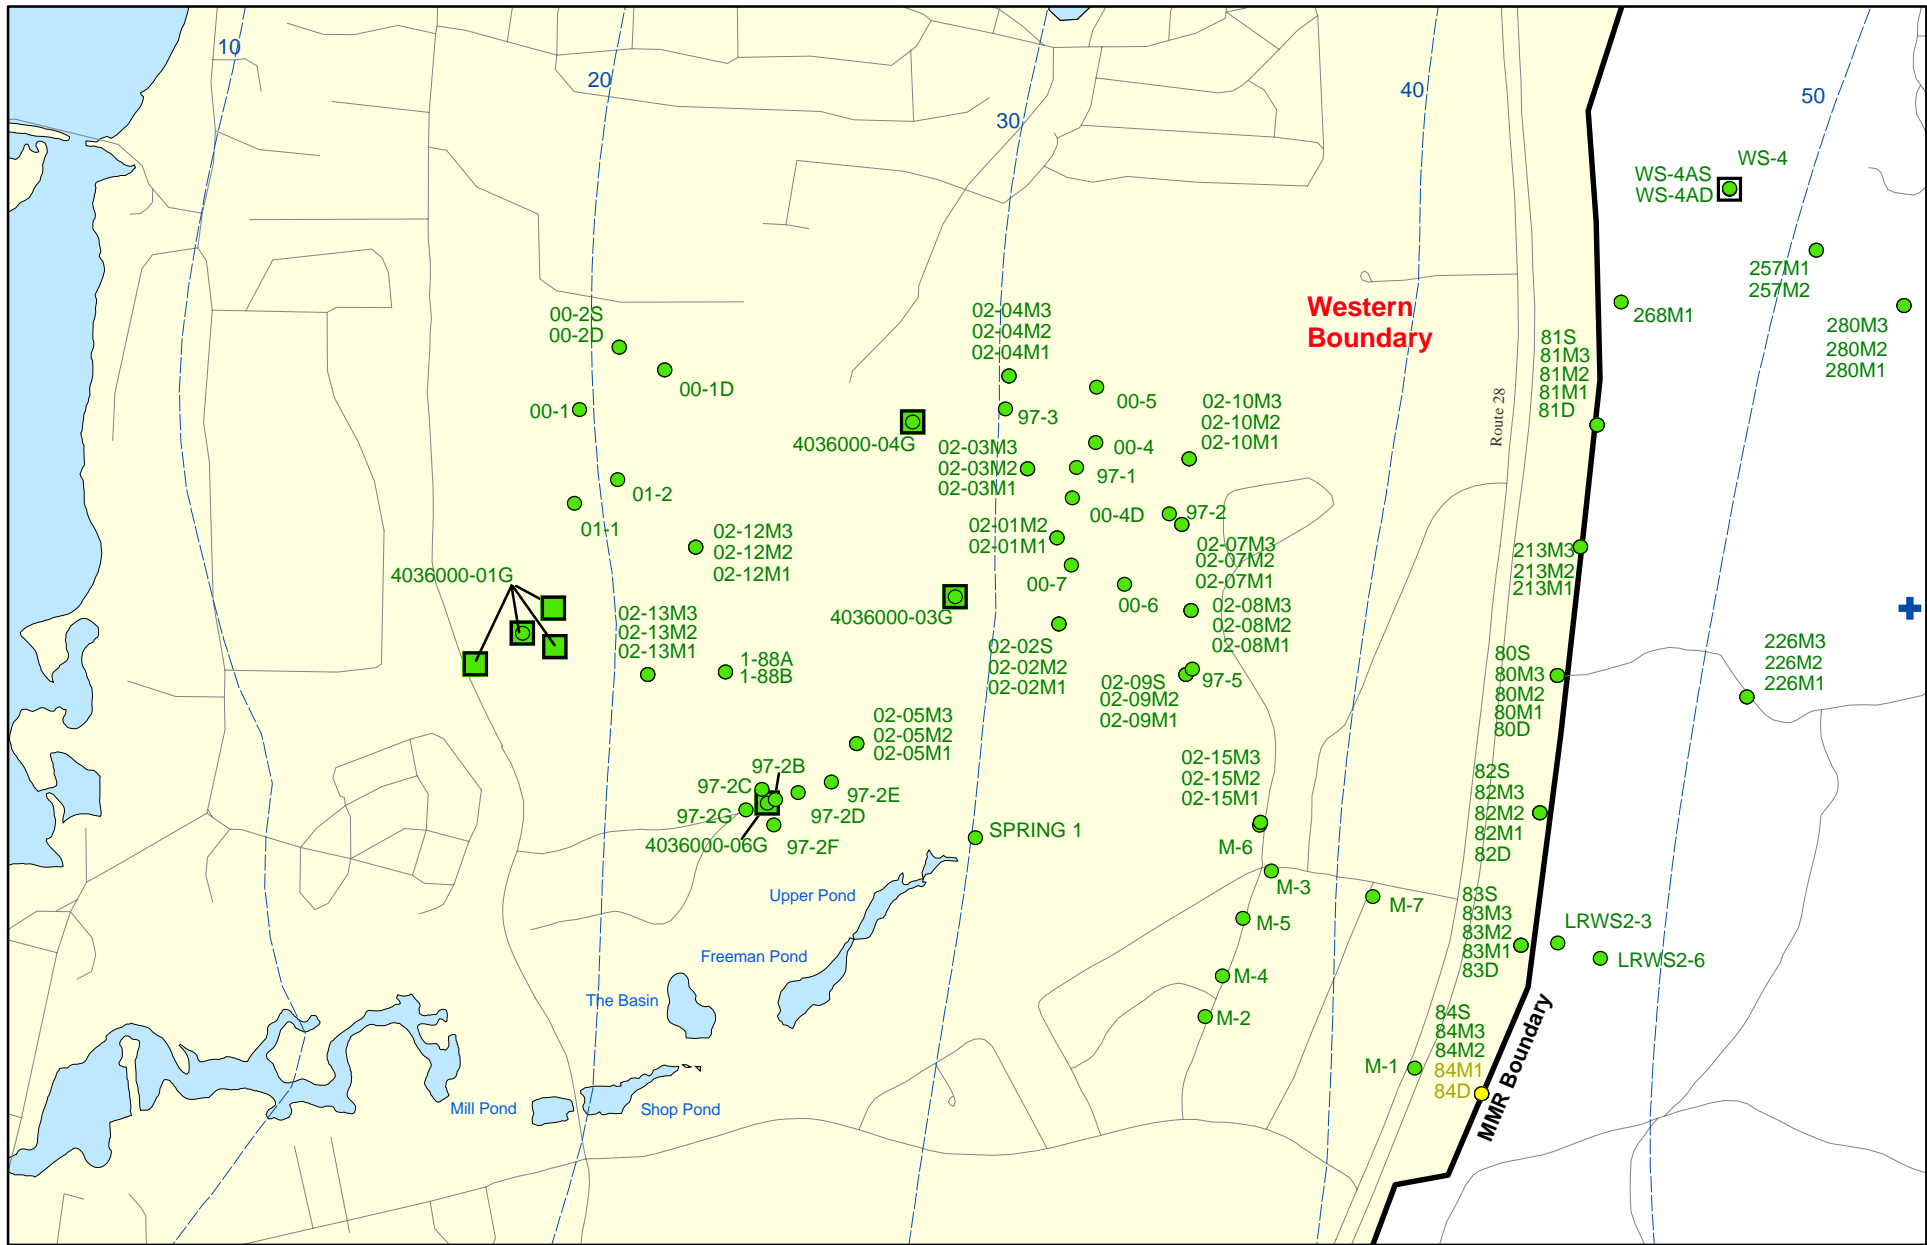


Sources & Notes:
 Base map data from US Geological Survey
 7 1/2 minute Topographic maps
 Source: Office of Geographic and
 Environmental Information (MassGIS)
 Commonwealth of Massachusetts
 Executive Office of Environmental Affairs

AMEC Earth & Environmental, Inc.
 Westford, Massachusetts


- Validated Detection Less than Maximum Contaminant Level/Health Advisories
- Validated Non-Detect
- + Current Gun Position
- Validated Non-Detect Water Supply Well
- Proposed Water Supply Well
- Water Table Contour (Feet NGVD)
 AMEC, September 2003

Note: Map dot colors are representative of the highest historical concentration at each well and not the current concentration level. Historical data presented on this figure range from November 1996 through 2007.

Explosives in Groundwater Compared to Maximum Contaminant Level/Health Advisories Validated Data as of 5/25/07



Inset Map B

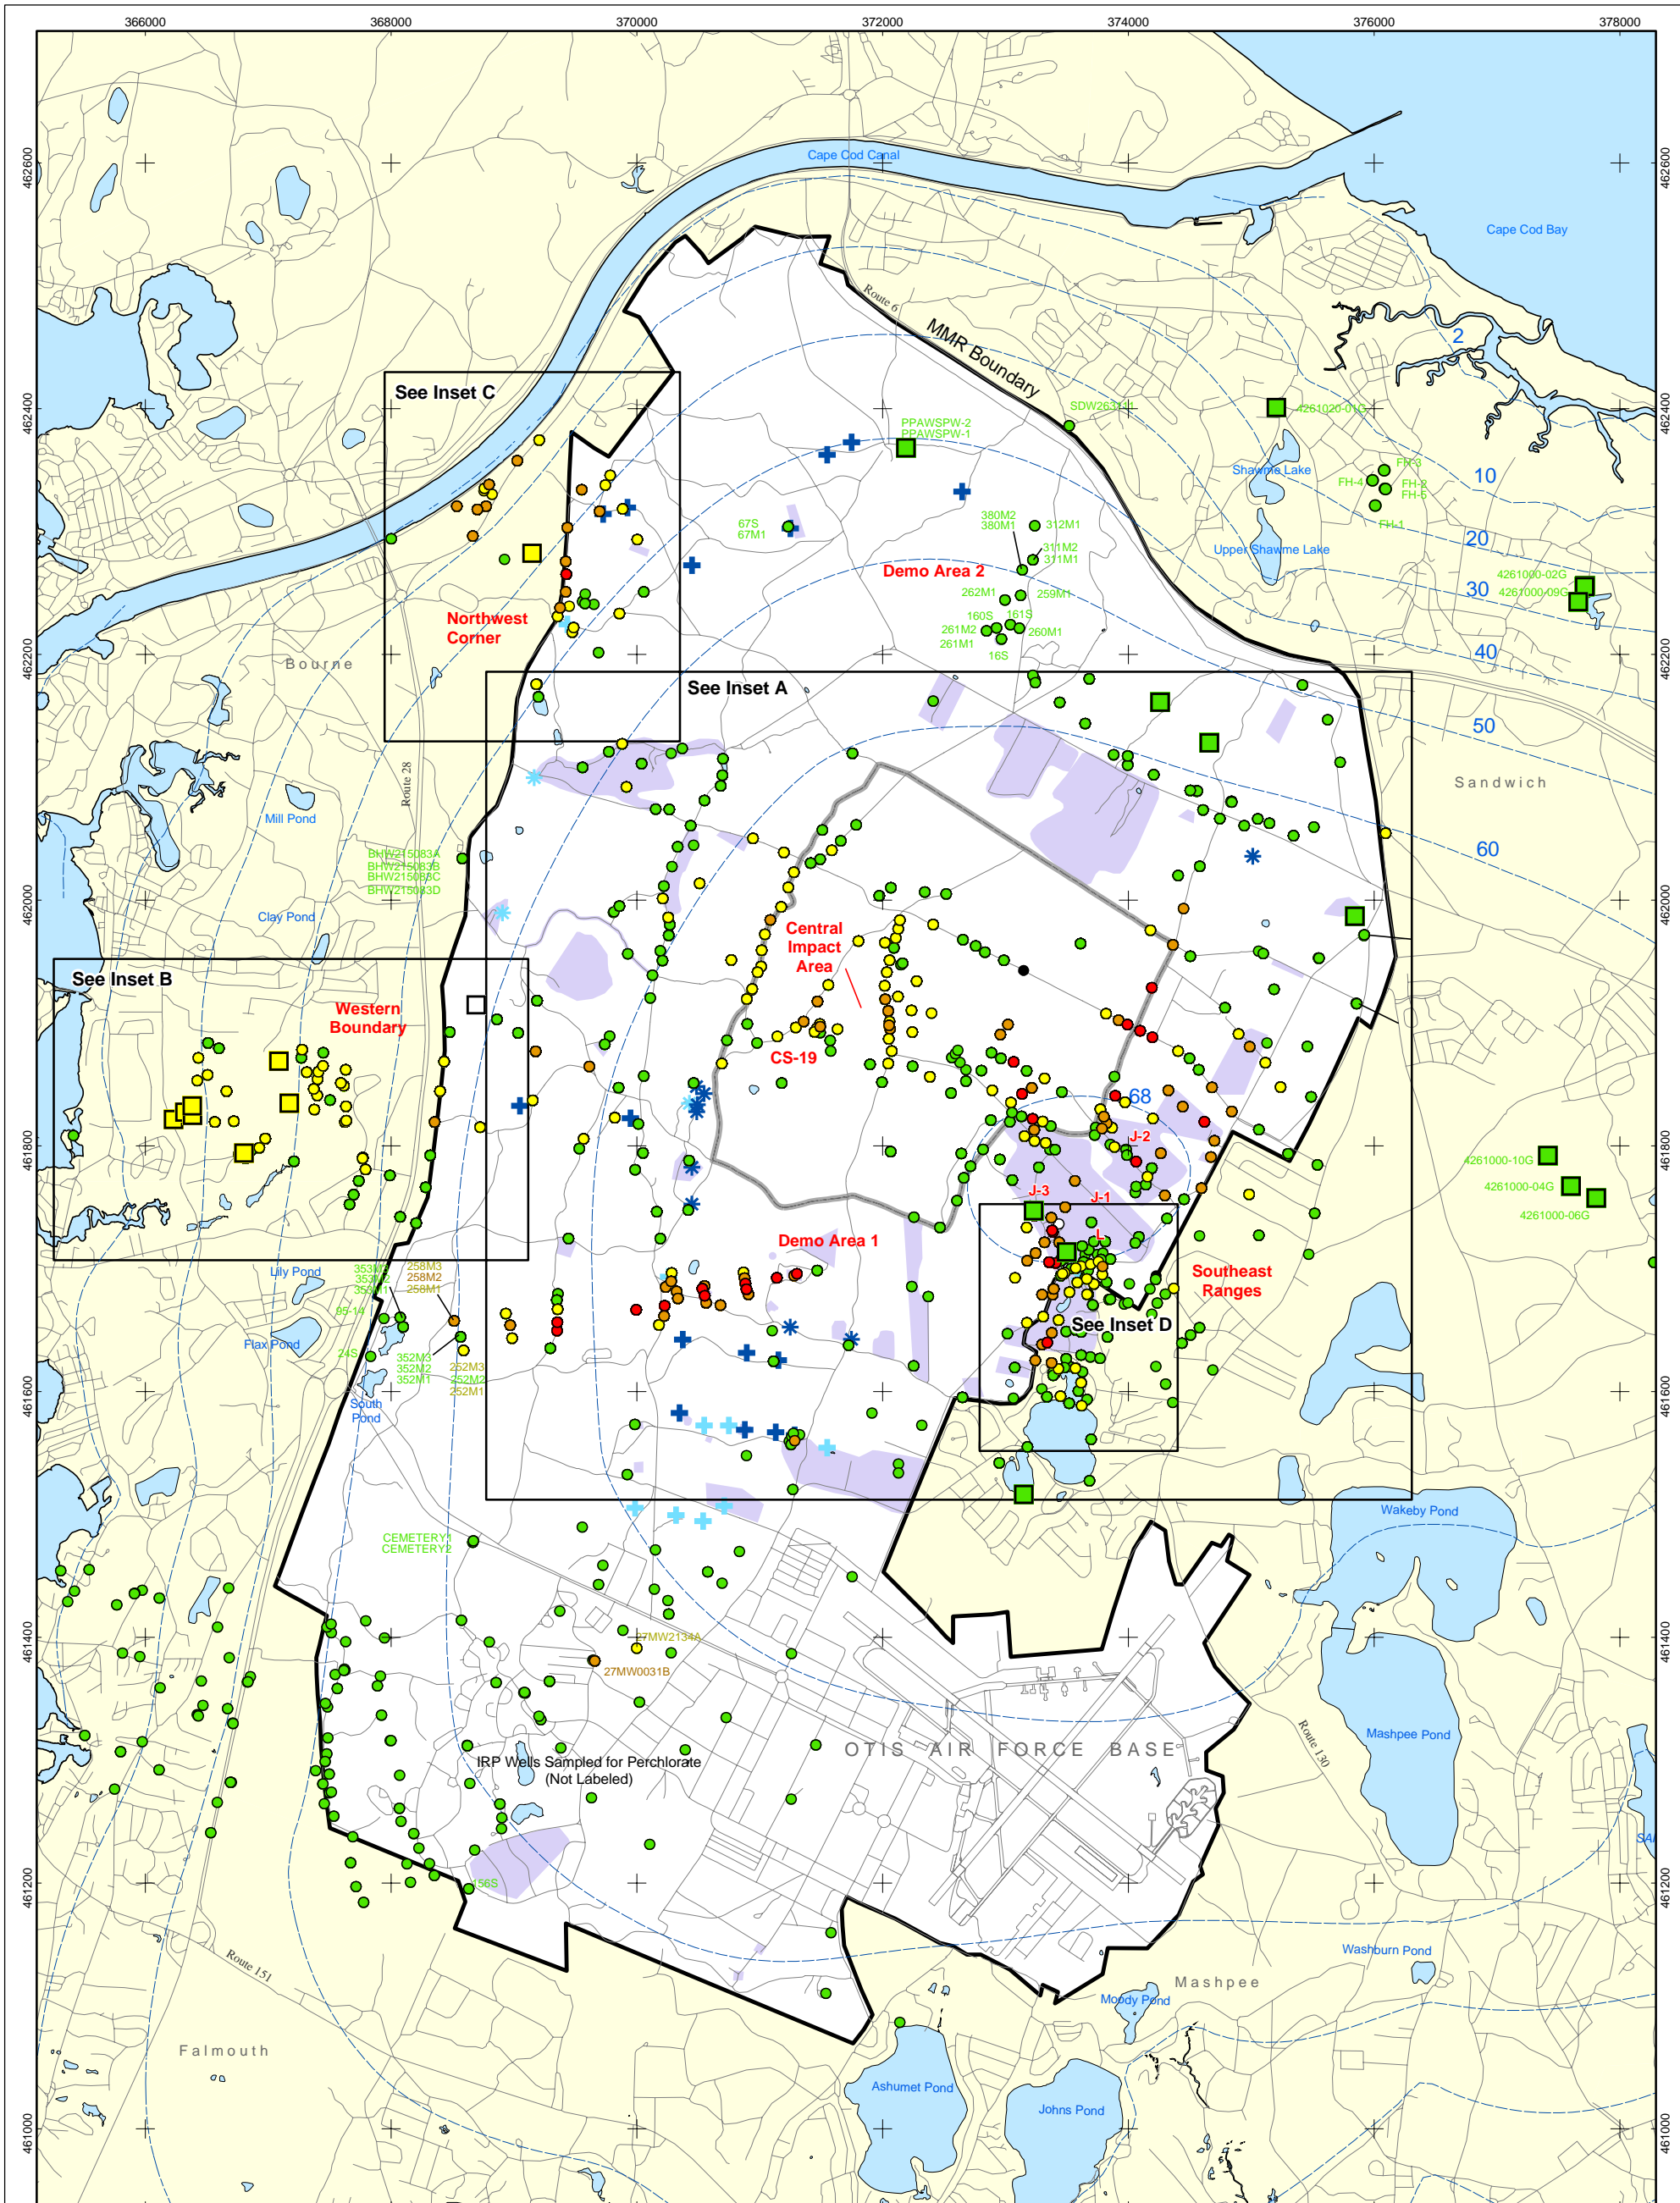


- Validated Detection Greater than or Equal to 24 ppb
- Validated Detection Greater than or Equal to 2 and Less than 24 ppb
- Validated Detection Greater than Non-Detect and Less than 2 ppb
- Validated Non-Detect

Note: Map dot colors are representative of the highest historical concentration at each well and not the current concentration level. Historical data presented on this figure range from November 1996 through 2007.

- Data Pending
- Proposed Monitoring Well
- Current Gun Position
- Current Mortar Position
- Old Gun Position
- Old Mortar Position




- Validated Non-Detect Water Supply Well
- Validated Detection Less than 2 ppb Water Supply Well
- Proposed Water Supply Well

- Water Table Contour (Feet NGVD) AMEC, September 2003
- Military Range Areas



Sources & Notes
 Base map data from US Geological Survey
 7 1/2 minute Topographic Maps
 Source: Office of Geographic and Environmental Information (MassGIS)
 Commonwealth of Massachusetts
 Executive Office of Environmental Affairs

**Perchlorate in Groundwater
 Compared to a 2 ppb Concentration
 Validated Data as of 5/25/07**

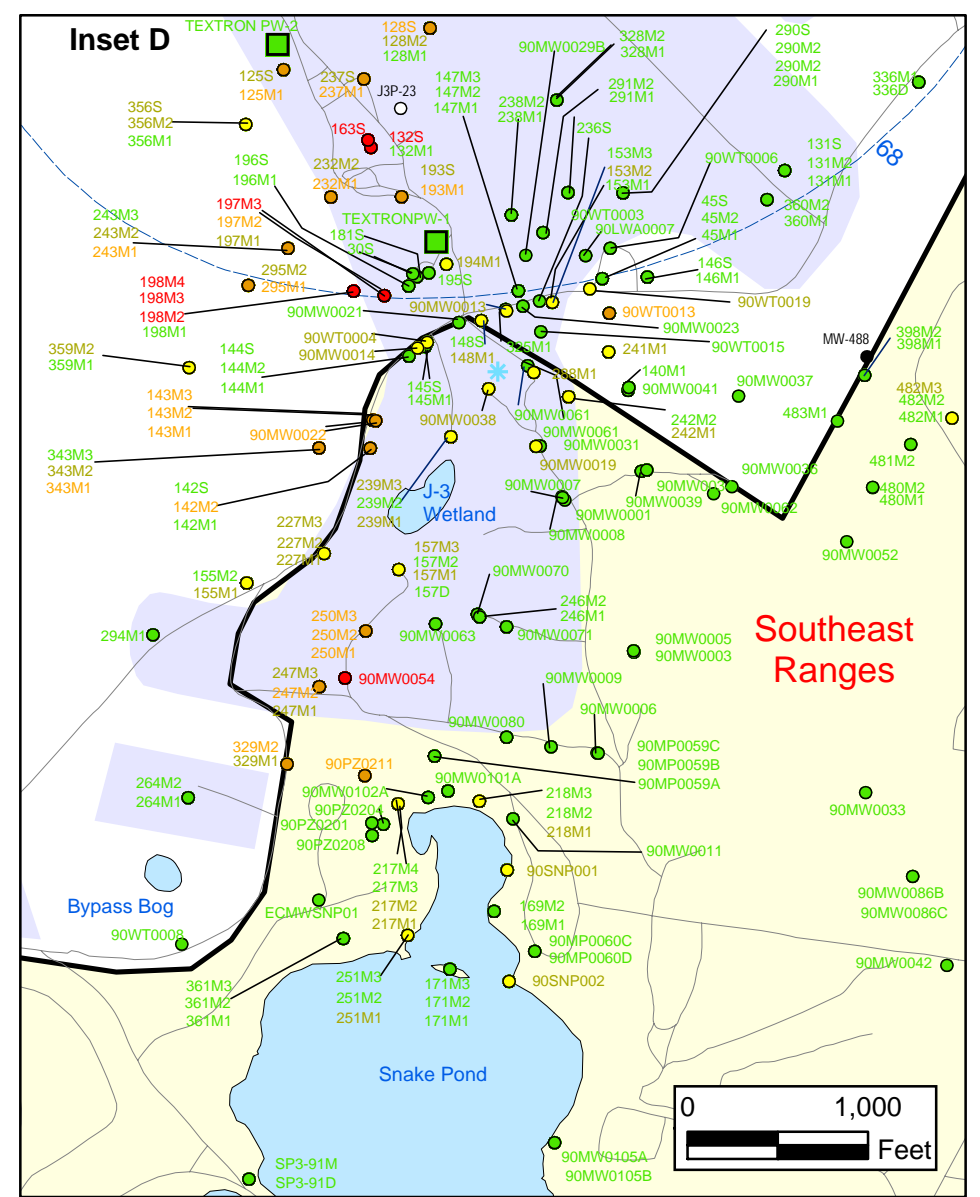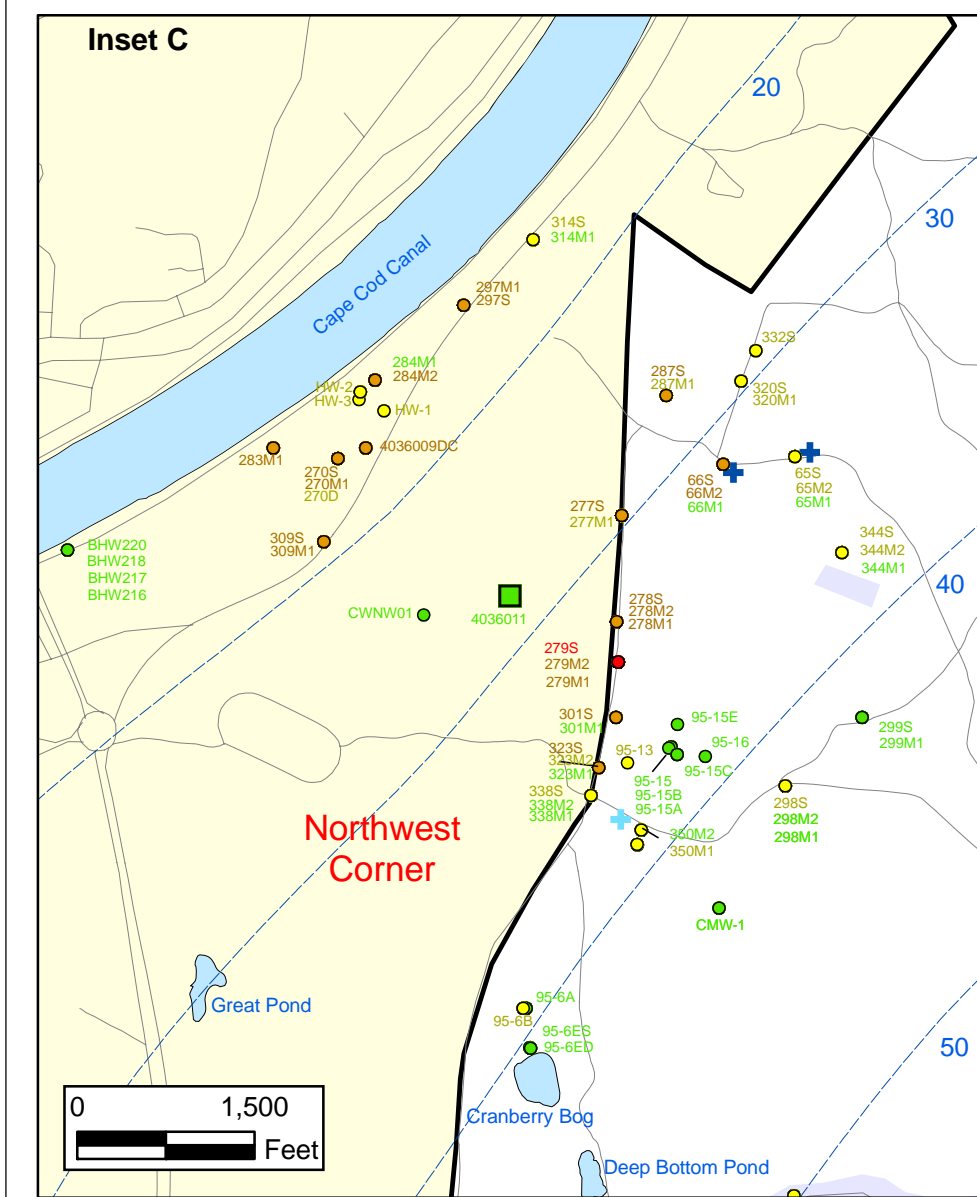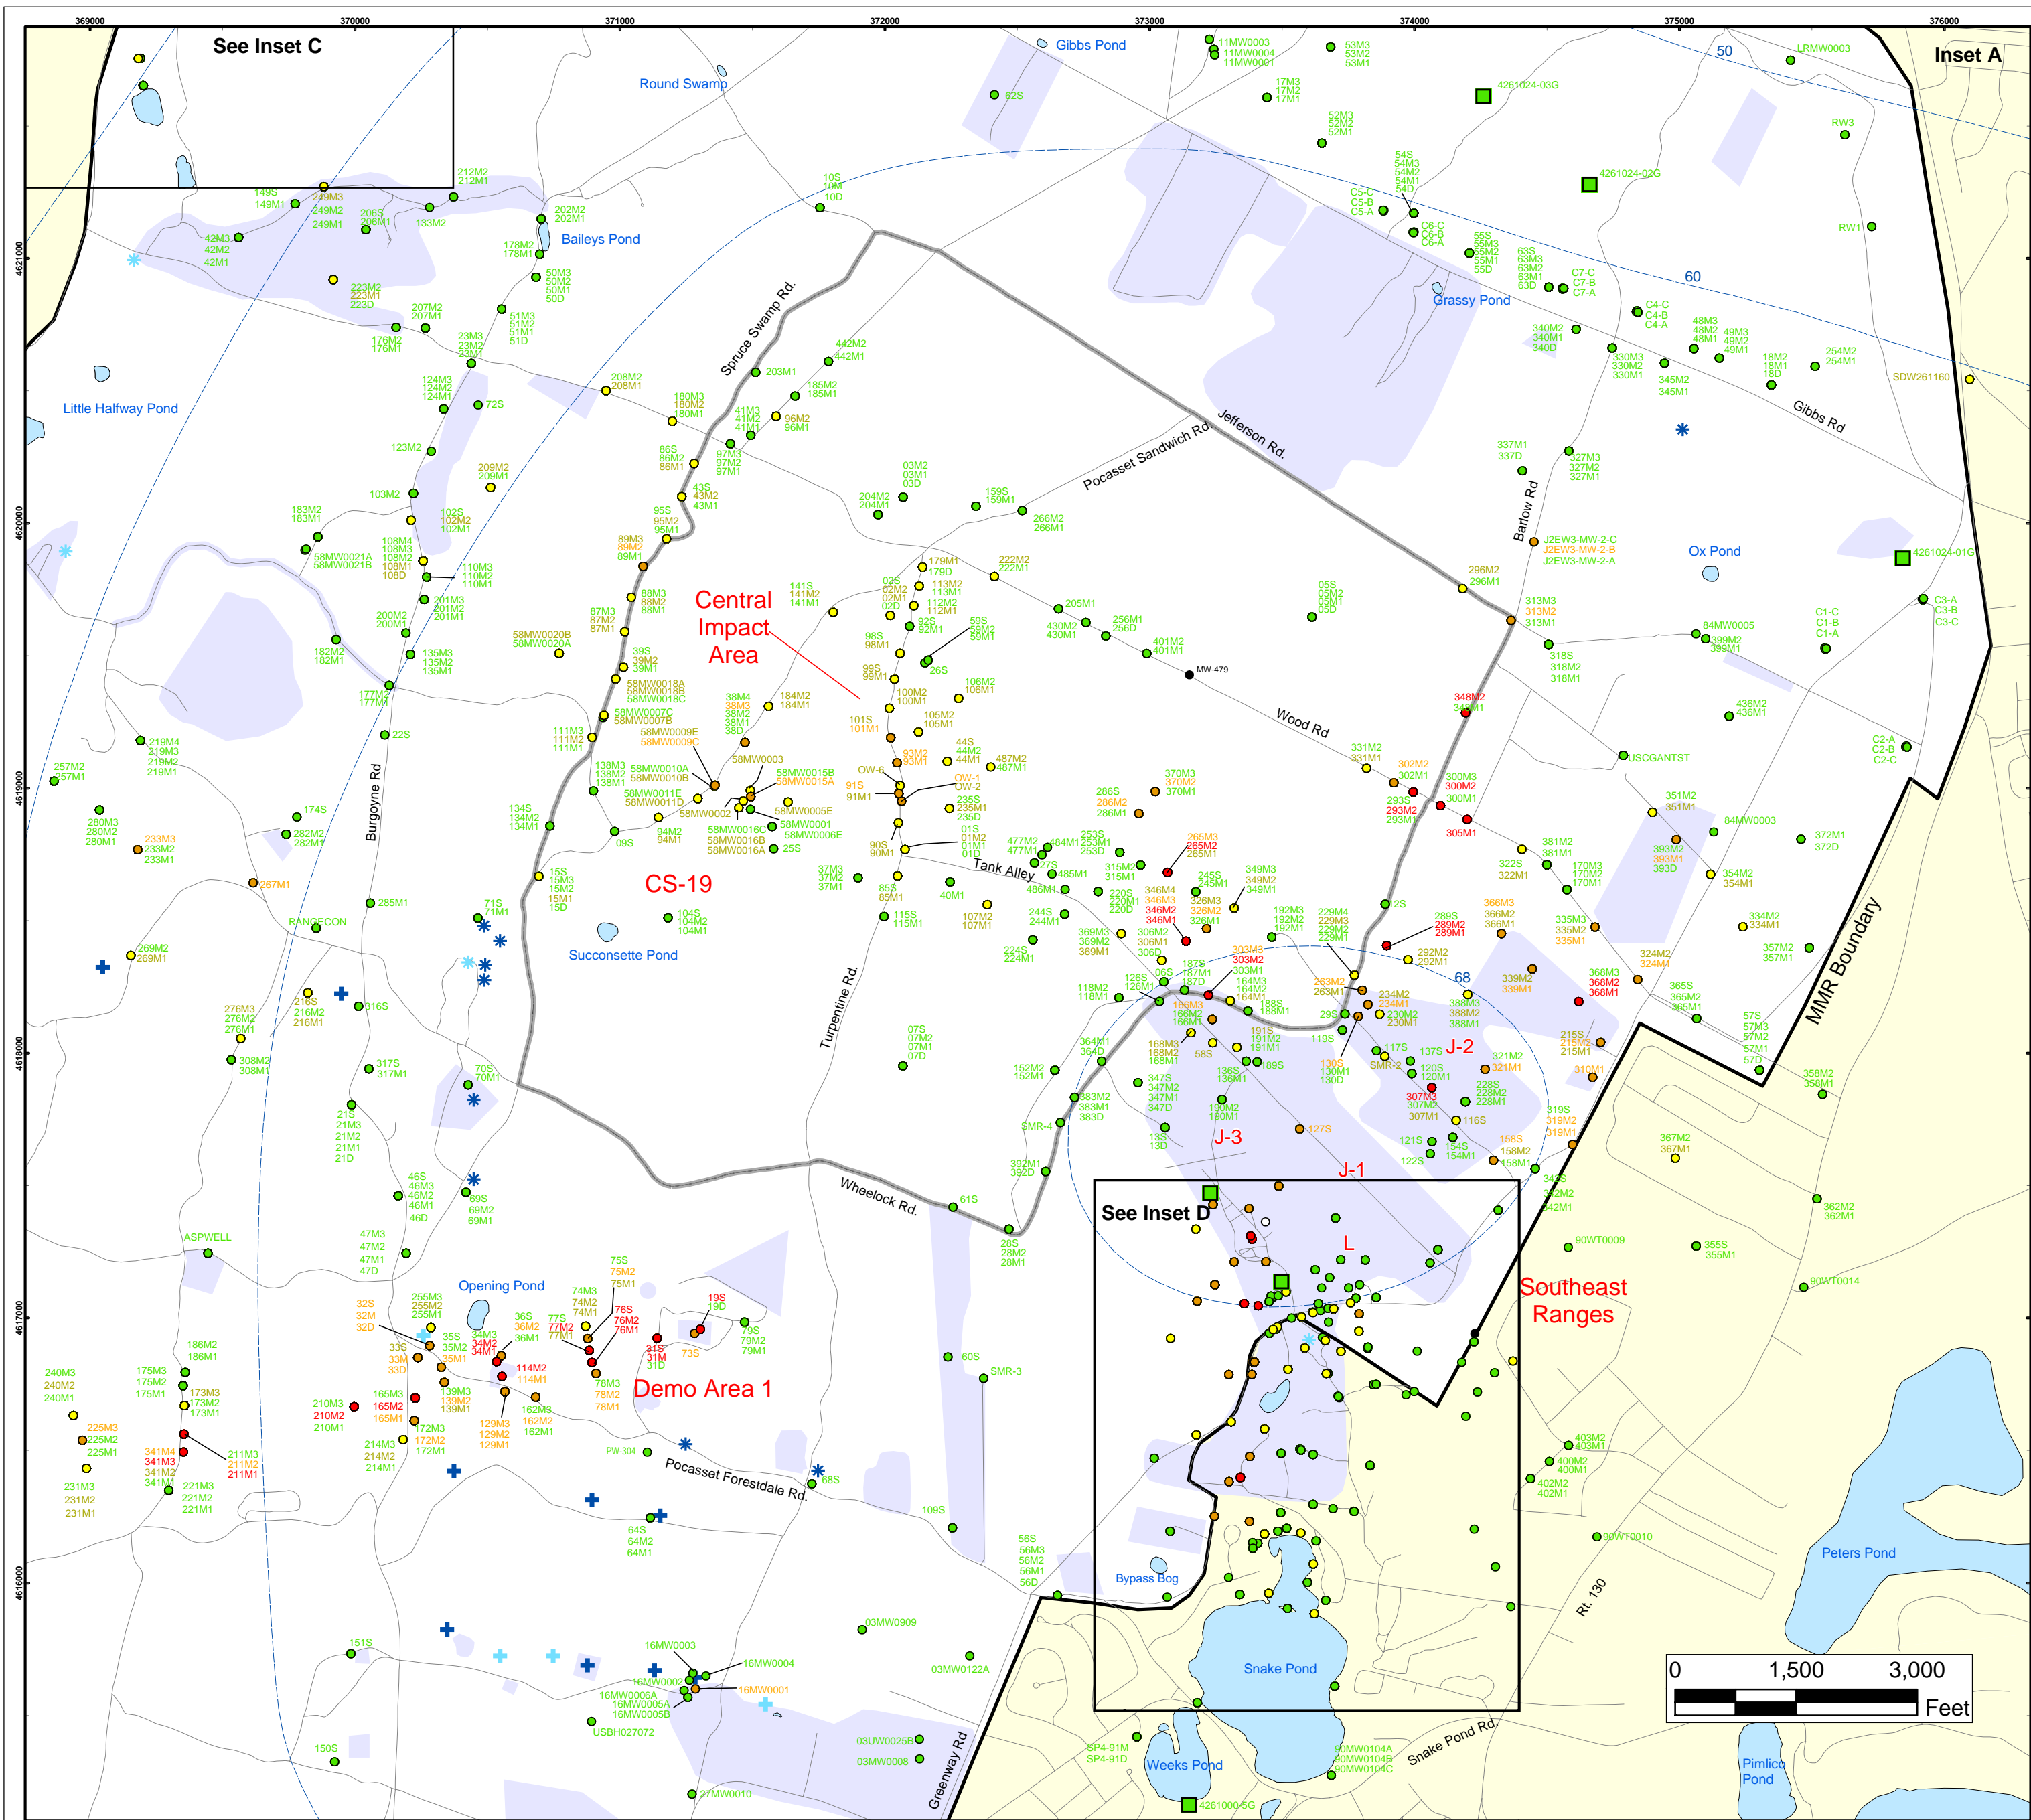

Perchlorate in Groundwater Compared to a 2 PPB Concentration Validated Data as of 5/25/07

- Validated Detection Greater than or Equal to 24 ppb
- Validated Detection Greater than or Equal to 2 and Less than 24 ppb
- Validated Detection Less than 2 ppb
- Validated Non-Detect
- Data Pending
- Proposed Monitoring Well
- Military Range Areas
- + Current Gun Position
- * Current Mortar Position
- + Old Gun Position
- * Old Mortar Position
- Validated Non-Detect Water Supply Well
- Water Table Contour (Feet NGVD), AMEC, September 2003



Note: Map dot colors are representative of the highest historical concentration at each well and not the current concentration level. Historical data presented on this figure range from November 1996 through 2007.

Impact Area
Groundwater Study Program

Sources & Notes
Base map data from US Geological Survey
7 1/2 minute Topographic Maps
Source: Office of Geographic and
Environmental Information (MassGIS)
Commonwealth of Massachusetts
Executive Office of Environmental Affairs

AMEC Earth & Environmental, Inc.
Westford, Massachusetts

FIGURE
Inset Map
8

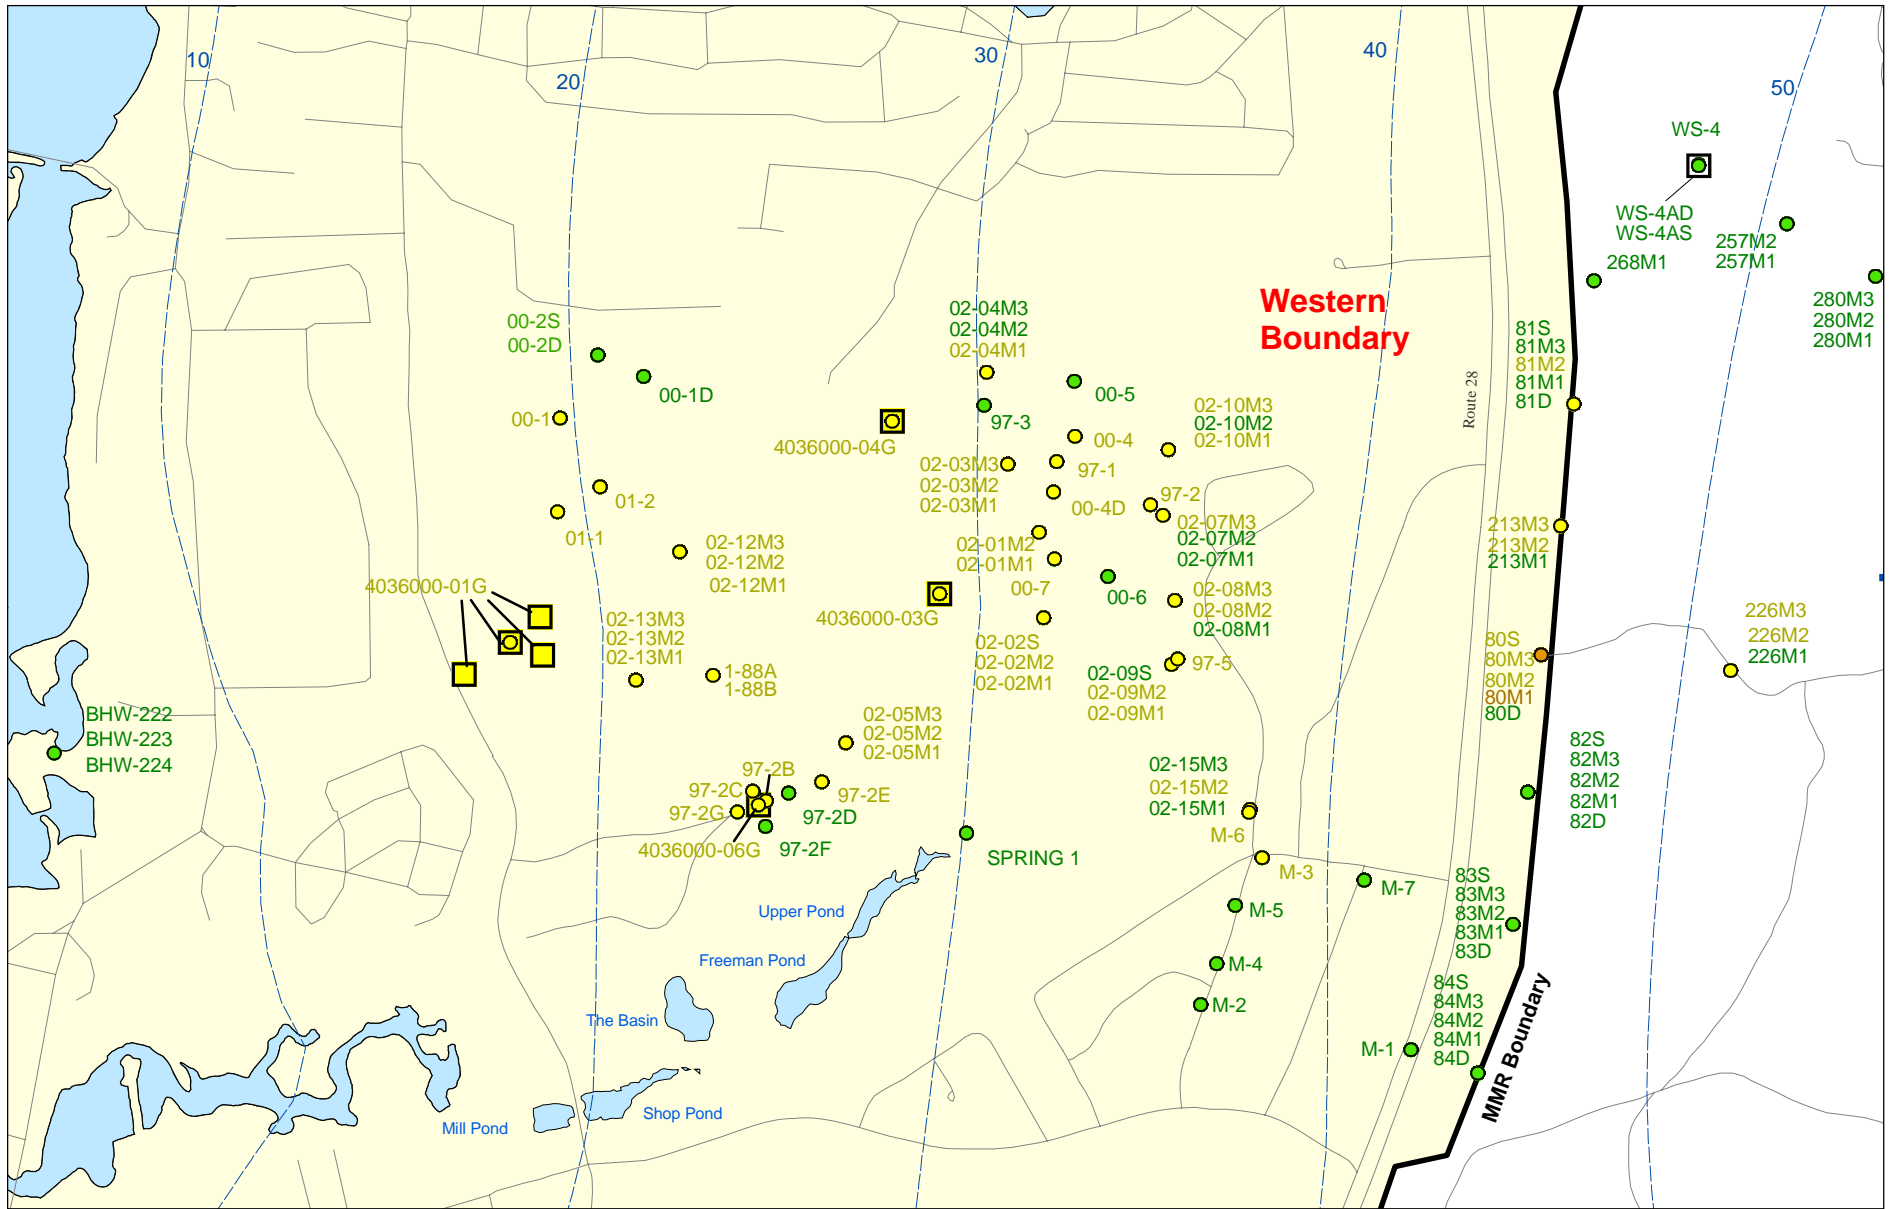


Sources & Notes:
Base map data from US Geological Survey
7 1/2 minute Topographic maps.
Source: Office of Geographic and
Environmental Information (MassGIS)
Commonwealth of Massachusetts
Executive Office of Environmental Affairs

- Validated Detection Greater than or Equal to 2 and Less than 24 ppb
- Validated Detection Greater than Non-Detect and Less than 2 ppb
- Validated Non-Detect
- Validated Detection Less than 2 ppb Water Supply Well
- Proposed Water Supply Well
- +

Note: Map dot colors are representative of the highest historical concentration at each well and not the current concentration level.
Historical data presented on this figure range from November 1996 through 2007.

- +
- Water Table Contour (Feet NGVD)
AMEC, September 2003

Perchlorate in Groundwater Compared to a 2 ppb Concentration Validated Data as of 5/25/07



AMEC Earth & Environmental, Inc.
Westford, Massachusetts

Inset Map B **8**

| Activity ID | Activity Description | Orig Dur | Rem Dur | Anticipated /Actual Start | Anticipated /Actual Finish | FY07 | | | | FY08 | | | | FY09 | | | | FY10 | | | | FY11 | | | | FY12 | | | | | | | | | | | | | | | | | | | | | |
|---|--|----------|---------|---------------------------|----------------------------|---|---|---|---|------|---|---|---|------|---|---|---|------|---|---|---|------|---|---|---|------|---|---|---|---|---|---|---|---|---|---|---|---|---|---|---|---|---|---|---|---|---|
| | | | | | | J | F | M | A | M | J | J | A | S | O | N | D | J | F | M | A | M | J | J | A | S | O | N | D | J | F | M | A | M | J | J | A | S | O | N | D | J | F | M | A | M | J |
| Demo 1 | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| Demolition Area 1 Soil | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| 00145 | Agency Review/Approve Draft Demo 1 RRA Soil COWR | 313* | 52* | 22DEC05A | 21MAR07 | Agency Review/Approve Draft Demo 1 RRA Soil COWR preparing RCL | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| DM0920 | Prepare/Submit Final Demo 1 RRA Soil COWR | 20 | 20 | 22MAR07 | 18APR07 | Prepare/Submit Final Demo 1 RRA Soil COWR | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| DL0000 | Prepare/Submit Draft Demo 1 Soil NFA DD | 45 | 45 | 19APR07 | 21JUN07 | Prepare/Submit Draft Demo 1 Soil NFA DD | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| DL0080 | Agency Review/Approve Draft Demo 1 Soil NFA DD | 55* | 55* | 22JUN07 | 10SEP07 | Agency Review/Approve Draft Demo 1 Soil NFA DD | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| DL0085 | Formal Public Comment Demo 1 Soil NFA DD | 30 | 30 | 09JUL07 | 07AUG07 | Formal Public Comment Demo 1 Soil NFA DD | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| DL0100 | Prepare/Submit Final Demo 1 Soil NFA DD | 20 | 20 | 11SEP07 | 09OCT07 | Prepare/Submit Final Demo 1 Soil NFA DD | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| DL0110 | EPA Issue Demo 1 Soil NFA DD | 15 | 15 | 10OCT07 | 30OCT07 | EPA Issue Demo 1 Soil NFA DD | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| Demolition Area 1 Groundwater | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| 31575 | Construct/Startup Demo 1 GW Treatment System | 211* | 102* | 01AUG06A | 31MAY07 | Construct/Startup Demo 1 GW Treatment System | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| CL0010 | Prepare/Submit Draft Demo 1 SPM Plan | 60 | 26 | 02JAN07A | 12FEB07 | Prepare/Submit Draft Demo 1 SPM Plan | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| CL0100 | Agency Review/Approve Draft Demo 1 SPM Plan | 55* | 55* | 13FEB07 | 01MAY07 | Agency Review/Approve Draft Demo 1 SPM Plan | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| CL0130 | Prepare/Submit Final Demo 1 SPM Plan | 20 | 20 | 02MAY07 | 30MAY07 | Prepare/Submit Final Demo 1 SPM Plan | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| CL0140 | Prepare/Submit Dr Demo 1 GW Int RA & Close-Out Rt | 60 | 60 | 05APR07 | 28JUN07 | Prepare/Submit Dr Demo 1 GW Int RA & Close-Out Rt | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| CL0220 | Agency Revw/Approv Dr Demo 1 GW Int RA & Close-Out | 55* | 55* | 29JUN07 | 17SEP07 | Agency Revw/Approv Dr Demo 1 GW Int RA & Close-Out | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| CL0240 | Prep/Sub Final Demo 1 GW Interim RA&Close-Out Rt | 20 | 20 | 18SEP07 | 16OCT07 | Prep/Sub Final Demo 1 GW Interim RA&Close-Out Rt | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| CL0245 | EPA Approve Demo 1 GW Interim RA & Close-Out Rt | 15 | 15 | 17OCT07 | 06NOV07 | EPA Approve Demo 1 GW Interim RA & Close-Out Rt | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| J-1 Range | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| J-1 Range Soil & Groundwater | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| 02185 | Prepare/Submit Draft J-1 GW RRA Pln Project Note | 66* | 0* | 02OCT06A | 05JAN07A | Prepare/Submit Draft J-1 GW RRA Pln Project Note | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| 02189 | Agency Review/Approve Draft J-1 GW RRA Pjct Note | 31* | 31* | 08JAN07A | 20FEB07 | Agency Review/Approve Draft J-1 GW RRA Pjct Note | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| 02192 | Informal Public Comment J-1 GW RRA Project Note | 15 | 15 | 20JAN07 | 03FEB07 | Informal Public Comment J-1 GW RRA Project Note | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| 0920 | Prepare/Submit Final J-1 GW RRA Pln Project Note | 10 | 10 | 21FEB07 | 06MAR07 | Prepare/Submit Final J-1 GW RRA Pln Project Note | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| 02187 | Design J-1 GW RRA Treatment System | 120* | 121* | 09JAN07A | 27JUN07 | Design J-1 GW RRA Treatment System Assumes: design starts with agency commitments. | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| 02191 | Construct/Startup J-1 GW RRA Treatment System | 66 | 66 | 17SEP07 | 20DEC07 | Construct/Startup J-1 GW RRA Treatment System Assumes: 66 days for procurement under PBC | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| CL0250 | Prepare/Submit Draft J-1 RRA GW SPM Plan | 45 | 45 | 25APR07 | 27JUN07 | Prepare/Submit Draft J-1 RRA GW SPM Plan | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| CL0330 | Agency Review/Approve Draft J-1 RRA GW SPM Plan | 55* | 55* | 28JUN07 | 14SEP07 | Agency Review/Approve Draft J-1 RRA GW SPM Plan | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | |

- General Notes:**
- A. 55 day - Agency Review/Approve Activity Includes:**
- 15 days: Agency Review/Comment
 - 15 days: Prepare/Submit RCL
 - 5 days: Agency Review RCL
 - 5 days: Agency Conduct CRM
 - 10 days: Prepare/Submit MOR
 - 5 days: Agency Approve MOR
- B. FY07 Priorities**
1. Demolition Area 1 GW
 2. J-2 Range GW
 3. J-1 Range GW
 4. J-3 Range GW
 5. Small Arms Ranges
 6. Gun & Mortar
 7. Demolition Area Soil
 8. Western Boundary
 9. Ammunition Supply Point

Start Date: 01JAN06
 Finish Date: 20DEC69
 Data Date: 07JAN07
 Run Date: 18JAN07 17:08

U197
 Sheet 1 of 14
 RCS - Revised Format
 as of 07JAN07

Activity Colors

- IAGWSP Activities
- Agency Activities
- Formal/Informal Public Comment Activities

| Activity ID | Activity Description | Orig Dur | Rem Dur | Anticipated /Actual Start | Anticipated /Actual Finish | FY07 | | | | FY08 | | | | FY09 | | | | FY10 | | | | FY11 | | | | FY12 | | | | | | | | | | | | | | | | | | | | | |
|-------------|--|----------|---------|---------------------------|----------------------------|---|---|---|---|------|---|---|---|------|---|---|---|------|---|---|---|------|---|---|---|------|---|---|---|---|---|---|---|---|---|---|---|---|---|---|---|---|---|---|---|---|---|
| | | | | | | J | F | M | A | M | J | J | A | S | O | N | D | J | F | M | A | M | J | J | A | S | O | N | D | J | F | M | A | M | J | J | A | S | O | N | D | J | F | M | A | M | J |
| 22130 | Agency Review/Approve CIA Dft Soil/GW FS Scm Rpt | 55 | 55 | 16APR07 | 02JUL07 | Agency Review/Approve CIA Dft Soil/GW FS Scm Rpt | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| 22131 | Prepare/Submit Final CIA Dft Soil/GW FS Scm Rpt | 20 | 20 | 03JUL07 | 31JUL07 | Prepare/Submit Final CIA Dft Soil/GW FS Scm Rpt | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| 22210 | Prepare/Submit Draft CIA Soil/GW FS | 135 | 135 | 02AUG07 | 14FEB08 | Prepare/Submit Draft CIA Soil/GW FS | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| 22230 | Agency Review/Approve CIA Soil/GW FS | 85 | 85 | 15FEB08 | 16JUN08 | Agency Review/Approve CIA Soil/GW FS | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| 22231 | Prepare/Submit Final CIA Soil/GW FS | 20 | 20 | 17JUN08 | 15JUL08 | Prepare/Submit Final CIA Soil/GW FS | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| 32510 | Prepare/Submit Draft CIA RSP | 60 | 60 | 19FEB08 | 12MAY08 | Prepare/Submit Draft CIA RSP | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| 32520 | Agency Review/Approve Draft CIA RSP | 75 | 75 | 13MAY08 | 27AUG08 | Agency Review/Approve Draft CIA RSP | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| 32530 | Prepare/Submit Final CIA RSP | 20 | 20 | 28AUG08 | 25SEP08 | Prepare/Submit Final CIA RSP | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| 32540 | Formal Public Comment CIA RSP | 30 | 30 | 26SEP08 | 26OCT08 | Formal Public Comment CIA RSP | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| CI0080 | Prepare/Submit Draft CIA DD | 20 | 20 | 27OCT08 | 24NOV08 | Prepare/Submit Draft CIA DD | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| CI0090 | Agency Review/Approve Draft CIA DD | 20 | 20 | 25NOV08 | 23DEC08 | Agency Review/Approve Draft CIA DD | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| CI0100 | Prepare/Submit Final CIA DD | 20 | 20 | 24DEC08 | 22JAN09 | Prepare/Submit Final CIA DD | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| CI0110 | EPA Issue CIA DD | 15 | 15 | 23JAN09 | 12FEB09 | EPA Issue CIA DD | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| 32579 | Design CIA Remedy | 230 | 230 | 16JUL08 | 12JUN09 | Design CIA Remedy | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| 32580 | Construct CIA Remedy | 427 | 427 | 17SEP09 | 27MAY11 | Construct CIA Remedy Assumes 66 days procurement | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| CI0120 | Prepare/Submit Draft CIA SPM Plan | 60 | 60 | 20MAR09 | 12JUN09 | Prepare/Submit Draft CIA SPM Plan | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| CI0130 | Agency Review/Approve Draft CIA SPM Plan | 55 | 55 | 15JUN09 | 31AUG09 | Agency Review/Approve Draft CIA SPM Plan | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| CI0140 | Prepare/Submit Final CIA SPM Plan | 20 | 20 | 01SEP09 | 29SEP09 | Prepare/Submit Final CIA SPM Plan | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| CI0150 | Prep/Sub Draft CIA Interim RA & Close-Out Rpt | 60 | 60 | 04APR11 | 27JUN11 | Prep/Sub Draft CIA Interim RA & Close-Out Rpt North Soil Final & GW | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| CI0160 | Agency Revw/Appro Draft CIA Interim RA & Close-Out | 55 | 55 | 28JUN11 | 14SEP11 | Agency Revw/Appro Draft CIA Interim RA & Close-Out North Soil Final & GW | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| CI0170 | Prepare/Submit CIA Interim RA & Close-Out Rpt | 20 | 20 | 15SEP11 | 13OCT11 | Prepare/Submit CIA Interim RA & Close-Out Rpt North Soil Final & GW | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| CI0180 | EPA Approve CIA Interim RA & Close-Out Rpt | 15 | 15 | 14OCT11 | 03NOV11 | EPA Approve CIA Interim RA & Close-Out Rpt North Soil Final & GW | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | |

Northwest Corner

Northwest Corner Soil & Groundwater

| | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | |
|--------|--|-----|-----|----------|---------|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|
| 03451 | Prepare/Submit Draft Northwest Corner RI/FS | 135 | 134 | 09NOV06A | 19SEP07 | Prepare/Submit Draft Northwest Corner RI/FS | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| 03453 | Agency Review/Approve Draft Northwest Corner RI/FS | 55* | 55* | 20SEP07 | 10DEC07 | Agency Review/Approve Draft Northwest Corner RI/FS | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| 03454 | Prepare/Submit Final Northwest Corner RI/FS | 20 | 20 | 11DEC07 | 09JAN08 | Prepare/Submit Final Northwest Corner RI/FS | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| SL0600 | Prepare/Submit Draft Northwest Corner RSP | 15 | 15 | 10JAN08 | 30JAN08 | Prepare/Submit Draft Northwest Corner RSP | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| SL0610 | Agency Review/Approve Draft Northwest Corner RSP | 55* | 55* | 31JAN08 | 17APR08 | Agency Review/Approve Draft Northwest Corner RSP | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| SL0620 | Prepare/Submit Final Northwest Corner RSP | 10 | 10 | 18APR08 | 01MAY08 | Prepare/Submit Final Northwest Corner RSP | | | | | | | | | | | | | | | | | | | | | | | | | | | |


| Activity ID | Activity Description | Orig Dur | Rem Dur | Anticipated /Actual Start | Anticipated /Actual Finish | FY07 | | | | | FY08 | | | | | FY09 | | | | | FY10 | | | | | FY11 | | | | | FY12 | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | |
|--|---|----------|---------|---------------------------|----------------------------|--|---|---|---|---|------|---|---|---|---|------|---|---|---|---|------|---|---|---|---|------|---|---|---|---|------|---|---|---|---|---|---|---|---|---|---|---|---|---|---|---|---|---|---|---|---|---|---|---|---|---|---|---|---|---|---|---|---|---|---|---|---|---|---|---|---|---|---|---|
| | | | | | | J | F | M | A | M | J | J | A | S | O | N | D | J | F | M | A | M | J | J | A | S | O | N | D | J | F | M | A | M | J | J | A | S | O | N | D | J | F | M | A | M | J | J | A | S | O | N | D | J | F | M | A | M | J | J | A | S | O | N | D | J | F | M | A | M | J | J | A | S |
| | | | | | | [Gantt Chart Area with task bars and labels] | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| SL0630 | Formal Public Comment Northwest Corner RSP | 30 | 30 | 02MAY08 | 01JUN08 | [Gantt Chart: Formal Public Comment Northwest Corner RSP] | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| SL0640 | Prepare/Submit Draft Northwest Corner DD | 20 | 20 | 02JUN08 | 27JUN08 | [Gantt Chart: Prepare/Submit Draft Northwest Corner DD] | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| SL0650 | Agency Review/Approve Draft Northwest Corner DD | 55* | 55* | 30JUN08 | 16SEP08 | [Gantt Chart: Agency Review/Approve Draft Northwest Corner DD] | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| SL0660 | Prepare/Submit Final Northwest Corner DD | 20 | 20 | 17SEP08 | 15OCT08 | [Gantt Chart: Prepare/Submit Final Northwest Corner DD] | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| SL0670 | EPA Issue Northwest Corner DD | 15 | 15 | 16OCT08 | 05NOV08 | [Gantt Chart: EPA Issue Northwest Corner DD] | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| SL0680 | Prepare/Submit Draft Northwest Corner LTM Plan | 60 | 60 | 06NOV08 | 03FEB09 | [Gantt Chart: Prepare/Submit Draft Northwest Corner LTM Plan] | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| SL0690 | Agency Review/Approve Draft Northwest Corner LTM | 55 | 55 | 04FEB09 | 22APR09 | [Gantt Chart: Agency Review/Approve Draft Northwest Corner LTM] | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| SL0700 | Prepare/Submit Final Northwest Corner LTM Plan | 20 | 20 | 23APR09 | 20MAY09 | [Gantt Chart: Prepare/Submit Final Northwest Corner LTM Plan] | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| SL0710 | Prep/Sub Draft NWC Interim RA & Close-Out Rpt | 60 | 60 | 26MAR09 | 18JUN09 | [Gantt Chart: Prep/Sub Draft NWC Interim RA & Close-Out Rpt] | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| SL0720 | Agency Revw/Appr Draft NWC Interim RA & Close-Out | 55* | 55* | 19JUN09 | 04SEP09 | [Gantt Chart: Agency Revw/Appr Draft NWC Interim RA & Close-Out] | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| SL0730 | Prepare/Submit NWC Interim RA & Close-Out Rpt | 20 | 20 | 08SEP09 | 05OCT09 | [Gantt Chart: Prepare/Submit NWC Interim RA & Close-Out Rpt] | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| SL0740 | EPA Approve NWC Interim RA & Close-Out Rpt | 15 | 15 | 06OCT09 | 27OCT09 | [Gantt Chart: EPA Approve NWC Interim RA & Close-Out Rpt] | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| Western Boundary | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| Western Boundary Soil & Groundwater | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| 03494 | Agency Revw/Apprv Draft Western Boundary Invest | 161* | 46* | 24JUL06A | 13MAR07 | [Gantt Chart: Agency Revw/Apprv Draft Western Boundary Invest] | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| WB1020 | Prepare/Submit Final Western Boundary Invest Rpt | 20 | 20 | 14MAR07 | 10APR07 | [Gantt Chart: Prepare/Submit Final Western Boundary Invest Rpt] | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| WB1022 | Prepare/Submit Draft Western Boundary RSP | 15 | 15 | 11APR07 | 01MAY07 | [Gantt Chart: Prepare/Submit Draft Western Boundary RSP] | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| WB1024 | Agency Review/Approve Draft Western Boundary RSP | 55* | 55* | 02MAY07 | 19JUL07 | [Gantt Chart: Agency Review/Approve Draft Western Boundary RSP] | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| WB1026 | Prepare/Submit Final Western Boundary RSP | 10 | 10 | 20JUL07 | 02AUG07 | [Gantt Chart: Prepare/Submit Final Western Boundary RSP] | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| WB1028 | Formal Public Comment Western Boundary RSP | 30 | 30 | 03AUG07 | 01SEP07 | [Gantt Chart: Formal Public Comment Western Boundary RSP] | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| WB4010 | Prepare/Submit Draft Western Boundary DD | 20 | 20 | 04SEP07 | 01OCT07 | [Gantt Chart: Prepare/Submit Draft Western Boundary DD] | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| WB4060 | Agency Review/Approve Draft Western Boundary DD | 55* | 55* | 02OCT07 | 20DEC07 | [Gantt Chart: Agency Review/Approve Draft Western Boundary DD] | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| WB4080 | Prepare/Submit Final Western Boundary DD | 20 | 20 | 21DEC07 | 21JAN08 | [Gantt Chart: Prepare/Submit Final Western Boundary DD] | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| WB4090 | EPA Issue Western Boundary DD | 15 | 15 | 22JAN08 | 11FEB08 | [Gantt Chart: EPA Issue Western Boundary DD] | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| WB4220 | Prepare/Submit Draft Western Boundary LTM Plan | 45 | 45 | 12FEB08 | 15APR08 | [Gantt Chart: Prepare/Submit Draft Western Boundary LTM Plan] | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| WB4300 | Agency Review/Approve Draft Western Bnd LTM Plan | 55* | 55* | 16APR08 | 02JUL08 | [Gantt Chart: Agency Review/Approve Draft Western Bnd LTM Plan] | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| WB4320 | Prepare/Submit Final Western Boundary LTM Plan | 20 | 20 | 03JUL08 | 31JUL08 | [Gantt Chart: Prepare/Submit Final Western Boundary LTM Plan] | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| WB4100 | Prepare/Submit Draft WB Interim RA & Close-Out | 60 | 60 | 05JUN08 | 28AUG08 | [Gantt Chart: Prepare/Submit Draft WB Interim RA & Close-Out] | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| WB4180 | Agency Revw/Appr Dr WB Interim RA & Close-Out | 55* | 55* | 29AUG08 | 18NOV08 | [Gantt Chart: Agency Revw/Appr Dr WB Interim RA & Close-Out] | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| WB4200 | Prep/Sub Final WB Interim RA & Close-Out Rpt | 20 | 20 | 19NOV08 | 17DEC08 | [Gantt Chart: Prep/Sub Final WB Interim RA & Close-Out Rpt] | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | |

| Activity ID | Activity Description | Orig Dur | Rem Dur | Anticipated /Actual Start | Anticipated /Actual Finish | FY07 | | | | | | | | | | | | FY08 | | | | | | | | | | | | FY09 | | | | | | | | | | | | FY10 | | | | | | | | | | | | FY11 | | | | | | | | | | | | FY12 | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | |
|-------------|--|----------|---------|---------------------------|----------------------------|---|--|--|---|--|--|---|--|--|---|--|--|------|--|--|---|--|--|---|--|--|---|--|--|------|--|--|---|--|--|---|--|--|---|--|--|------|--|--|---|--|--|---|--|--|---|--|--|------|--|--|---|--|--|---|--|--|---|--|--|------|--|--|---|--|--|---|--|--|---|--|--|---|--|--|---|--|--|---|--|--|---|--|--|---|--|--|---|--|--|---|--|--|---|--|--|---|--|--|---|--|--|---|--|--|---|--|--|---|--|--|---|--|--|---|--|--|---|--|--|---|--|--|---|--|--|---|--|--|---|--|--|---|--|--|---|--|--|---|--|--|---|--|--|---|--|--|---|--|--|---|--|--|---|--|--|---|--|--|---|--|--|---|--|--|---|--|--|---|--|--|---|--|--|---|--|--|---|--|--|---|--|--|---|--|--|---|--|--|---|--|--|---|--|--|---|--|--|---|--|--|---|--|--|---|--|--|---|--|--|---|--|--|
| | | | | | | J | | | F | | | M | | | A | | | M | | | J | | | J | | | A | | | S | | | O | | | N | | | D | | | J | | | F | | | M | | | A | | | M | | | J | | | J | | | A | | | S | | | O | | | N | | | D | | | J | | | F | | | M | | | A | | | M | | | J | | | J | | | A | | | S | | | O | | | N | | | D | | | J | | | F | | | M | | | A | | | M | | | J | | | J | | | A | | | S | | | O | | | N | | | D | | | J | | | F | | | M | | | A | | | M | | | J | | | J | | | A | | | S | | | O | | | N | | | D | | | J | | | F | | | M | | | A | | | M | | | J | | | J | | | A | | | S | | | O | | | N | | |
| | | | | | | Hatched area indicating scheduling constraints or dependencies. | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| CL1860 | Prepare/Submit Final G&M Soil RRA Plan | 20 | 20 | 31AUG07 | 28SEP07 | [Task bar with green arrow] | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| 00571 | Conduct G&M Soil RRA | 132 | 132 | 17SEP07 | 26MAR08 | [Task bar with green arrow] | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| CL1900 | Prepare/Submit Draft G&M Soil COWR | 60 | 60 | 27MAR08 | 19JUN08 | [Task bar with green arrow] | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| CL1990 | Agency Review/Approve Draft G&M Soil COWR | 55* | 55* | 20JUN08 | 08SEP08 | [Task bar with orange arrow] | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| CL2000 | Prepare/Submit G&M Final Soil COWR | 20 | 20 | 09SEP08 | 06OCT08 | [Task bar with green arrow] | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| 00555 | Prepare/Submit Draft G&M Soil/GW Investigat Rpt | 242 | 242 | 13JUN07 | 28MAY08 | [Task bar with green arrow] | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| 00557 | Agency Review/Approve Draft G&M Soil/GW Investig | 55* | 55* | 29MAY08 | 14AUG08 | [Task bar with orange arrow] | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| 00560 | Prepare Final G&M Soil/GW Investigation Report | 20 | 20 | 15AUG08 | 12SEP08 | [Task bar with green arrow] | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| CL2230 | Prepare/Submit Draft G&M DD | 20 | 20 | 15SEP08 | 10OCT08 | [Task bar with green arrow] | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| CL2280 | Agency Review/Approve Draft G&M DD | 55* | 55* | 14OCT08 | 02JAN09 | [Task bar with orange arrow] | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| CL2300 | Formal Public Comment G&M DD | 30 | 30 | 28OCT08 | 28NOV08 | [Task bar with yellow arrow] | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| CL2310 | Prepare/Submit Final G&M DD | 20 | 20 | 05JAN09 | 30JAN09 | [Task bar with green arrow] | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| CL2320 | EPA Issue G&M DD | 15 | 15 | 02FEB09 | 23FEB09 | [Task bar with orange arrow] | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| CL2325 | Prepare/Submit Draft G&M LTM Plan | 45 | 45 | 24FEB09 | 27APR09 | [Task bar with green arrow] | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| CL2335 | Agency Review/Approve Draft G&M LTM Plan | 60* | 60* | 28APR09 | 22JUL09 | [Task bar with orange arrow] | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| CL2345 | Prepare/Submit Final G&M LTM Plan | 20 | 20 | 23JUL09 | 19AUG09 | [Task bar with green arrow] | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| CL2355 | Prepare/Submit Draft G&M Interim RA & Close-Out | 60 | 60 | 24JUN09 | 17SEP09 | [Task bar with green arrow] | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| CL2365 | Agency Review/Approve Draft G&M Interim RA & Close-Out | 55 | 55 | 18SEP09 | 08DEC09 | [Task bar with orange arrow] | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| CL2375 | Prep/Sub Final G&M Interim RA & Close-Out Rpt | 20 | 20 | 16DEC09 | 14JAN10 | [Task bar with green arrow] | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| CL2385 | EPA Approve G&M Interim RA & Close-Out Rpt | 15 | 15 | 15JAN10 | 04FEB10 | [Task bar with orange arrow] | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | |

Former A Range

Former A Range Soil & Groundwater

| | | | | | |
|--------|--|------|------|----------|---------|
| 01586 | Prepare/Submit Draft Former A RI/FS | 429* | 219* | 09MAR06A | 16NOV07 |
| 01588 | Agency Review/Approve Former A RI/FS | 55 | 55 | 19NOV07 | 06FEB08 |
| 01562 | Prepare/Submit Final Former A RI/FS | 20 | 20 | 07FEB08 | 06MAR08 |
| FA0400 | Prepare/Submit Draft Former A RSP | 15 | 15 | 07MAR08 | 27MAR08 |
| FA0410 | Agency Review/Approve Draft Former A RSP | 55 | 55 | 28MAR08 | 13JUN08 |
| FA0420 | Prepare/Submit Final Former A RSP | 10 | 10 | 16JUN08 | 27JUN08 |
| FA0430 | Formal Public Comment Former A RSP | 30 | 30 | 28JUN08 | 28JUL08 |
| FA0500 | Prepare/Submit Draft Former A DD | 20 | 20 | 29JUL08 | 25AUG08 |

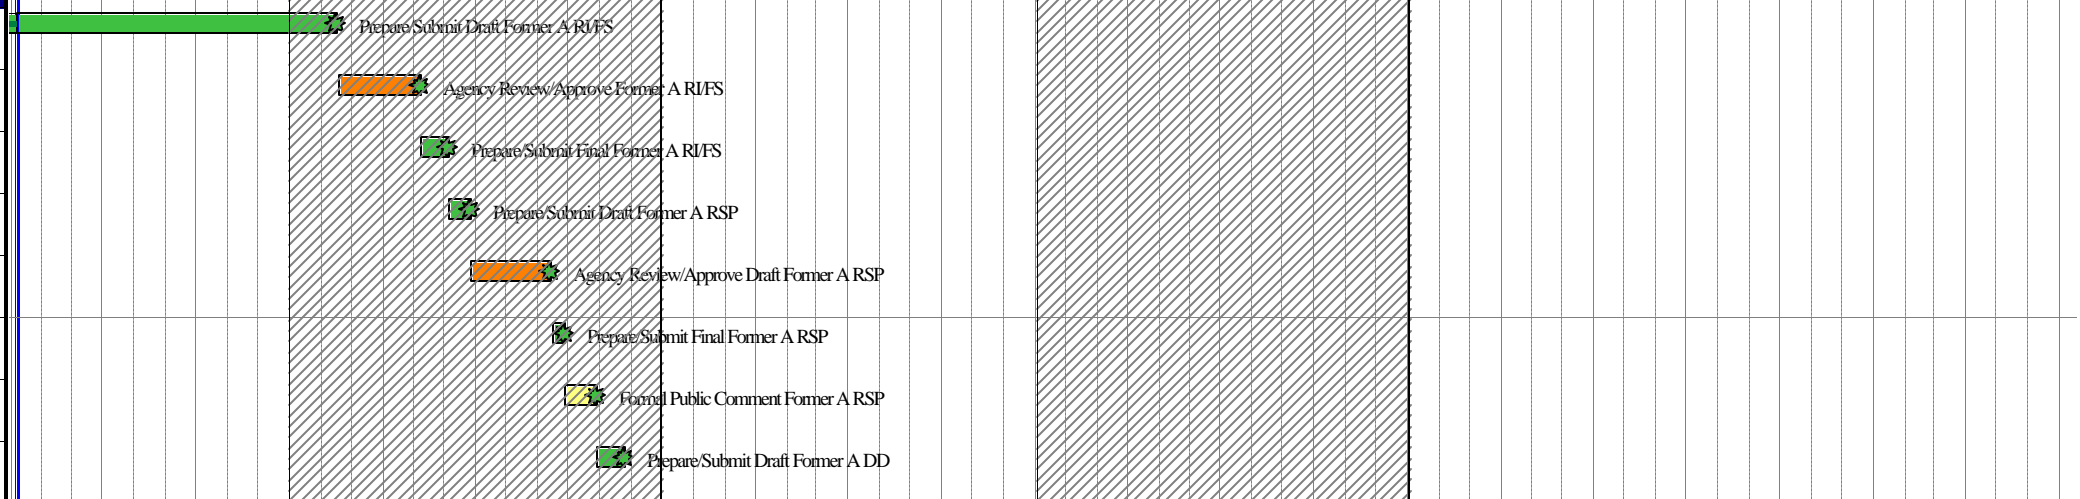

| Activity ID | Activity Description | Orig Dur | Rem Dur | Anticipated /Actual Start | Anticipated /Actual Finish | FY07 | | | | FY08 | | | | FY09 | | | | FY10 | | | | FY11 | | | | FY12 | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | |
|-------------|---|----------|---------|---------------------------|----------------------------|------|---|---|---|------|---|---|---|------|---|---|---|------|---|---|---|------|---|---|---|------|---|---|---|---|---|---|---|---|---|---|---|---|---|---|---|---|---|---|---|---|---|---|---|---|---|---|---|---|---|---|---|---|---|---|---|---|---|---|---|
| | | | | | | J | F | M | A | M | J | J | A | S | O | N | D | J | F | M | A | M | J | J | A | S | O | N | D | J | F | M | A | M | J | J | A | S | O | N | D | J | F | M | A | M | J | J | A | S | O | N | D | J | F | M | A | M | J | J | A | S | O | N | D |
| | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| FA0510 | Agency Review/Approve Draft Former A DD | 55 | 55 | 26AUG08 | 13NOV08 | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| FA0530 | Prepare/Submit Final Former A DD | 20 | 20 | 14NOV08 | 12DEC08 | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| FA0540 | EPA Issue Former A DD | 15 | 15 | 15DEC08 | 06JAN09 | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| FA0550 | Prepare/Submit Draft Former A LTM Plan | 45 | 45 | 07JAN09 | 11MAR09 | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| FA0560 | Agency Review/Approve Draft Former A LTM Plan | 55 | 55 | 12MAR09 | 28MAY09 | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| FA0570 | Prepare/Submit Final Former A LTM Plan | 20 | 20 | 29MAY09 | 25JUN09 | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| FA0580 | Prepare/Submit Drft Frm A Interim RA & Close-Out | 60 | 60 | 30APR09 | 24JUL09 | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| FA0590 | Agency Revw/Appro Dr Frm A Interim RA & Close-Out | 55 | 55 | 27JUL09 | 13OCT09 | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| FA0600 | Prep/Sub Final Frm A Interim RA & Close-Out Rpt | 20 | 20 | 14OCT09 | 10NOV09 | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| FA0610 | EPA Approve Former A Interim RA & Close-Out Rpt | 15 | 15 | 12NOV09 | 03DEC09 | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | |

Former K Range

Former K Range Soil & Groundwater

| | | | | | | | | | | | | | | | | | | | | | | | | | | | | | |
|--------|---|------|-----|----------|---------|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|
| 01510 | Agency Review/Approve Former K RI Report | 328* | 35* | 04NOV05A | 26FEB07 | | | | | | | | | | | | | | | | | | | | | | | | |
| K01572 | Prepare/Submit Draft Final Former K RI Report | 88 | 88 | 04JUN07* | 05OCT07 | | | | | | | | | | | | | | | | | | | | | | | | |
| K01573 | Agency Review/Approve Dr Final Former K RI Rpt | 55 | 55 | 09OCT07 | 27DEC07 | | | | | | | | | | | | | | | | | | | | | | | | |
| K01574 | Prepare/Submit Final Former K RI Report | 20 | 20 | 28DEC07 | 25JAN08 | | | | | | | | | | | | | | | | | | | | | | | | |
| FK0500 | Prepare/Submit Draft Former K DD | 20 | 20 | 28JAN08 | 25FEB08 | | | | | | | | | | | | | | | | | | | | | | | | |
| FK0510 | Agency Review/Approve Draft Former K DD | 55 | 55 | 26FEB08 | 12MAY08 | | | | | | | | | | | | | | | | | | | | | | | | |
| FK0520 | Formal Public Comment Former K DD | 30 | 30 | 11MAR08 | 09APR08 | | | | | | | | | | | | | | | | | | | | | | | | |
| FK0530 | Prepare/Submit Final Former K DD | 20 | 20 | 13MAY08 | 10JUN08 | | | | | | | | | | | | | | | | | | | | | | | | |
| FK0540 | EPA Issue Former K DD | 15 | 15 | 11JUN08 | 01JUL08 | | | | | | | | | | | | | | | | | | | | | | | | |
| FK0550 | Prepare/Submit Draft Former K LTM Plan | 45 | 45 | 02JUL08 | 04SEP08 | | | | | | | | | | | | | | | | | | | | | | | | |
| FK0560 | Agency Review/Approve Draft Former K LTM Plan | 55 | 55 | 05SEP08 | 24NOV08 | | | | | | | | | | | | | | | | | | | | | | | | |
| FK0570 | Prepare/Submit Final Former K LTM Plan | 20 | 20 | 25NOV08 | 23DEC08 | | | | | | | | | | | | | | | | | | | | | | | | |
| FK0580 | Prepare/Submit Drft Frm K Interim RA & Close-Out | 60 | 60 | 27OCT08 | 22JAN09 | | | | | | | | | | | | | | | | | | | | | | | | |
| FK0590 | Agency Revw/Appro Dr Frm K Interim RA & Close-Out | 55 | 55 | 23JAN09 | 10APR09 | | | | | | | | | | | | | | | | | | | | | | | | |
| FK0600 | Prep/Sub Final Frm K Interim RA & Close-Out Rpt | 20 | 20 | 13APR09 | 08MAY09 | | | | | | | | | | | | | | | | | | | | | | | | |
| FK0610 | EPA Approve Former K Interim RA & Close-Out Rpt | 15 | 15 | 11MAY09 | 01JUN09 | | | | | | | | | | | | | | | | | | | | | | | | |

Phase II b

Phase II (b) Soil & Groundwater

| | | | | | | | | | | | | | | | | | | | | | | | | | | | | | |
|-------|--|--------|-----|----------|---------|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|
| 01560 | Agency Review/Approve Draft IIb Investig. Report | 1,030* | 64* | 01APR03A | 06APR07 | | | | | | | | | | | | | | | | | | | | | | | | |
|-------|--|--------|-----|----------|---------|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|

| Activity ID | Activity Description | Orig Dur | Rem Dur | Anticipated /Actual Start | Anticipated /Actual Finish | FY07 | | | | | | | | | | | | FY08 | | | | | | | | | | | | FY09 | | | | | | | | | | | | FY10 | | | | | | | | | | | | FY11 | | | | | | | | | | | | FY12 | | | | | | | | | | | | | | | | | | | | | | | |
|-------------|--|----------|---------|---------------------------|----------------------------|------|---|---|---|---|---|---|---|---|---|---|---|------|---|---|---|---|---|---|---|---|---|---|---|------|---|---|---|---|---|---|---|---|---|---|---|------|---|---|---|---|---|---|---|---|---|---|---|------|---|---|---|---|---|---|---|---|---|---|---|------|---|---|---|---|---|---|---|---|---|---|---|---|---|---|---|---|---|---|---|---|--|--|--|
| | | | | | | J | F | M | A | M | J | J | A | S | O | N | D | J | F | M | A | M | J | J | A | S | O | N | D | J | F | M | A | M | J | J | A | S | O | N | D | J | F | M | A | M | J | J | A | S | O | N | D | J | F | M | A | M | J | J | A | S | O | N | D | J | F | M | A | M | J | J | A | S | O | N | D | J | F | M | A | M | J | J | A | S | | | |
| | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| WA0006 | Agency Review/Approve Draft WASA Soil/GW Investg | 55 | 55 | 08MAY08 | 25JUL08 | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| WA0008 | Prepare Final WASA Soil/GW Investigation Report | 20 | 20 | 28JUL08 | 22AUG08 | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| WA0000 | Prepare/Submit Draft WASA Soil RRA Plan | 60 | 60 | 25AUG08 | 19NOV08 | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| WA0010 | Agency Review/Approve Draft WASA Soil RRA Plan | 55 | 55 | 21NOV08 | 09FEB09 | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| WA0020 | Informal Public Comment WASA Soil RRA Plan | 15 | 15 | 12DEC08 | 27DEC08 | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| WA0030 | Prepare/Submit Final WASA Soil RRA Plan | 20 | 20 | 10FEB09 | 10MAR09 | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| WA0040 | Conduct WASA Soil RRA | 30 | 30 | 11MAR09 | 21APR09 | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| WA0050 | Prepare/Submit Draft WASA Soil COWR | 60 | 60 | 22APR09 | 16JUL09 | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| WA0060 | Agency Review/Approve Draft WASA Soil COWR | 55 | 55 | 17JUL09 | 02OCT09 | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| WA0070 | Prepare/Submit WASA Final Soil COWR | 20 | 20 | 05OCT09 | 02NOV09 | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| WA0080 | Prepare/Submit Draft WASA NFA DD | 45 | 45 | 03NOV09 | 08JAN10 | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| WA0090 | Agency Review/Approve Draft WASA NFA DD | 55 | 55 | 11JAN10 | 29MAR10 | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| WA0100 | Formal Public Comment WASA NFA DD | 22 | 22 | 25JAN10 | 24FEB10 | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| WA0110 | Prepare/Submit Final WASA NFA DD | 20 | 20 | 30MAR10 | 26APR10 | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| WA0120 | EPA Issue WASA NFA DD | 15 | 15 | 27APR10 | 17MAY10 | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | |
