
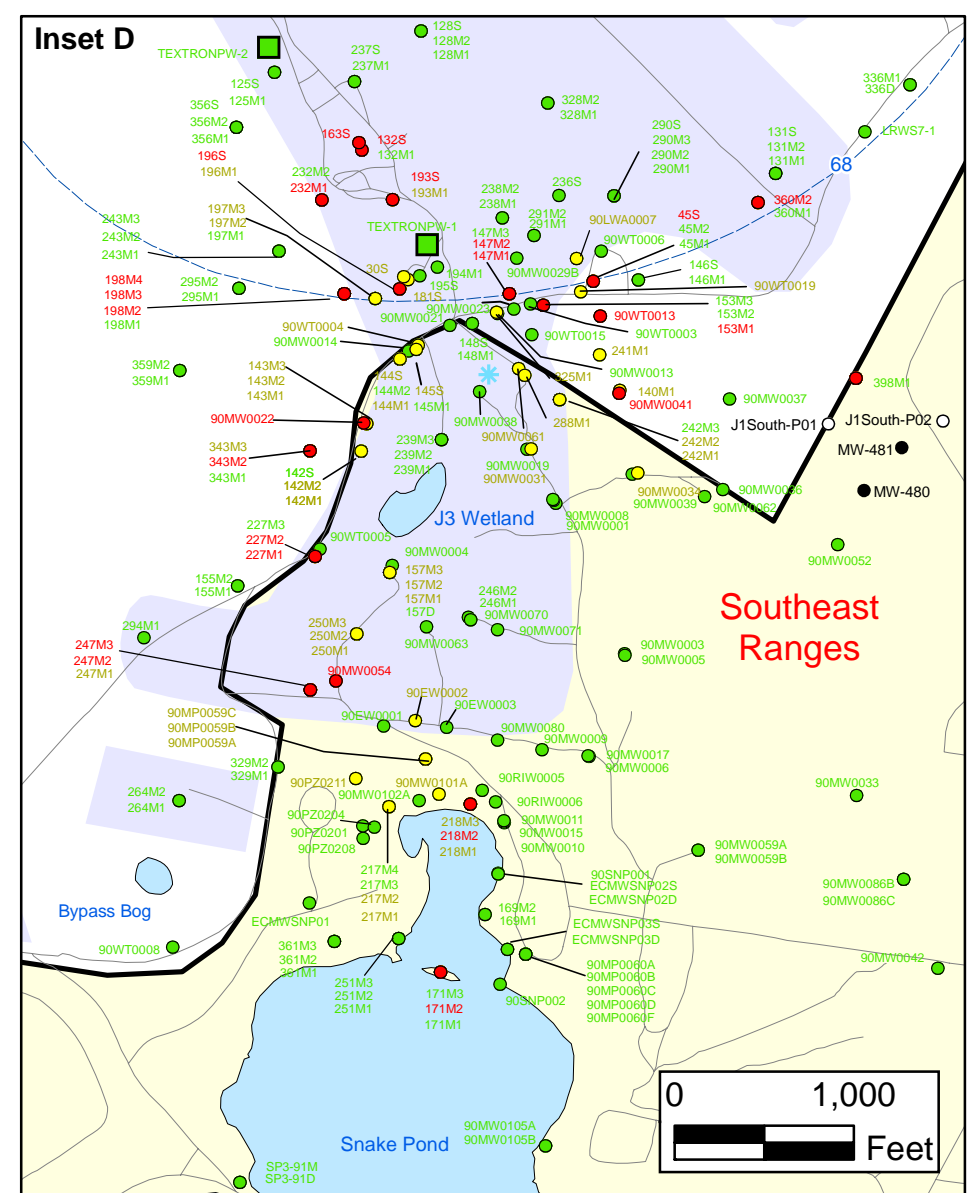
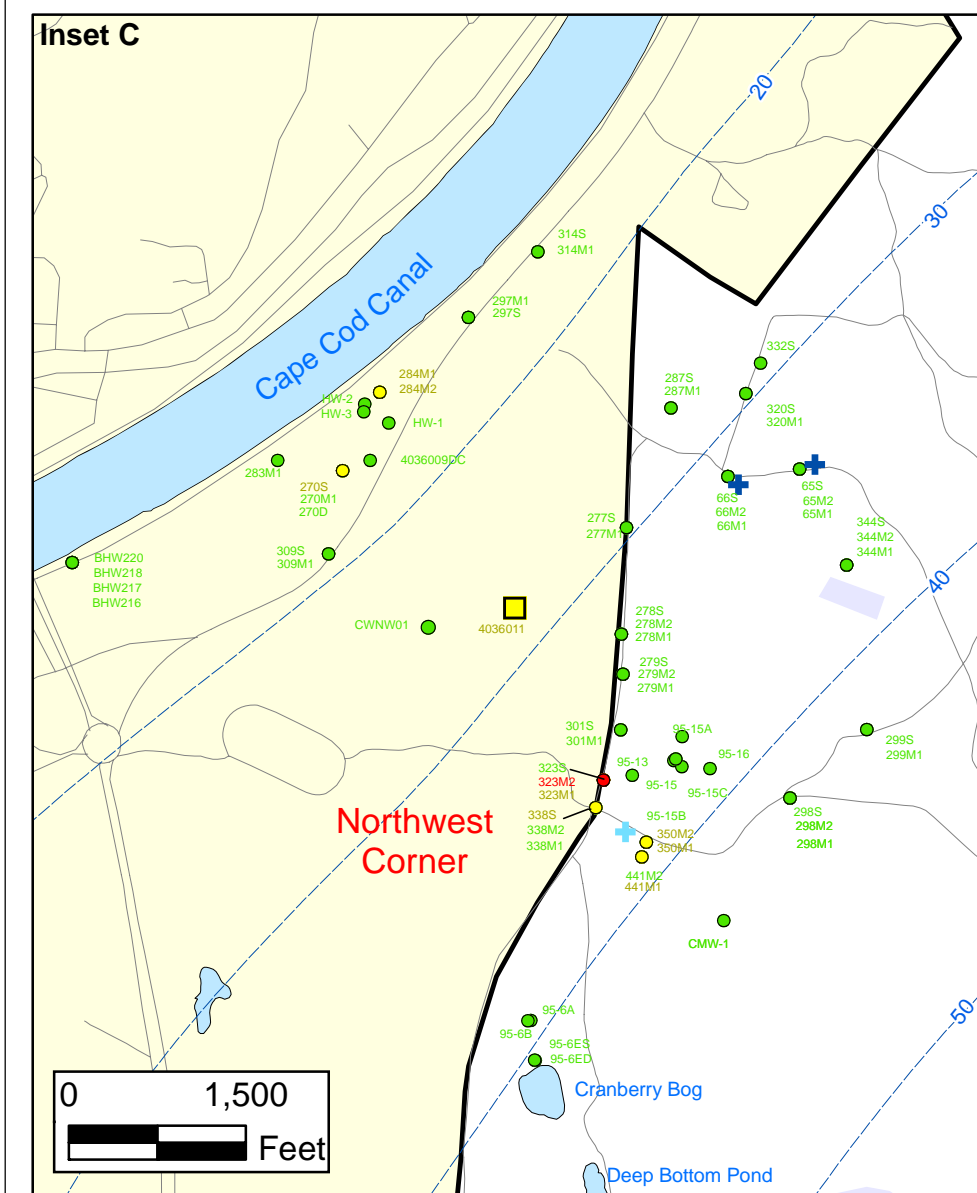


Explosives in Groundwater Compared to Maximum Contaminant Level/Health Advisories
Validated Data as of 2/23/07

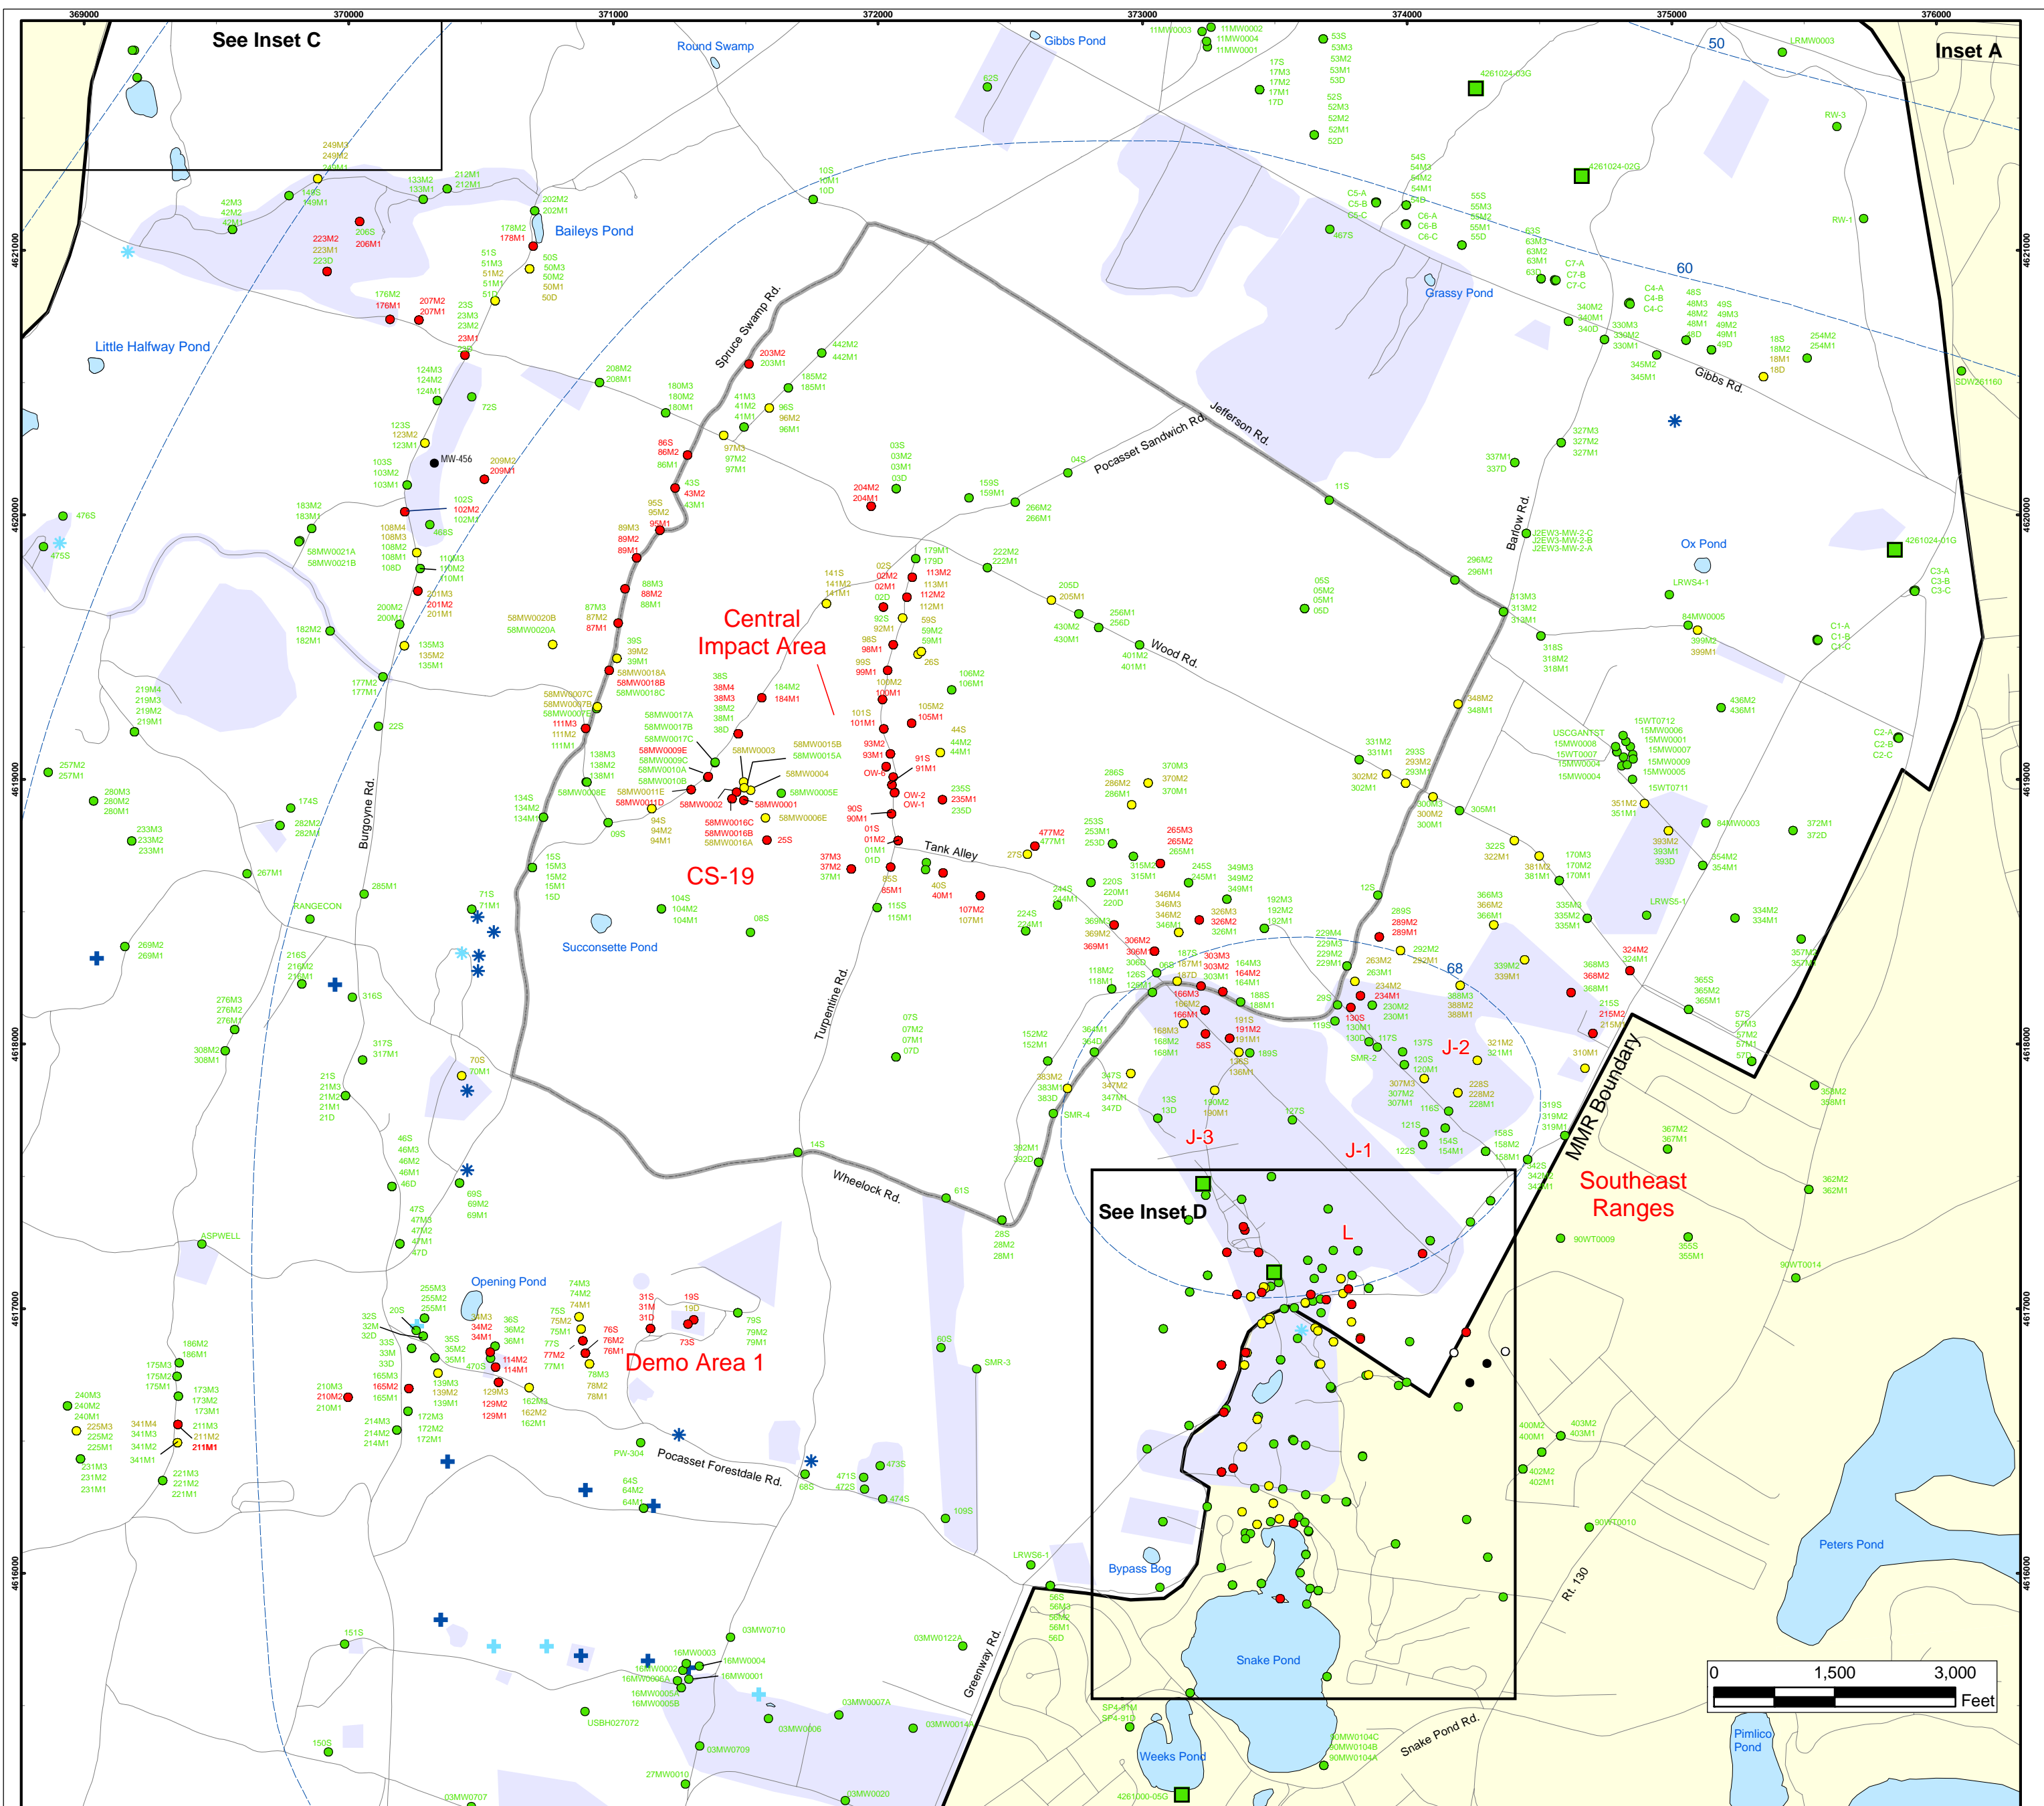

Explosives in Groundwater Compared to Maximum Contaminant Level/Health Advisories

Validated Data as of 2/23/07



- Validated Detection Greater than or Equal to Maximum Contaminant Level/Health Advisories
- Validated Detection Less than Maximum Contaminant Level/Health Advisories
- Validated Non-Detect
- Data Pending
- Proposed Monitoring Well
- Military Range Areas
- + Current Gun Position
- * Current Mortar Position
- + Old Gun Position
- * Old Mortar Position
- Validated Non-Detect Water Supply Well
- Validated Detection Less than Maximum Contaminant Level/Health Advisories Water Supply Well
- Water Table Contour (Feet NGVD), AMEC, September 2003

Note: Map dot colors are representative of the highest historical concentration at each well and not the current concentration level. Historical data presented on this figure range from November 1996 through 2007.

AMEC Earth & Environmental, Inc.
Westford, Massachusetts

Sources & Notes
Base map data from US Geological Survey
7 1/2 minute Topographic Maps
Source: Office of Geographic and
Environmental Information (MassGIS)
Commonwealth of Massachusetts
Executive Office of Environmental Affairs

FIGURE 1
Inset Map

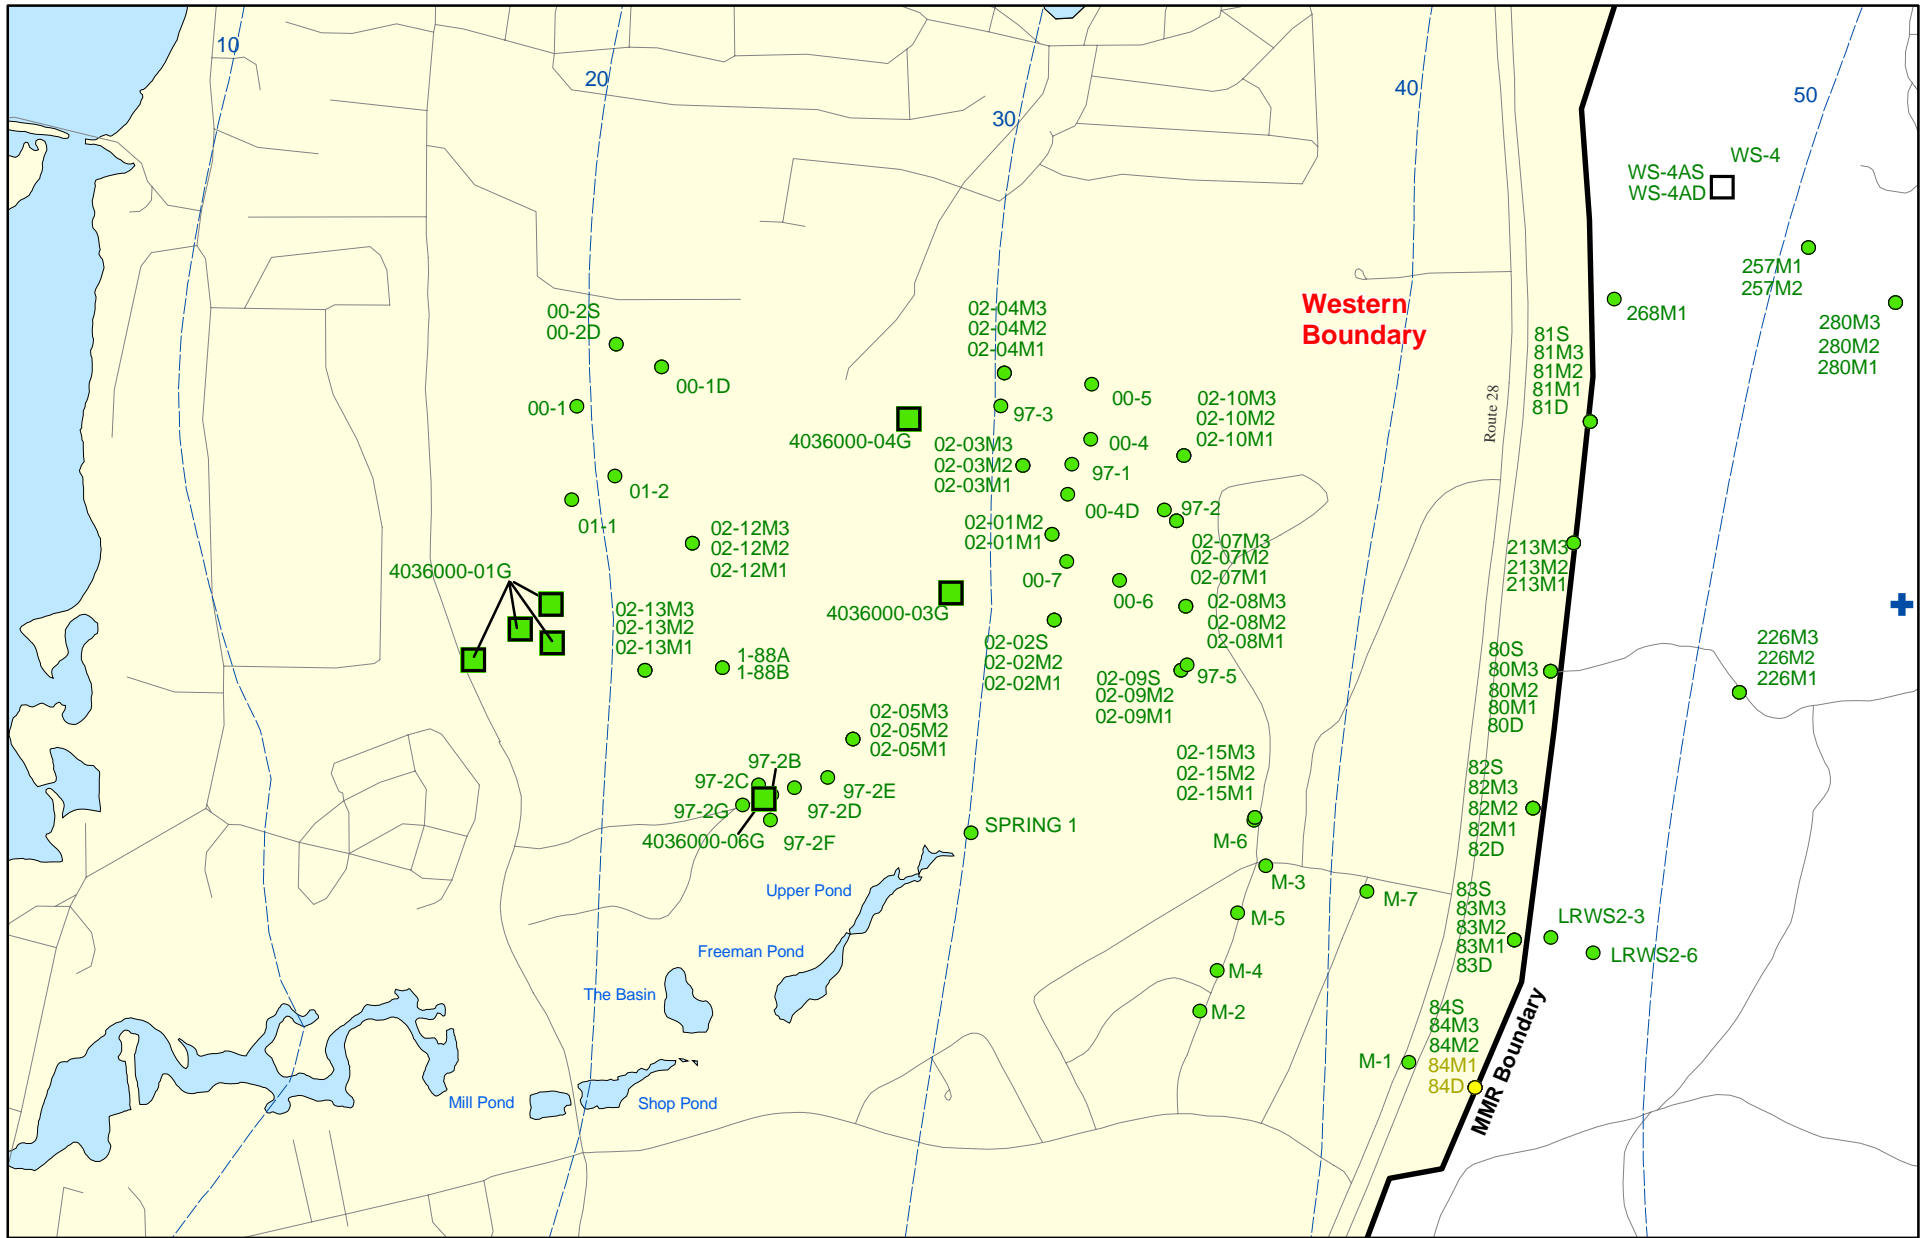



Sources & Notes:
 Base map data from US Geological Survey
 7 1/2 minute Topographic maps.
 Source: Office of Geographic and
 Environmental Information (MassGIS)
 Commonwealth of Massachusetts
 Executive Office of Environmental Affairs

- Validated Detection Less than Maximum Contaminant Level/Health Advisories
- Validated Non-Detect
- + Current Gun Position
- Validated Non-Detect Water Supply Well
- Proposed Water Supply Well
- Water Table Contour (Feet NGVD)
AMEC, September 2003

Note: Map dot colors are representative of the highest historical concentration at each well and not the current concentration level.
 Historical data presented on this figure range from November 1996 through 2007.

Explosives in Groundwater Compared to Maximum Contaminant Level/Health Advisories Validated Data as of 2/23/07



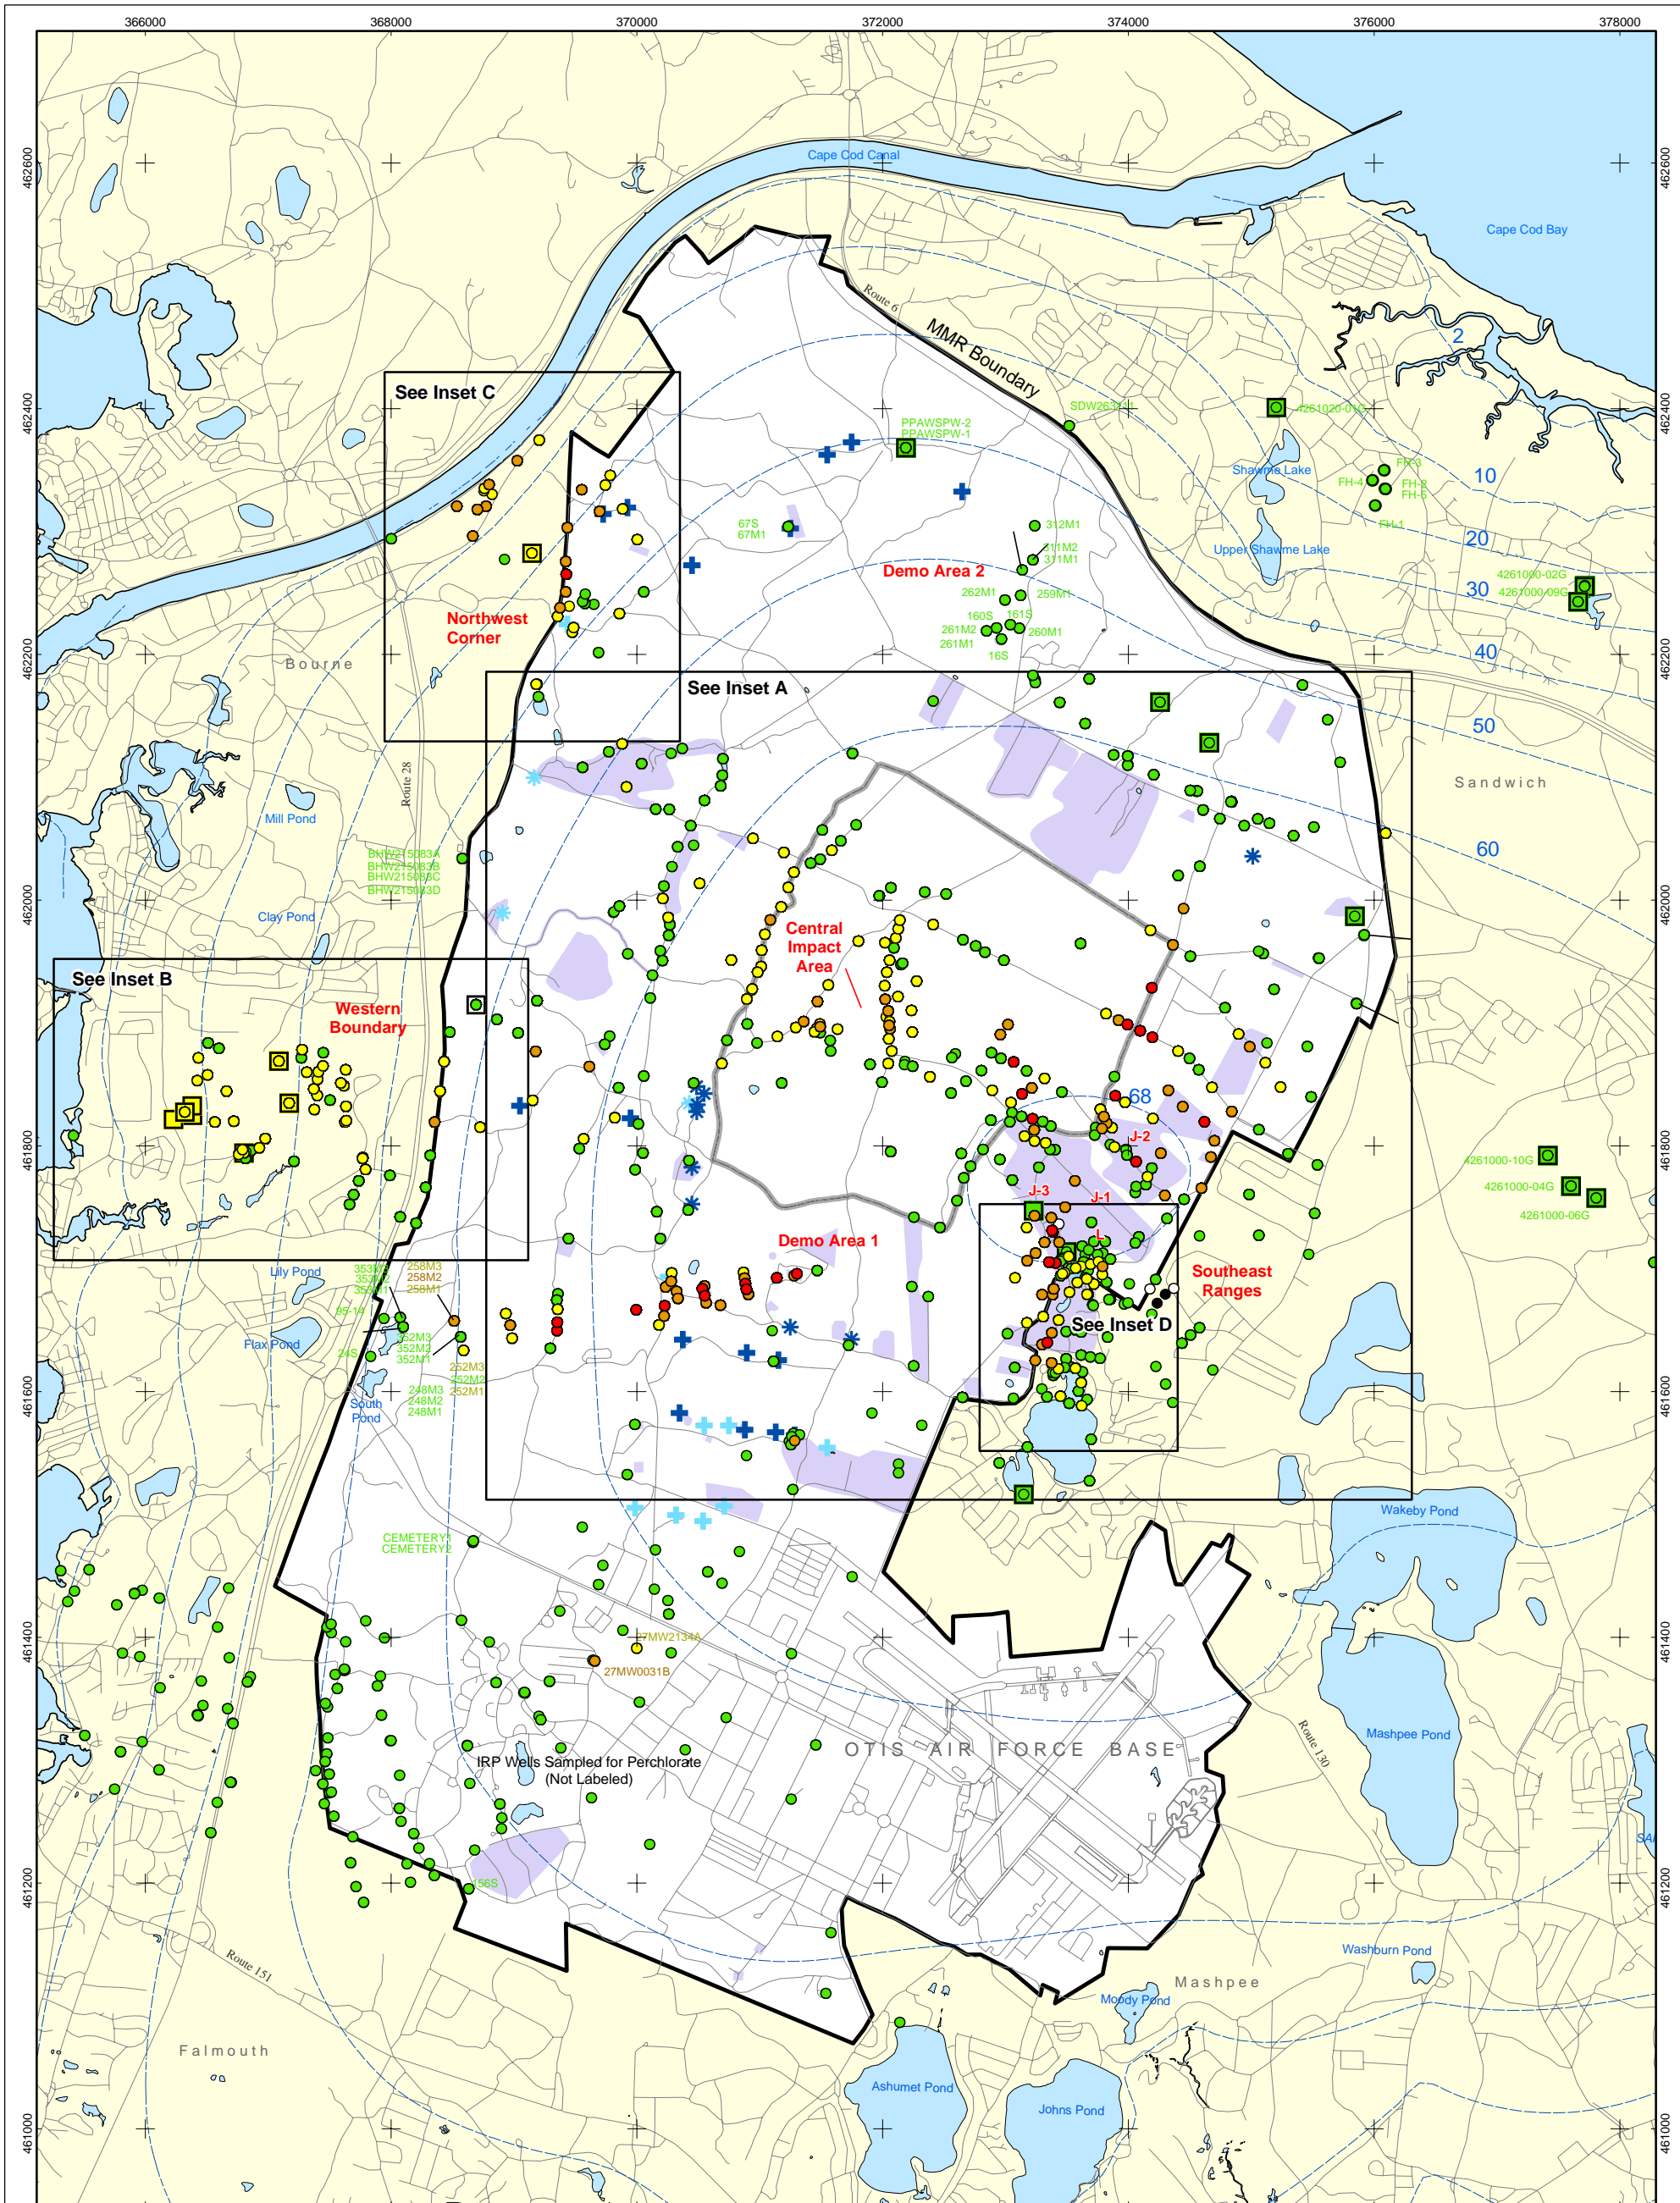


- Validated Detection Greater than or Equal to 24 ppb
- Validated Detection Greater than or Equal to 2 and Less than 24 ppb
- Validated Detection Greater than Non-Detect and Less than 2 ppb
- Validated Non-Detect

Note: Map dot colors are representative of the highest historical concentration at each well and not the current concentration level. Historical data presented on this figure range from November 1996 through 2007.

- Data Pending
- Proposed Monitoring Well
- Current Gun Position
- Current Mortar Position
- Old Gun Position
- Old Mortar Position




- Validated Non-Detect Water Supply Well
- Validated Detection Less than 2 ppb Water Supply Well
- Proposed Water Supply Well
- Water Table Contour (Feet NGVD) AMEC, September 2003
- Military Range Areas



0 2,000 4,000
Feet

Sources & Notes
Base map data from US Geological Survey
7 1/2 minute Topographic Maps.
Source: Office of Geographic and Environmental Information (MassGIS)
Commonwealth of Massachusetts
Executive Office of Environmental Affairs

**Perchlorate in Groundwater
Compared to a 2 ppb Concentration
Validated Data as of 2/23/07**

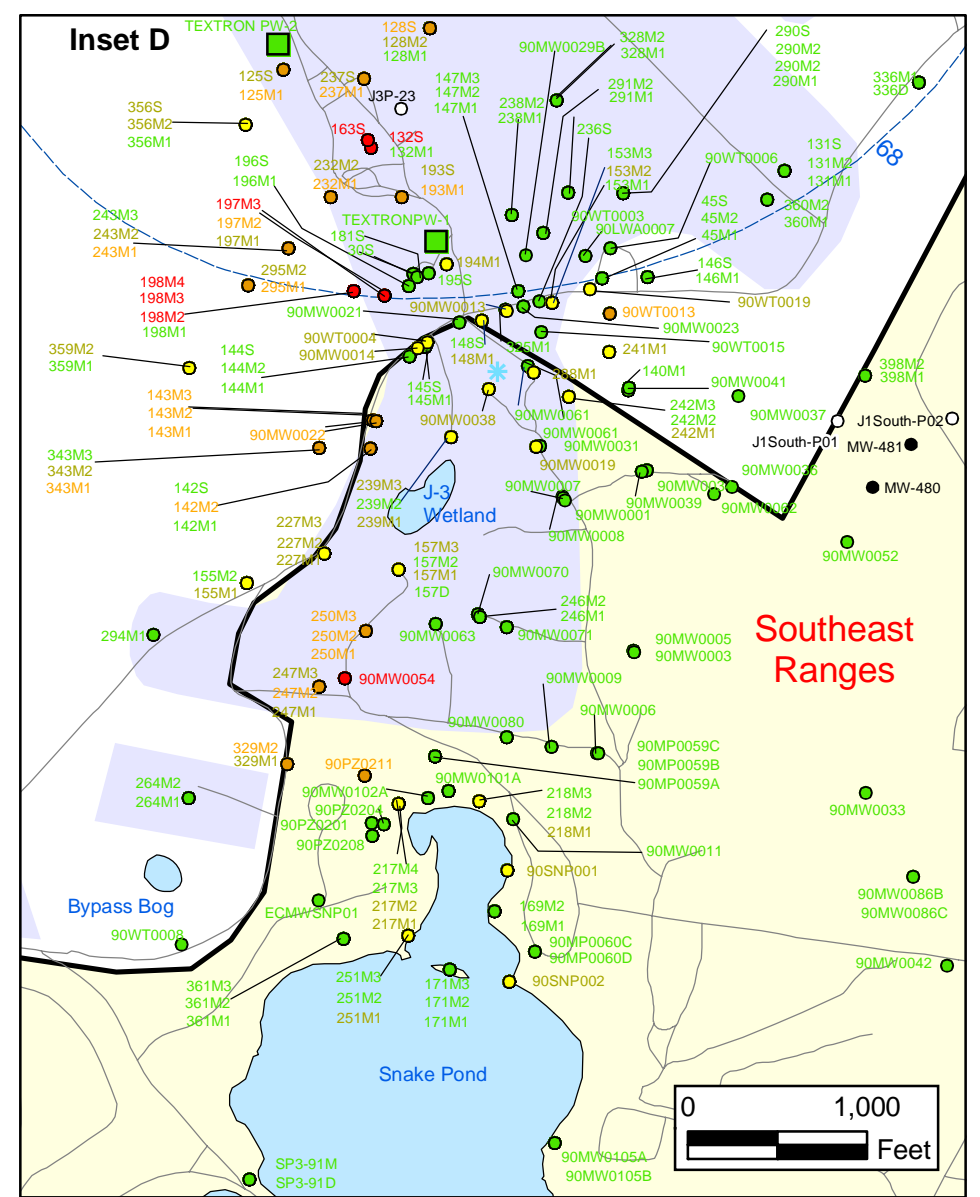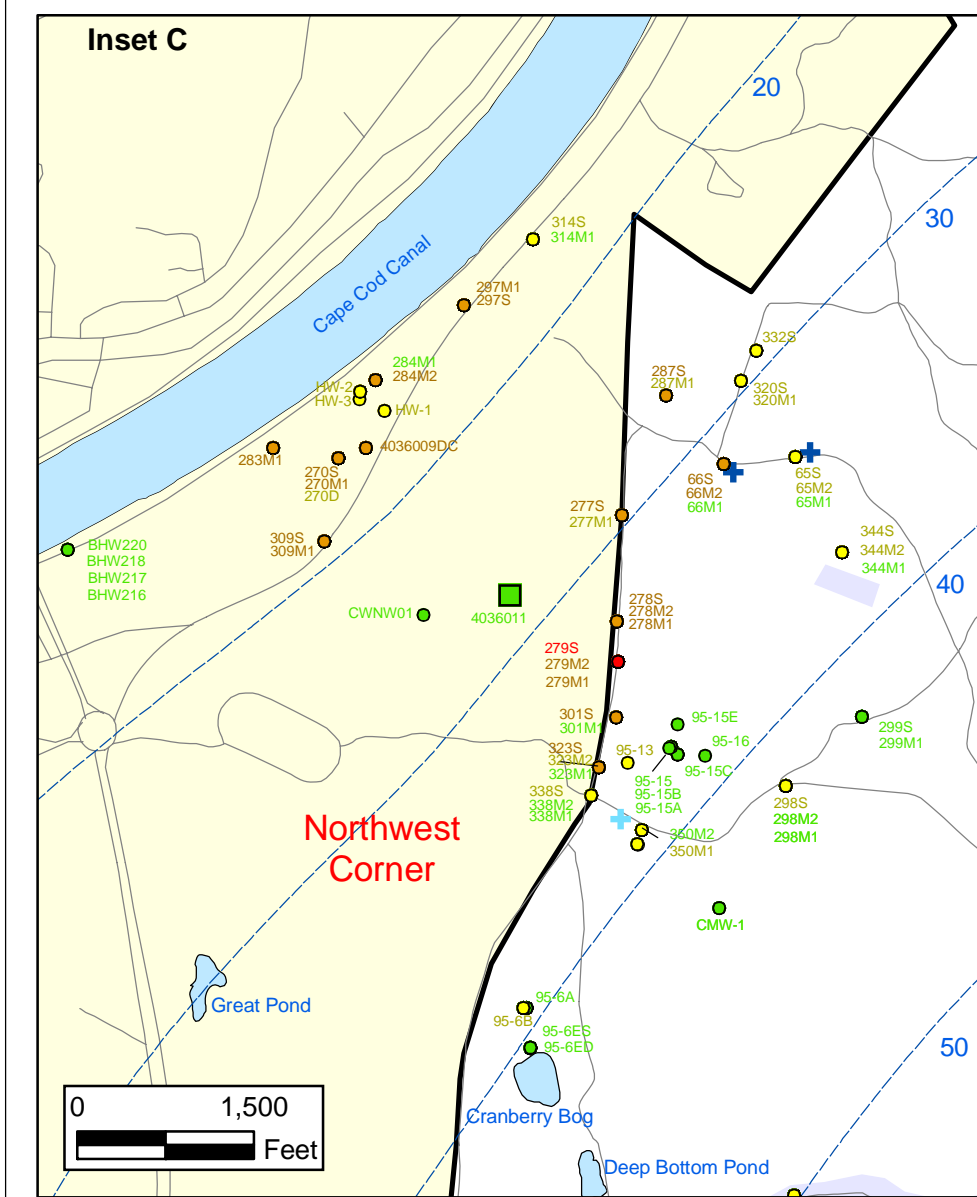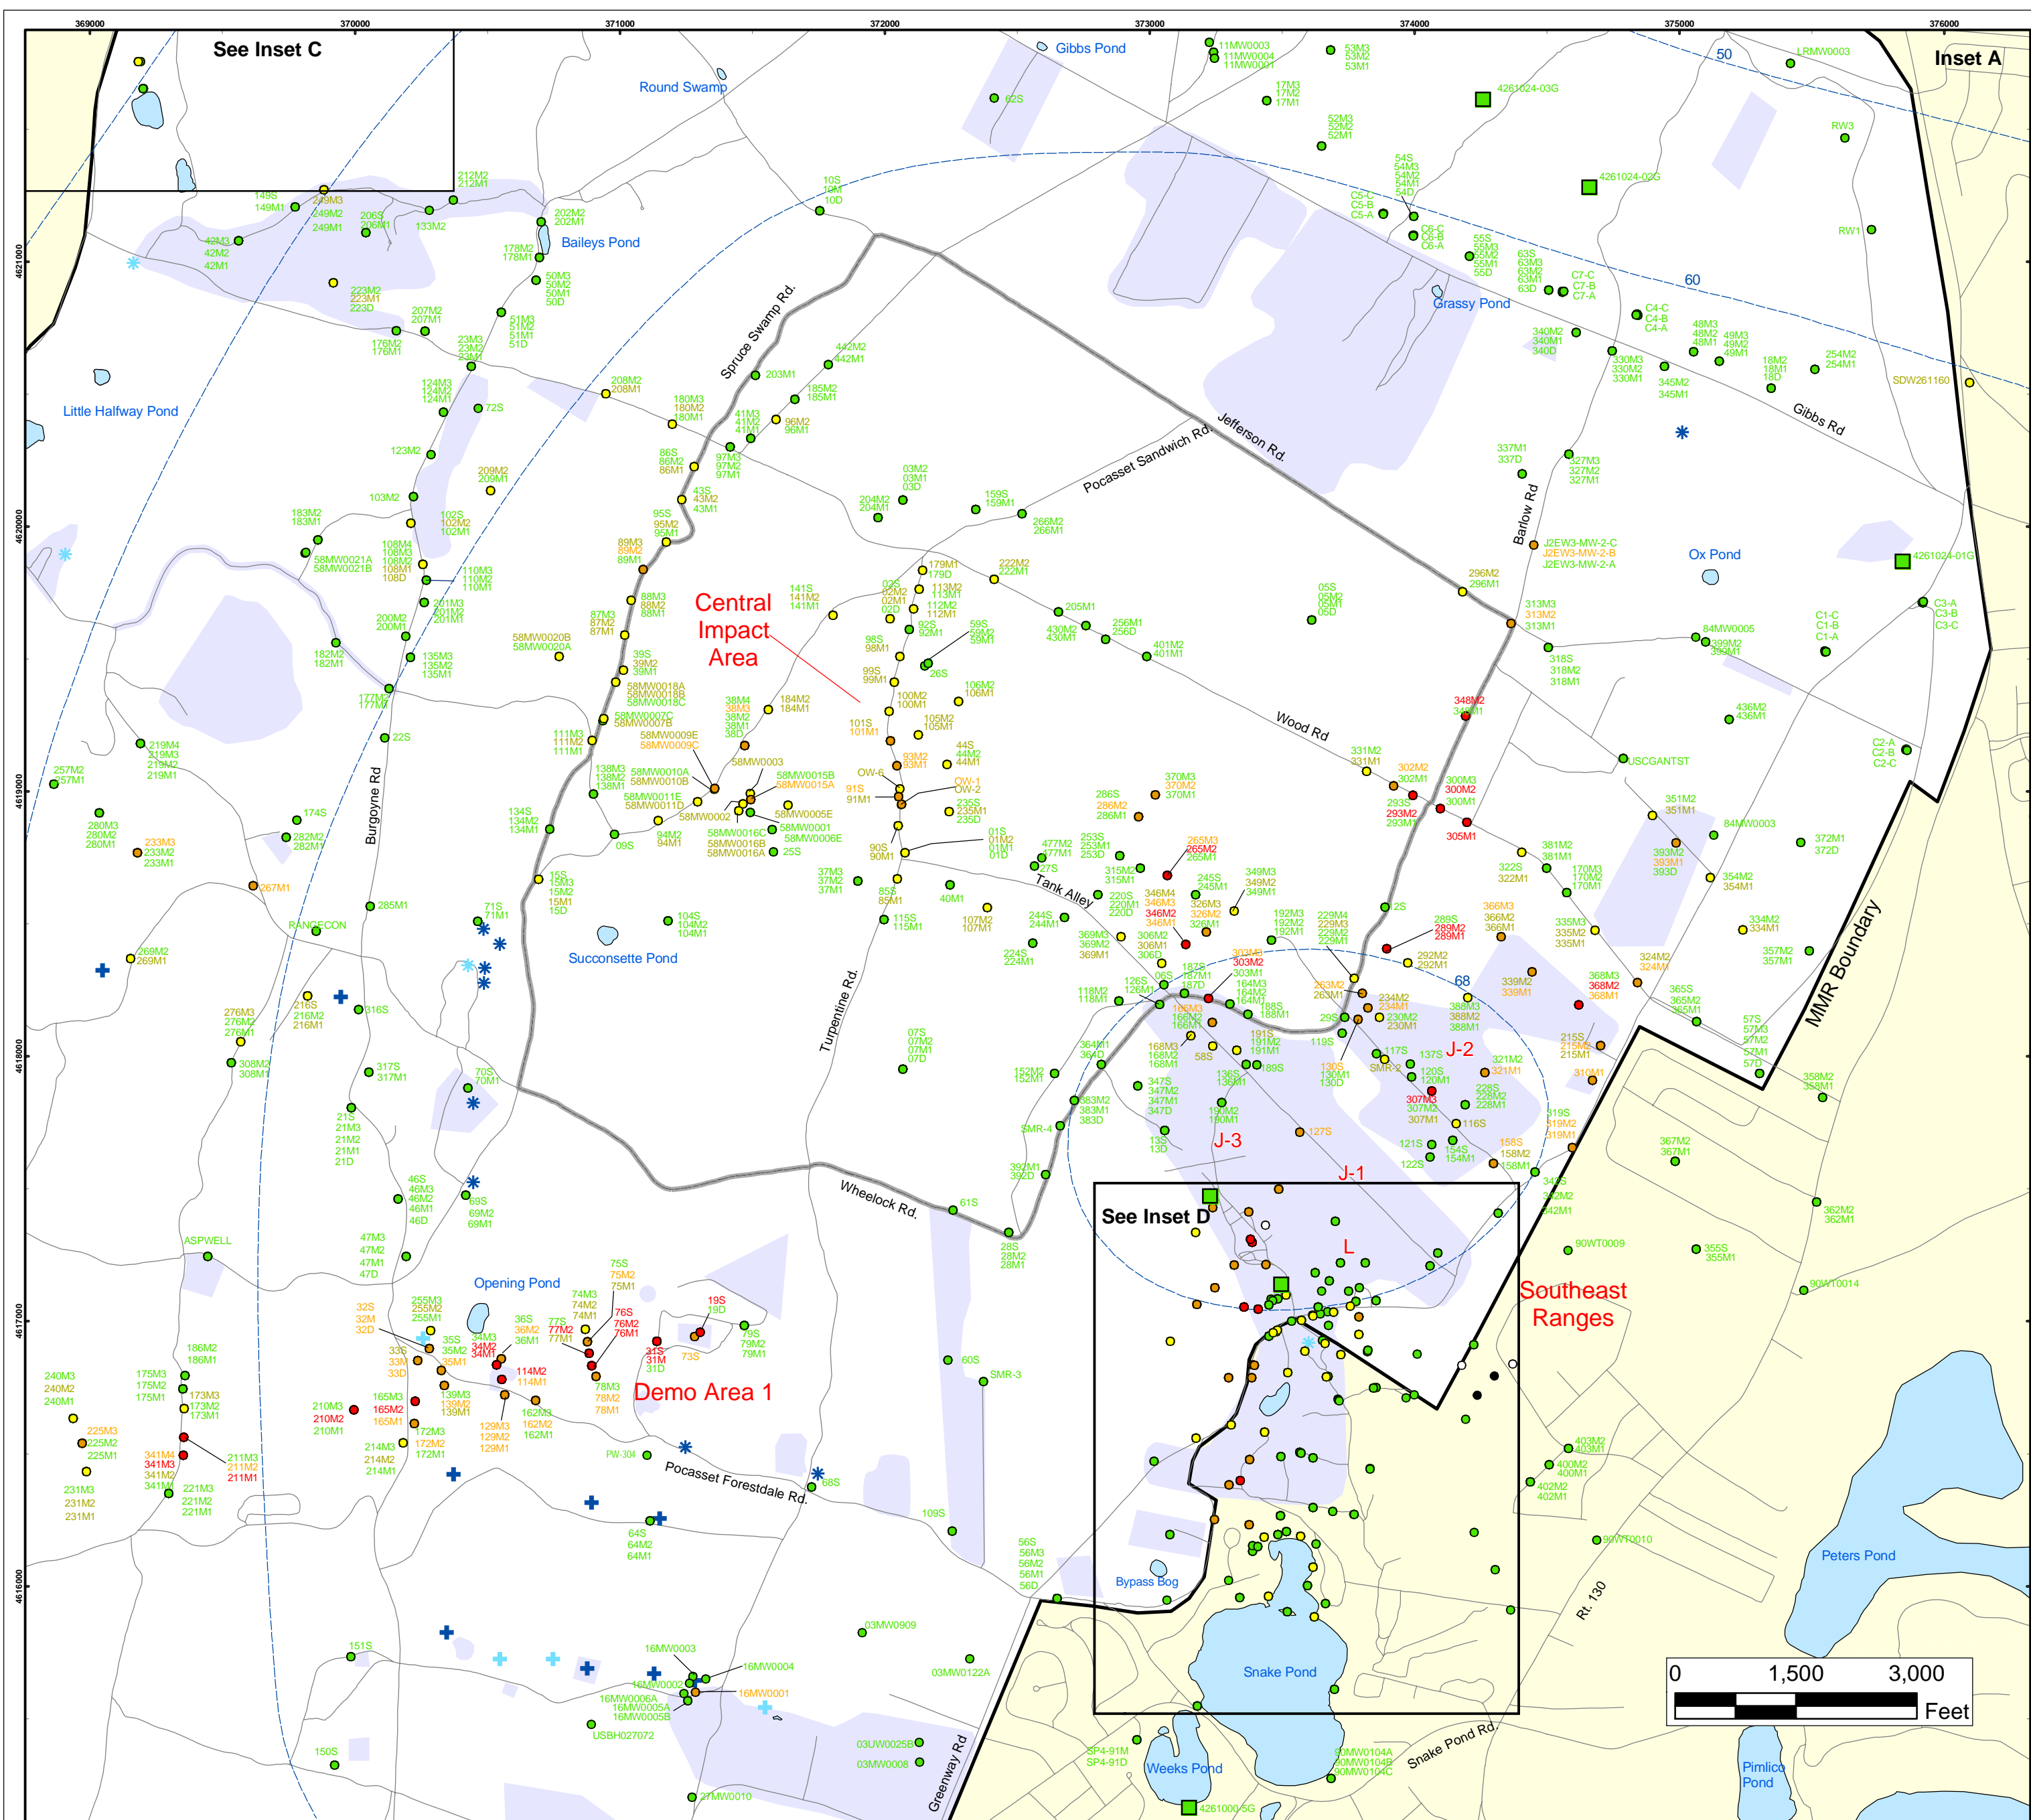

Perchlorate in Groundwater Compared to a 2 PPB Concentration Validated Data as of 2/23/07

- Validated Detection Greater than or Equal to 24 ppb
- Validated Detection Greater than or Equal to 2 and Less than 24 ppb
- Validated Detection Less than 2 ppb
- Validated Non-Detect
- Data Pending
- Proposed Monitoring Well
- Military Range Areas
- + Current Gun Position
- * Current Mortar Position
- + Old Gun Position
- * Old Mortar Position
- Validated Non-Detect Water Supply Well
- Water Table Contour (Feet NGVD), AMEC, September 2003



Note: Map dot colors are representative of the highest historical concentration at each well and not the current concentration level. Historical data presented on this figure range from November 1996 through 2007.

Impact Area
Groundwater Study Program

Sources & Notes
Base map data from US Geological Survey
7 1/2 minute Topographic Maps
Source: Office of Geographic and
Environmental Information (MassGIS)
Commonwealth of Massachusetts
Executive Office of Environmental Affairs

AMEC Earth & Environmental, Inc.
Westford, Massachusetts

FIGURE
Inset Map
8

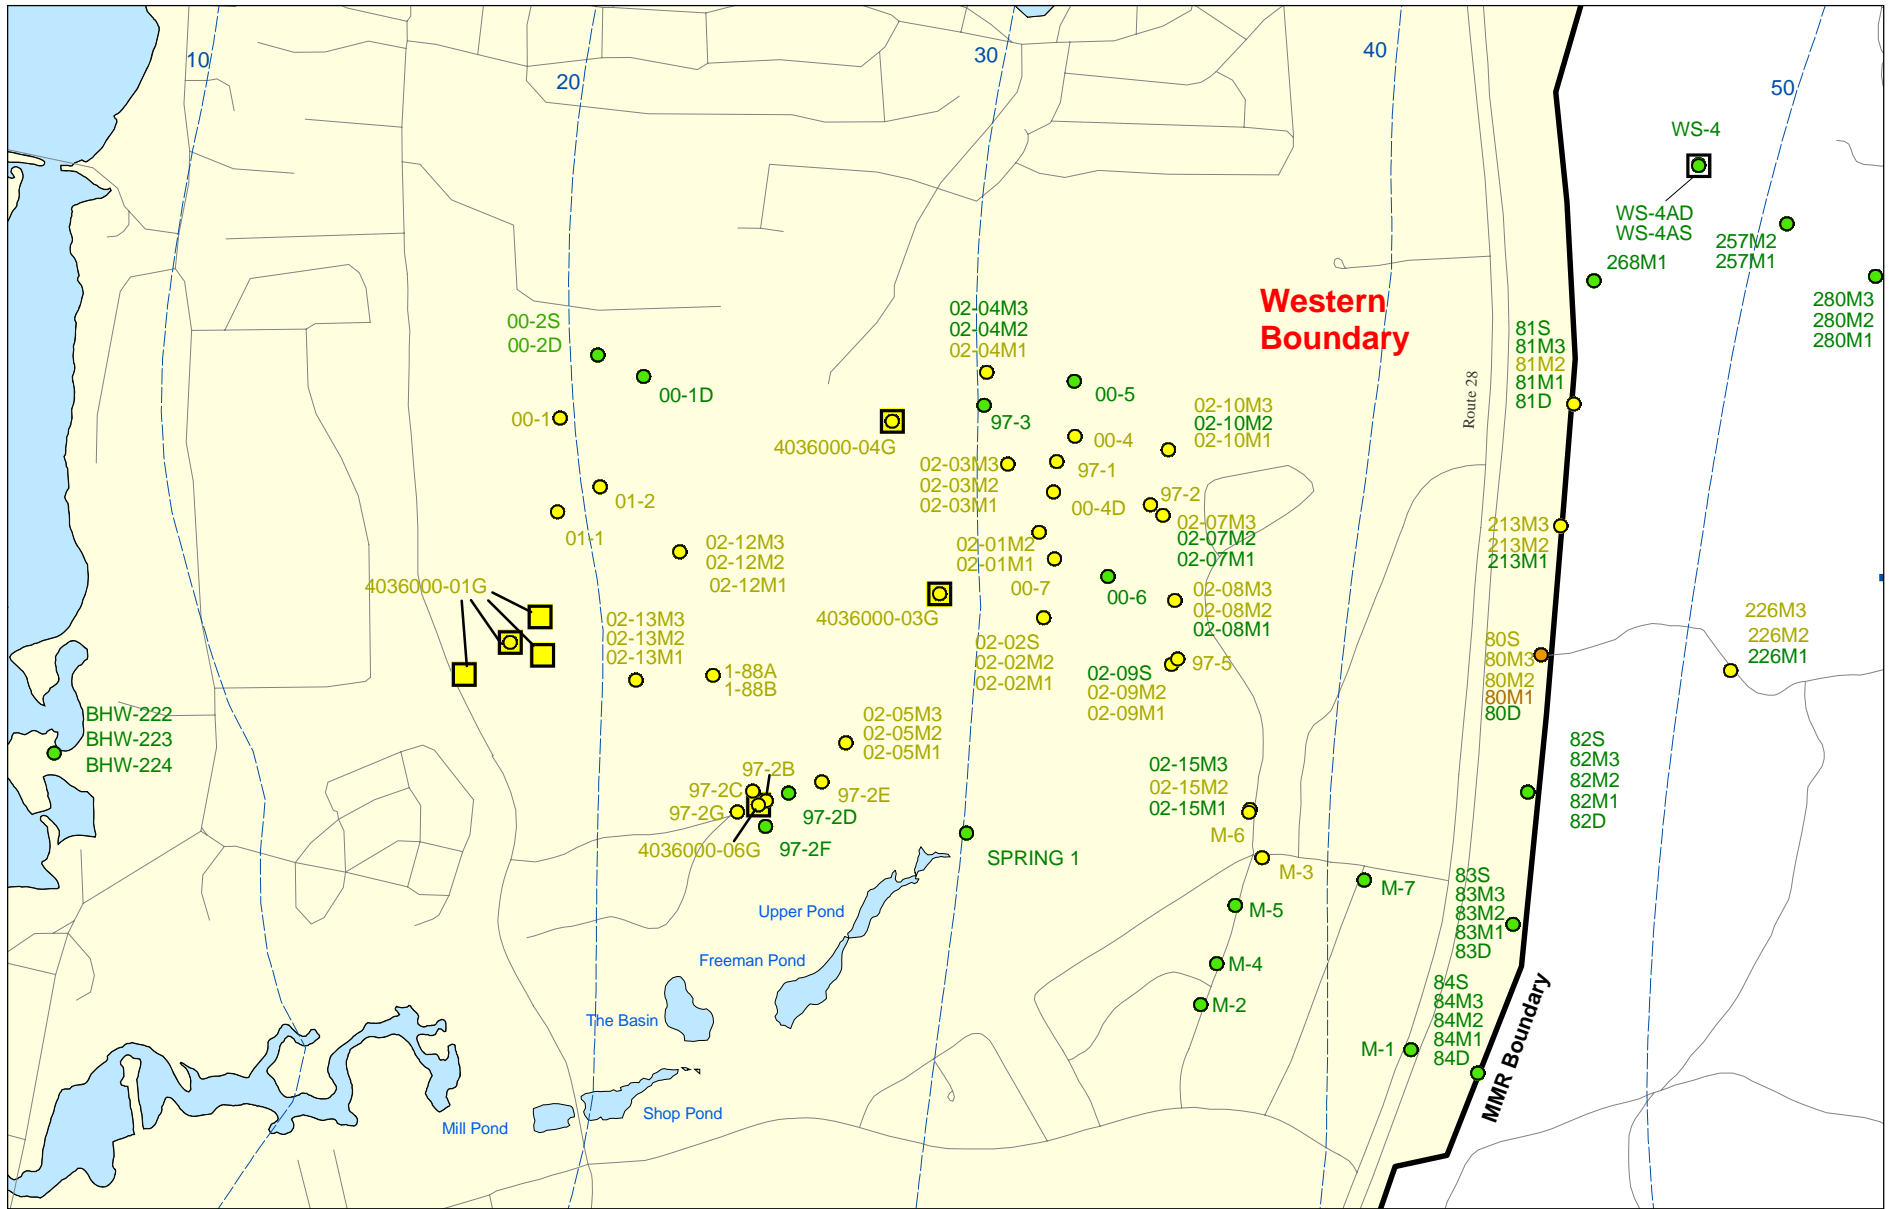


Sources & Notes:
 Base map data from US Geological Survey
 7 1/2 minute Topographic maps.
 Source: Office of Geographic and
 Environmental Information (MassGIS)
 Commonwealth of Massachusetts
 Executive Office of Environmental Affairs

- Validated Detection Greater than or Equal to 2 and Less than 24 ppb
- Validated Detection Greater than Non-Detect and Less than 2 ppb
- Validated Non-Detect

- Validated Detection Less than 2 ppb Water Supply Well
- Proposed Water Supply Well
- ⊕ Current Gun Position
- - - Water Table Contour (Feet NGVD)
AMEC, September 2003

Note: Map dot colors are representative of the highest historical concentration at each well and not the current concentration level.
 Historical data presented on this figure range from November 1996 through 2007.

Perchlorate in Groundwater Compared to a 2 ppb Concentration
Validated Data as of 2/23/07



AMEC Earth & Environmental, Inc.
 Westford, Massachusetts

Inset Map B **8**

Activity ID	Activity Description	Orig Dur	Rem Dur	Anticipated /Actual Start	Anticipated /Actual Finish	FY07					FY08					FY09					FY10					FY11					FY12																																					
						J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M
Demo 1																																																																				
Demolition Area 1 Soil																																																																				
00145	Agency Review/Approve Draft Demo 1 RRA Soil COWR	313*	52*	22DEC05A	21MAR07	Agency Review/Approve Draft Demo 1 RRA Soil COWR preparing RCL																																																														
DM0920	Prepare/Submit Final Demo 1 RRA Soil COWR	20	20	22MAR07	18APR07	Prepare/Submit Final Demo 1 RRA Soil COWR																																																														
DL0000	Prepare/Submit Draft Demo 1 Soil NFA DD	45	45	19APR07	21JUN07	Prepare/Submit Draft Demo 1 Soil NFA DD																																																														
DL0080	Agency Review/Approve Draft Demo 1 Soil NFA DD	55*	55*	22JUN07	10SEP07	Agency Review/Approve Draft Demo 1 Soil NFA DD																																																														
DL0085	Formal Public Comment Demo 1 Soil NFA DD	30	30	09JUL07	07AUG07	Formal Public Comment Demo 1 Soil NFA DD																																																														
DL0100	Prepare/Submit Final Demo 1 Soil NFA DD	20	20	11SEP07	09OCT07	Prepare/Submit Final Demo 1 Soil NFA DD																																																														
DL0110	EPA Issue Demo 1 Soil NFA DD	15	15	10OCT07	30OCT07	EPA Issue Demo 1 Soil NFA DD																																																														
Demolition Area 1 Groundwater																																																																				
31575	Construct/Startup Demo 1 GW Treatment System	211*	102*	01AUG06A	31MAY07	Construct/Startup Demo 1 GW Treatment System																																																														
CL0010	Prepare/Submit Draft Demo 1 SPM Plan	60	26	02JAN07A	12FEB07	Prepare/Submit Draft Demo 1 SPM Plan																																																														
CL0100	Agency Review/Approve Draft Demo 1 SPM Plan	55*	55*	13FEB07	01MAY07	Agency Review/Approve Draft Demo 1 SPM Plan																																																														
CL0130	Prepare/Submit Final Demo 1 SPM Plan	20	20	02MAY07	30MAY07	Prepare/Submit Final Demo 1 SPM Plan																																																														
CL0140	Prepare/Submit Dr Demo 1 GW Int RA & Close-Out Rt	60	60	05APR07	28JUN07	Prepare/Submit Dr Demo 1 GW Int RA & Close-Out Rt																																																														
CL0220	Agency Revw/Appr Dr Demo 1 GW Int RA & Close-Out	55*	55*	29JUN07	17SEP07	Agency Revw/Appr Dr Demo 1 GW Int RA & Close-Out																																																														
CL0240	Prep/Sub Final Demo 1 GW Interim RA&Close-Out Rt	20	20	18SEP07	16OCT07	Prep/Sub Final Demo 1 GW Interim RA&Close-Out Rt																																																														
CL0245	EPA Approve Demo 1 GW Interim RA & Close-Out Rt	15	15	17OCT07	06NOV07	EPA Approve Demo 1 GW Interim RA & Close-Out Rt																																																														
J-1 Range																																																																				
J-1 Range Soil & Groundwater																																																																				
02185	Prepare/Submit Draft J-1 GW RRA Pln Project Note	66*	0*	02OCT06A	05JAN07A	Prepare/Submit Draft J-1 GW RRA Pln Project Note																																																														
02189	Agency Review/Approve Draft J-1 GW RRA Pjct Note	31*	31*	08JAN07A	20FEB07	Agency Review/Approve Draft J-1 GW RRA Pjct Note																																																														
02192	Informal Public Comment J-1 GW RRA Project Note	15	15	20JAN07	03FEB07	Informal Public Comment J-1 GW RRA Project Note																																																														
0920	Prepare/Submit Final J-1 GW RRA Pln Project Note	10	10	21FEB07	06MAR07	Prepare/Submit Final J-1 GW RRA Pln Project Note																																																														
02187	Design J-1 GW RRA Treatment System	120*	121*	09JAN07A	27JUN07	Design J-1 GW RRA Treatment System Assumes: design starts with agency commitments.																																																														
02191	Construct/Startup J-1 GW RRA Treatment System	66	66	17SEP07	20DEC07	Construct/Startup J-1 GW RRA Treatment System Assumes: 66 days for procurement under PBC																																																														
CL0250	Prepare/Submit Draft J-1 RRA GW SPM Plan	45	45	25APR07	27JUN07	Prepare/Submit Draft J-1 RRA GW SPM Plan																																																														
CL0330	Agency Review/Approve Draft J-1 RRA GW SPM Plan	55*	55*	28JUN07	14SEP07	Agency Review/Approve Draft J-1 RRA GW SPM Plan																																																														

General Notes:

A. 55 day - Agency Review/Approve Activity Includes:

- 15 days: Agency Review/Comment
- 15 days: Prepare/Submit RCL
- 5 days: Agency Review RCL
- 5 days: Agency Conduct CRM
- 10 days: Prepare/Submit MOR
- 5 days: Agency Approve MOR

B. FY07 Priorities

1. Demolition Area 1 GW
2. J-2 Range GW
3. J-1 Range GW
4. J-3 Range GW
5. Small Arms Ranges
6. Gun & Mortar
7. Demolition Area Soil
8. Western Boundary
9. Ammunition Supply Point

Activity Colors

- IAGWSP Activities
- Agency Activities
- Formal/Informal Public Comment Activities

Activity ID	Activity Description	Orig Dur	Rem Dur	Anticipated /Actual Start	Anticipated /Actual Finish	FY07												FY08												FY09												FY10												FY11												FY12																							
						J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D
J-2 Range Groundwater																																																																																									
CL0830	Prepare/Submit Draft J-2 GW RRA COWR	130*	37*	23AUG06A	28FEB07																																																																																				
CL0910	Agency Review/Approve Draft J-2 GW COWR	55*	55*	01MAR07	16MAY07																																																																																				
CL0930	Prepare/Submit Final J-2 GW RRA COWR	44	44	17MAY07	19JUL07																																																																																				
00699	Prepare/Submit Draft J-2 GW RI/FS Rpt	183*	8*	27APR06A	17JAN07																																																																																				
00353	Agency Review/Approve J-2 GW RI/FS Rpt	55*	55*	18JAN07	05APR07																																																																																				
0698	Prepare/Submit Final J-2 GW RI/FS Rpt	20	20	06APR07	03MAY07																																																																																				
CL1200	Prepare/Submit Draft J-2 GW RSP	15	15	18JAN07	07FEB07																																																																																				
CL1280	Agency Review/Approve Draft J-2 GW RSP	55*	55*	08FEB07	26APR07																																																																																				
CL1300	Prepare/Submit Final J-2 GW RSP	10	10	27APR07	10MAY07																																																																																				
CL1305	Formal Public Comment J-2 GW RSP	30	30	11MAY07	10JUN07																																																																																				
CL1310	Prepare/Submit Draft J-2 GW DD	20	20	11JUN07	09JUL07																																																																																				
CL1390	Agency Review/Approve Draft J-2 GW DD	55*	55*	10JUL07	25SEP07																																																																																				
CL1410	Prepare/Submit Final J-2 GW DD	20	20	26SEP07	24OCT07																																																																																				
CL1415	EPA Issue J-2 GW DD	15	15	25OCT07	15NOV07																																																																																				
00368	Design J-2 Range GW Treatment System	100	100	08FEB07	29JUN07																																																																																				
00369	Construct/Startup J-2 Range GW Treatment System	176	176	26SEP07	06JUN08																																																																																				
CL0500	Prepare/Submit Draft J-2 SPM Plan	60	60	06APR07	29JUN07																																																																																				
CL0580	Agency Review/Approve Draft J-2 SPM Plan	55*	55*	02JUL07	18SEP07																																																																																				
CL0600	Prepare/Submit Final J-2 SPM Plan	20	20	19SEP07	17OCT07																																																																																				
CL0610	Prep/Sub Draft J-2 GW Interim RA & Close-Out Rpt	60	60	11APR08	07JUL08																																																																																				
CL0690	Agency Revw/Appr Dr J-2 GW Interim RA & Close-Out	55*	55*	08JUL08	23SEP08																																																																																				
CL0710	Prepare/Submit J-2 GW Interim RA & Close-Out Rpt	20	20	24SEP08	22OCT08																																																																																				
CL0715	EPA Approve J-2 GW Interim RA & Close-Out Rpt	15	15	23OCT08	13NOV08																																																																																				
J-3 Range																																																																																									
J-3 Range Soil																																																																																									
J30027	Conduct J-3 Supplemental Soil Investigation	58	58	15JAN07	05APR07																																																																																				
J30031	Prepare/Submit Draft J-3 Soil Investig Addendum	132	132	06APR07	12OCT07																																																																																				
J30033	Agency Review/Approve J-3 Soil Investig Addendum	55*	55*	15OCT07	03JAN08																																																																																				
J30042	Prepare/Submit Final J-3 Soil Investig Addendum	20	20	04JAN08	31JAN08																																																																																				

Activity ID	Activity Description	Orig Dur	Rem Dur	Anticipated /Actual Start	Anticipated /Actual Finish	FY07												FY08												FY09												FY10												FY11												FY12																																																																																																																																				
						J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S																																																																																																																
L Range																																																																																																																																																																																																						
L Range Soil & Groundwater																																																																																																																																																																																																						
02316	Resolve Comments on Draft L Soil RI Report	315*	48*	14DEC05A	15MAR07		Resolve Comments on Draft L Soil RI Report Note: excludes UXO																																																																																																																																																																																															
0622	Resolve Comments on L GW Risk Assessment Rpt	210*	48*	16MAY06A	15MAR07		Resolve Comments on L GW Risk Assessment Rpt																																																																																																																																																																																															
0703	Prepare/Submit Draft L Soil/GW RI/FS Rpt	121*	121*	06APR07	26SEP07		Prepare/Submit Draft L Soil/GW RI/FS Rpt																																																																																																																																																																																															
0724	Agency Review/Approve Draft L Soil/GW RI/FS Rpt	55*	55*	27SEP07	17DEC07		Agency Review/Approve Draft L Soil/GW RI/FS Rpt																																																																																																																																																																																															
0722	Prepare/Submit Final L Soil/GW RI/FS Rpt	20	20	18DEC07	16JAN08		Prepare/Submit Final L Soil/GW RI/FS Rpt																																																																																																																																																																																															
SL0382	Prepare/Submit Draft L RSP	15	15	17JAN08	06FEB08		Prepare/Submit Draft L RSP																																																																																																																																																																																															
SL0383	Agency Review/Approve Draft L RSP	55	55	07FEB08	24APR08		Agency Review/Approve Draft L RSP																																																																																																																																																																																															
SL0384	Prepare/Submit Final L RSP	10	10	25APR08	08MAY08		Prepare/Submit Final L RSP																																																																																																																																																																																															
SL0386	Formal Public Comment L RSP	30	30	09MAY08	08JUN08		Formal Public Comment L RSP																																																																																																																																																																																															
SL0388	Prepare/Submit Draft L DD	20	20	09JUN08	07JUL08		Prepare/Submit Draft L DD																																																																																																																																																																																															
SL0391	Agency Review/Approve Draft L DD	55*	55*	08JUL08	23SEP08		Agency Review/Approve Draft L DD																																																																																																																																																																																															
SL0392	Prepare/Submit Final L DD	20	20	24SEP08	22OCT08		Prepare/Submit Final L DD																																																																																																																																																																																															
SL0394	EPA Issue L DD	15	15	23OCT08	13NOV08		EPA Issue L DD																																																																																																																																																																																															
SL0400	Prepare/Submit Draft L LTM Plan	60	60	14NOV08	10FEB09		Prepare/Submit Draft L LTM Plan																																																																																																																																																																																															
SL0410	Agency Review/Approve Draft L LTM Plan	55*	55*	11FEB09	29APR09		Agency Review/Approve Draft L LTM Plan																																																																																																																																																																																															
SL0420	Prepare/Submit Final L LTM Plan	20	20	30APR09	28MAY09		Prepare/Submit Final L LTM Plan																																																																																																																																																																																															
SL0430	Prepare/Submit Draft L Interim RA & Close-Out Rpt	60	60	02APR09	25JUN09		Prepare/Submit Draft L Interim RA & Close-Out Rpt																																																																																																																																																																																															
SL0440	Agency Revw/Appr Draft L Interim RA & Close-Out	55*	55*	26JUN09	14SEP09		Agency Revw/Appr Draft L Interim RA & Close-Out																																																																																																																																																																																															
SL0450	Prepare/Subm Final L Interim RA & Close-Out Rpt	20	20	15SEP09	13OCT09		Prepare/Subm Final L Interim RA & Close-Out Rpt																																																																																																																																																																																															
SL0460	EPA Approve L Interim RA & Close-Out Rpt	15	15	14OCT09	03NOV09		EPA Approve L Interim RA & Close-Out Rpt																																																																																																																																																																																															
Central Impact Area																																																																																																																																																																																																						
CIA Soil & Groundwater																																																																																																																																																																																																						
03122	Agency Review/Approve Draft CIA Soil RRA COWR	364*	18*	19AUG05A	31JAN07		Agency Review/Approve Draft CIA Soil RRA COWR																																																																																																																																																																																															
CIA2770	Prepare/Submit Final CIA Soil RRA COWR	20	20	01FEB07	01MAR07		Prepare/Submit Final CIA Soil RRA COWR																																																																																																																																																																																															
00261	Prepare/Submit Draft CIA Soil Investigation Rpt	846*	144*	04APR04A	31JUL07		Prepare/Submit Draft CIA Soil Investigation Rpt																																																																																																																																																																																															
00263	Agency Review/Approve Draft CIA Soil Investigatn	55	55	01AUG07	18OCT07		Agency Review/Approve Draft CIA Soil Investigatn																																																																																																																																																																																															
00299	Prepare/Submit Final CIA Soil Investigation Rpt	20	20	19OCT07	16NOV07		Prepare/Submit Final CIA Soil Investigation Rpt																																																																																																																																																																																															
02030	Agency Review/Approve Draft CIA GW Report	719*	6*	19MAR04A	15JAN07		Agency Review/Approve Draft CIA GW Report																																																																																																																																																																																															
22110	Prepare/Submit Drft CIA Soil/GW FS Screening Rpt	504*	6*	14APR05A	13APR07		Prepare/Submit Drft CIA Soil/GW FS Screening Rpt																																																																																																																																																																																															

Activity ID	Activity Description	Orig Dur	Rem Dur	Anticipated /Actual Start	Anticipated /Actual Finish	FY07												FY08												FY09												FY10												FY11												FY12											
						J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D
FA0510	Agency Review/Approve Draft Former A DD	55	55	26AUG08	13NOV08																																																																								
FA0530	Prepare/Submit Final Former A DD	20	20	14NOV08	12DEC08																																																																								
FA0540	EPA Issue Former A DD	15	15	15DEC08	06JAN09																																																																								
FA0550	Prepare/Submit Draft Former A LTM Plan	45	45	07JAN09	11MAR09																																																																								
FA0560	Agency Review/Approve Draft Former A LTM Plan	55	55	12MAR09	28MAY09																																																																								
FA0570	Prepare/Submit Final Former A LTM Plan	20	20	29MAY09	25JUN09																																																																								
FA0580	Prepare/Submit Drft Fm A Interim RA & Close-Out	60	60	30APR09	24JUL09																																																																								
FA0590	Agency Revw/Appr Dr Fm A Interim RA & Close-Out	55	55	27JUL09	13OCT09																																																																								
FA0600	Prep/Sub Final Fm A Interim RA & Close-Out Rpt	20	20	14OCT09	10NOV09																																																																								
FA0610	EPA Approve Former A Interim RA & Close-Out Rpt	15	15	12NOV09	03DEC09																																																																								
Former K Range																																																																													
Former K Range Soil & Groundwater																																																																													
01510	Agency Review/Approve Former K RI Report	328*	35*	04NOV05A	26FEB07																																																																								
K01572	Prepare/Submit Draft Final Former K RI Report	88	88	04JUN07*	05OCT07																																																																								
K01573	Agency Review/Approve Dr Final Former K RI Rpt	55	55	09OCT07	27DEC07																																																																								
K01574	Prepare/Submit Final Former K RI Report	20	20	28DEC07	25JAN08																																																																								
FK0500	Prepare/Submit Draft Former K DD	20	20	28JAN08	25FEB08																																																																								
FK0510	Agency Review/Approve Draft Former K DD	55	55	26FEB08	12MAY08																																																																								
FK0520	Fornal Public Comment Former K DD	30	30	11MAR08	09APR08																																																																								
FK0530	Prepare/Submit Final Former K DD	20	20	13MAY08	10JUN08																																																																								
FK0540	EPA Issue Former K DD	15	15	11JUN08	01JUL08																																																																								
FK0550	Prepare/Submit Draft Former K LTM Plan	45	45	02JUL08	04SEP08																																																																								
FK0560	Agency Review/Approve Draft Former K LTM Plan	55	55	08SEP08	24NOV08																																																																								
FK0570	Prepare/Submit Final Former K LTM Plan	20	20	25NOV08	23DEC08																																																																								
FK0580	Prepare/Submit Drft Fm K Interim RA & Close-Out	60	60	27OCT08	22JAN09																																																																								
FK0590	Agency Revw/Appr Dr Fm K Interim RA & Close-Out	55	55	23JAN09	10APR09																																																																								
FK0600	Prep/Sub Final Fm K Interim RA & Close-Out Rpt	20	20	13APR09	08MAY09																																																																								
FK0610	EPA Approve Former K Interim RA & Close-Out Rpt	15	15	11MAY09	01JUN09																																																																								
Phase II b																																																																													
Phase II (b) Soil & Groundwater																																																																													
01560	Agency Review/Approve Draft IIb Investig. Report	1,030*	64*	01APR03A	06APR07																																																																								

Activity ID	Activity Description	Orig Dur	Rem Dur	Anticipated /Actual Start	Anticipated /Actual Finish	FY07					FY08					FY09					FY10					FY11					FY12																									
						J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M
2B1140	Prepare/Submit Final Phase IIb Investigation Rpt	20	20	09APR07	04MAY07																																																			
2B0200	Prepare/Submit Draft Phase IIb NFA DD	45	45	07MAY07	10JUL07																																																			
2B0201	Agency Review/Approve Draft Phase IIb NFA DD	55	55	11JUL07	26SEP07																																																			
2B0202	Formal Public Comment Phase IIb NFA DD	30	30	25JUL07	23AUG07																																																			
2B0203	Prepare/Submit Final Phase IIb NFA DD	20	20	27SEP07	25OCT07																																																			
2B0204	EPA Issue Phase IIb NFA DD	15	15	26OCT07	16NOV07																																																			
Small Arms Range																																																								
Small Arms Range Soil & Groundwater																																																								
016900	Prepare/Submit Draft SAR E/T Investigation Rpt	56*	0*	10OCT06A	14DEC06A																																																			
016901	Agency Review/Appr Draft SAR E/T Investig Rpt	20	14	15DEC06A	25JAN07																																																			
016902	Prep/Sub Draft SAR E/T Suppl Investigation Rpt	39	39	10JAN07A	02MAR07																																																			
016903	Agency Rev/Appr Draft SAR E/T Suppl Investig Rpt	45	45	10JAN07A	12MAR07																																																			
016990	Prepare/Submit Final SAR E/T Investigation Rpt	20	20	13MAR07	09APR07																																																			
01723	Prepare/Submit Draft SAR Soil/GW Investigatn WP	32*	32*	22JAN07*	07MAR07																																																			
01725	Agency Review/Approve Draft SAR Soil/GW Invest WP	55*	55*	08MAR07	23MAY07																																																			
01727	Prepare/Submit Final SAR Soil/GW Investigatn WP	20	20	24MAY07	21JUN07																																																			
01597	Conduct SAR Soil/GW Investigation	60	60	29MAR07	21JUN07																																																			
01599	Agency Monitor SAR Soil/GW Investigation	60	60	29MAR07	21JUN07																																																			
01800	Prepare/Submit Draft SAR Soil RRA Plan	49	49	26APR07	05JUL07																																																			
01804	Agency Review/Approve Draft SAR Soil RRA Plan	55	55	06JUL07	21SEP07																																																			
SAR01805	Informal Public Comment SAR Soil RRA Plan	15	15	27JUL07	10AUG07																																																			
01898	Prepare/Submit Final SAR Soil RRA Plan	20	20	24SEP07	22OCT07																																																			
01900	Conduct SAR Soil RRA	90	90	24SEP07	01FEB08																																																			
01812	Prepare/Submit Draft SAR Soil RRA COWR	40	40	04FEB08	31MAR08																																																			
01816	Agency Review/Approve Draft SAR Soil RRA COWR	55	55	01APR08	17JUN08																																																			
01899	Prepare/Submit Final SAR Soil RRA COWR	10	10	18JUN08	01JUL08																																																			
SAR1900	Prepare/Submit Draft SAR Soil/GW Investigat Rpt	135	135	22JUN07	07JAN08																																																			
SAR1910	Agency Review/Approve Draft SAR Soil/GW Investig	55*	55*	08JAN08	25MAR08																																																			
SAR1920	Prepare Final SAR Soil/GW Investigation Report	20	20	26MAR08	22APR08																																																			
SAR2000	Prepare/Submit Draft SAR DD	15	15	23APR08	13MAY08																																																			

Activity ID	Activity Description	Orig Dur	Rem Dur	Anticipated /Actual Start	Anticipated /Actual Finish	FY07												FY08												FY09												FY10												FY11												FY12																							
						J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S			
WA0006	Agency Review/Approve Draft WASA Soil/GW Investg	55	55	08MAY08	25JUL08																																																																																				
WA0008	Prepare Final WASA Soil/GW Investigation Report	20	20	28JUL08	22AUG08																																																																																				
WA0000	Prepare/Submit Draft WASA Soil RRA Plan	60	60	25AUG08	19NOV08																																																																																				
WA0010	Agency Review/Approve Draft WASA Soil RRA Plan	55	55	21NOV08	09FEB09																																																																																				
WA0020	Informal Public Comment WASA Soil RRA Plan	15	15	12DEC08	27DEC08																																																																																				
WA0030	Prepare/Submit Final WASA Soil RRA Plan	20	20	10FEB09	10MAR09																																																																																				
WA0040	Conduct WASA Soil RRA	30	30	11MAR09	21APR09																																																																																				
WA0050	Prepare/Submit Draft WASA Soil COWR	60	60	22APR09	16JUL09																																																																																				
WA0060	Agency Review/Approve Draft WASA Soil COWR	55	55	17JUL09	02OCT09																																																																																				
WA0070	Prepare/Submit WASA Final Soil COWR	20	20	05OCT09	02NOV09																																																																																				
WA0080	Prepare/Submit Draft WASA NFA DD	45	45	03NOV09	08JAN10																																																																																				
WA0090	Agency Review/Approve Draft WASA NFA DD	55	55	11JAN10	29MAR10																																																																																				
WA0100	Formal Public Comment WASA NFA DD	22	22	25JAN10	24FEB10																																																																																				
WA0110	Prepare/Submit Final WASA NFA DD	20	20	30MAR10	26APR10																																																																																				
WA0120	EPA Issue WASA NFA DD	15	15	27APR10	17MAY10																																																																																				
