
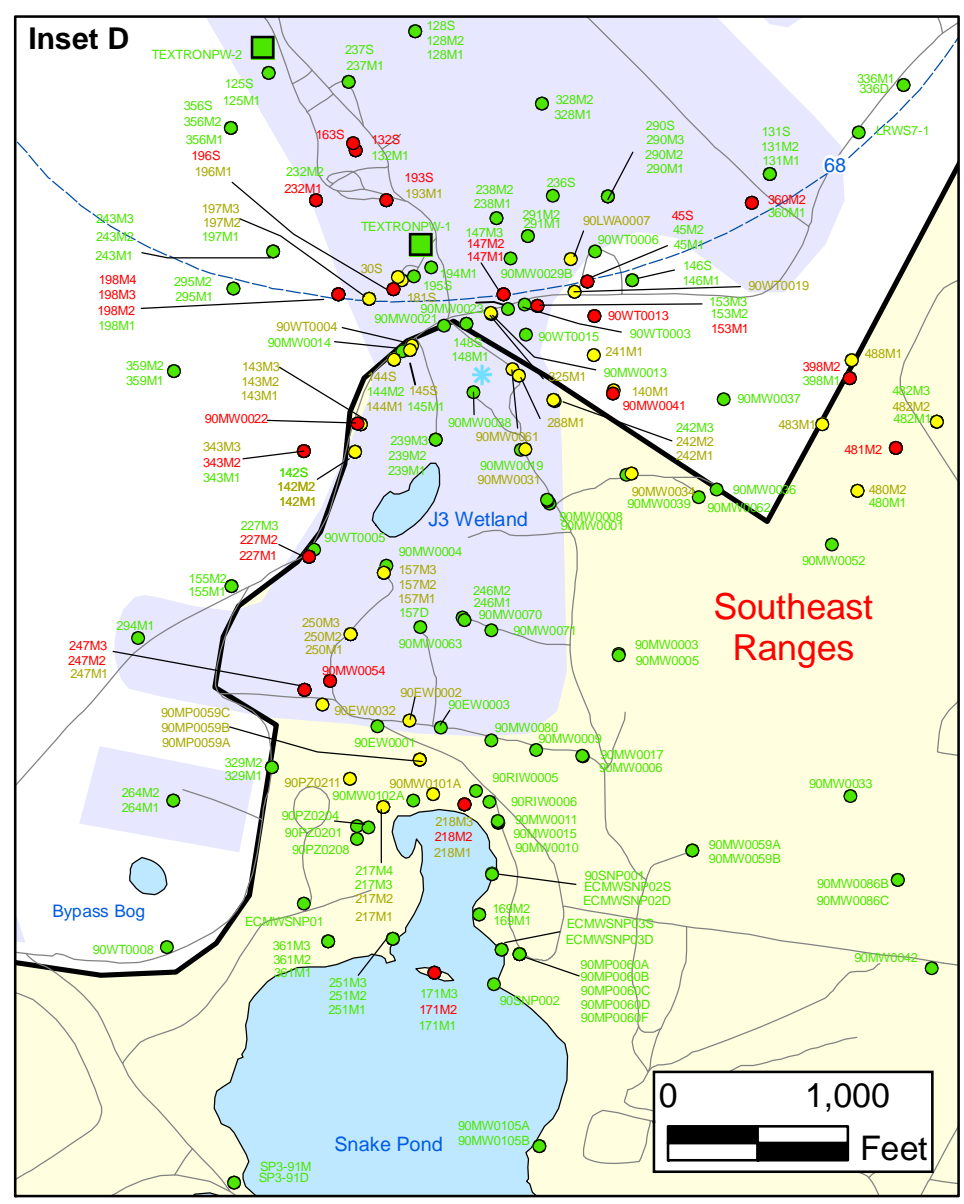
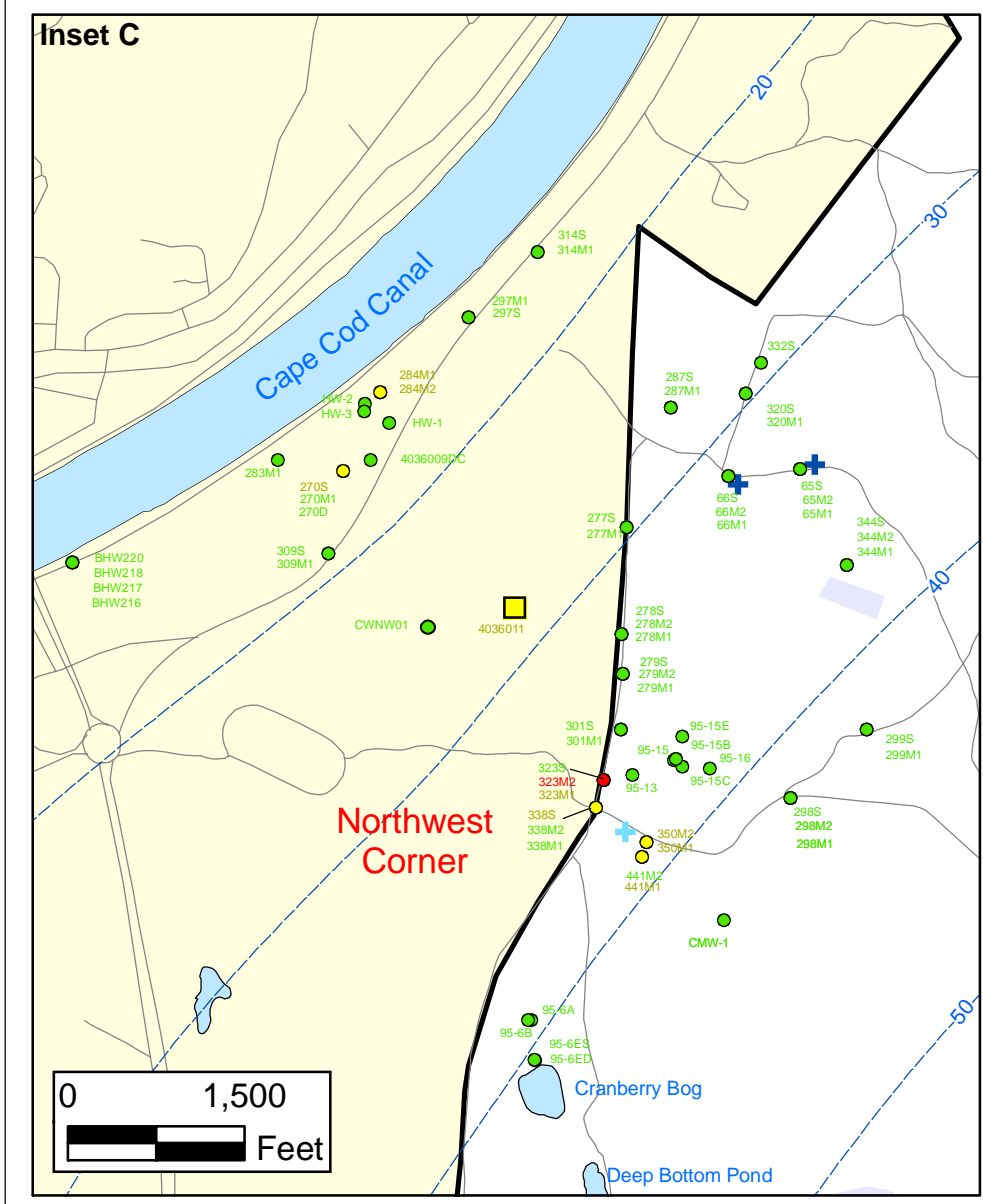


Explosives in Groundwater Compared to Maximum Contaminant Level/Health Advisories
Validated Data as of 11/28/07

FIGURE 1

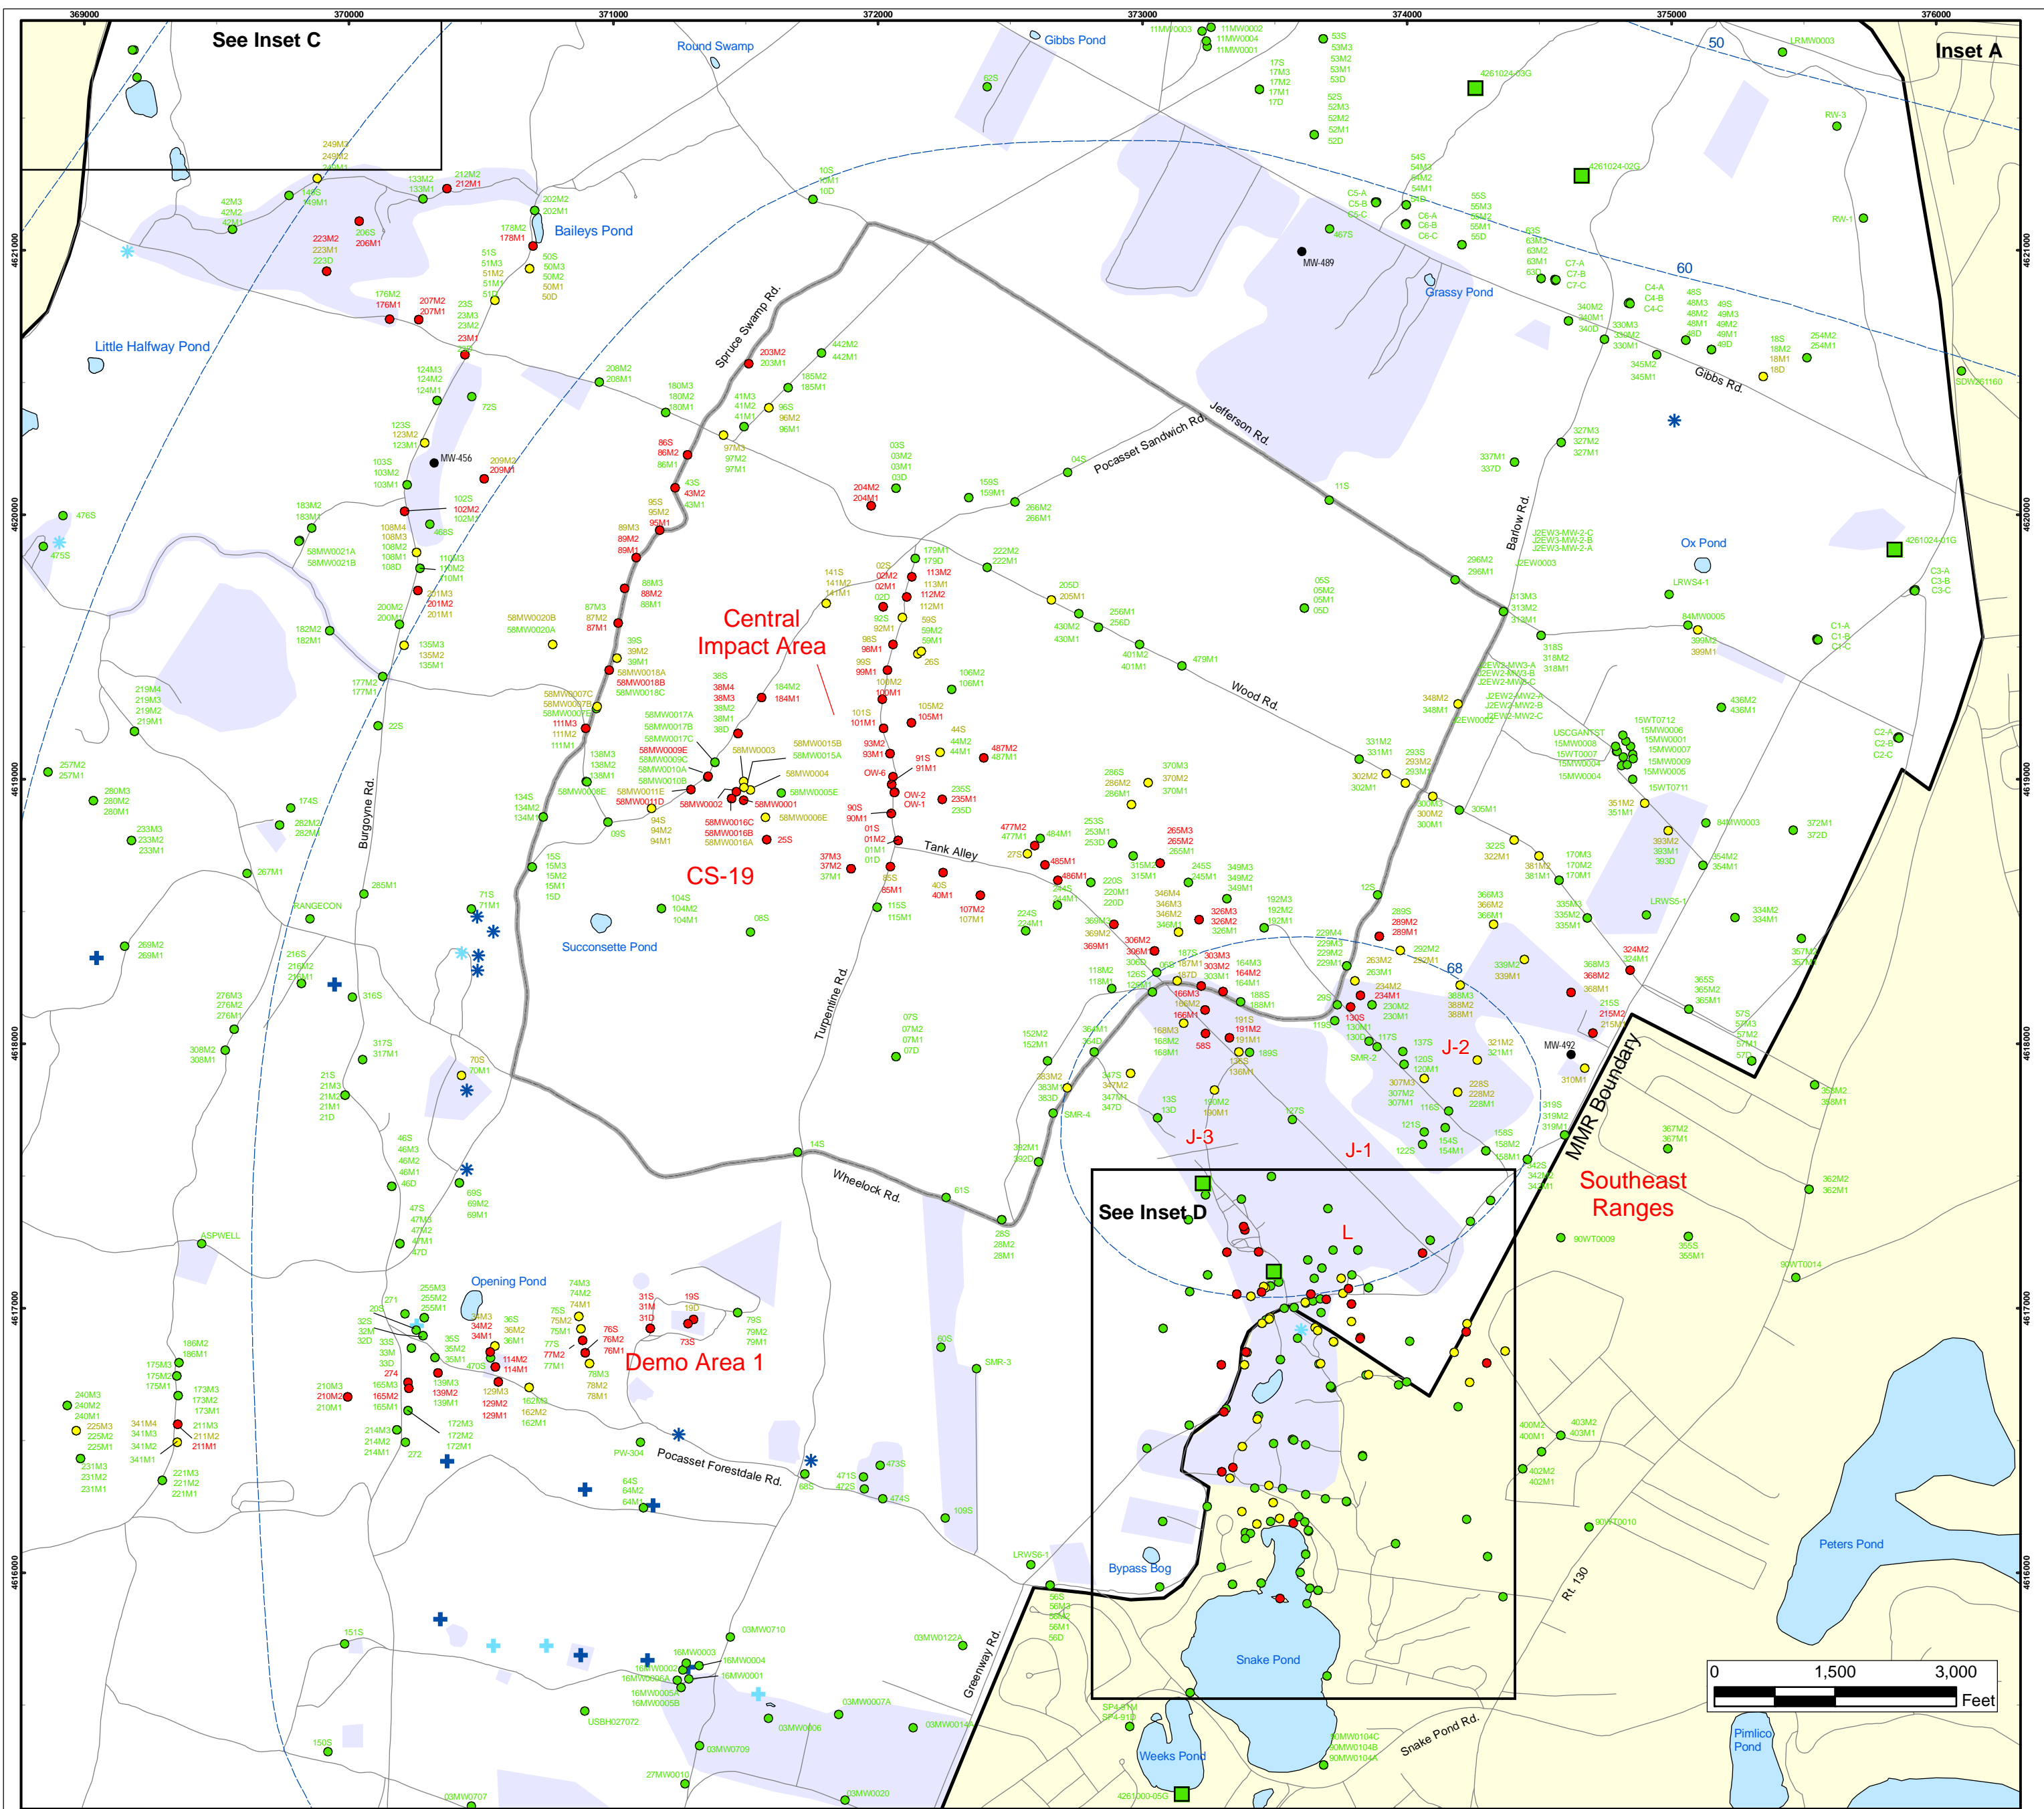

Explosives in Groundwater Compared to Maximum Contaminant Level/Health Advisories

Validated Data as of 11/28/07

- Validated Detection Greater than or Equal to Maximum Contaminant Level/Health Advisories
- Validated Detection Less than Maximum Contaminant Level/Health Advisories
- Validated Non-Detect
- Data Pending
- Proposed Monitoring Well
- Military Range Areas
- + Current Gun Position
- * Current Mortar Position
- + Old Gun Position
- * Old Mortar Position
- Validated Non-Detect Water Supply Well
- Validated Detection Less than Maximum Contaminant Level/Health Advisories Water Supply Well
- Water Table Contour (Feet NGVD), AMEC, September 2003

Note: Map dot colors are representative of the highest historical concentration at each well and not the current concentration level. Historical data presented on this figure range from November 1996 through 2007.


**Impact Area
Groundwater Study Program**

AMEC Earth & Environmental, Inc.
Westford, Massachusetts

**FIGURE
1**

Inset Map

Sources & Notes
Base map data from US Geological Survey
7 1/2 minute Topographic Maps
Source: Office of Geographic and
Environmental Information (MassGIS)
Commonwealth of Massachusetts
Executive Office of Environmental Affairs

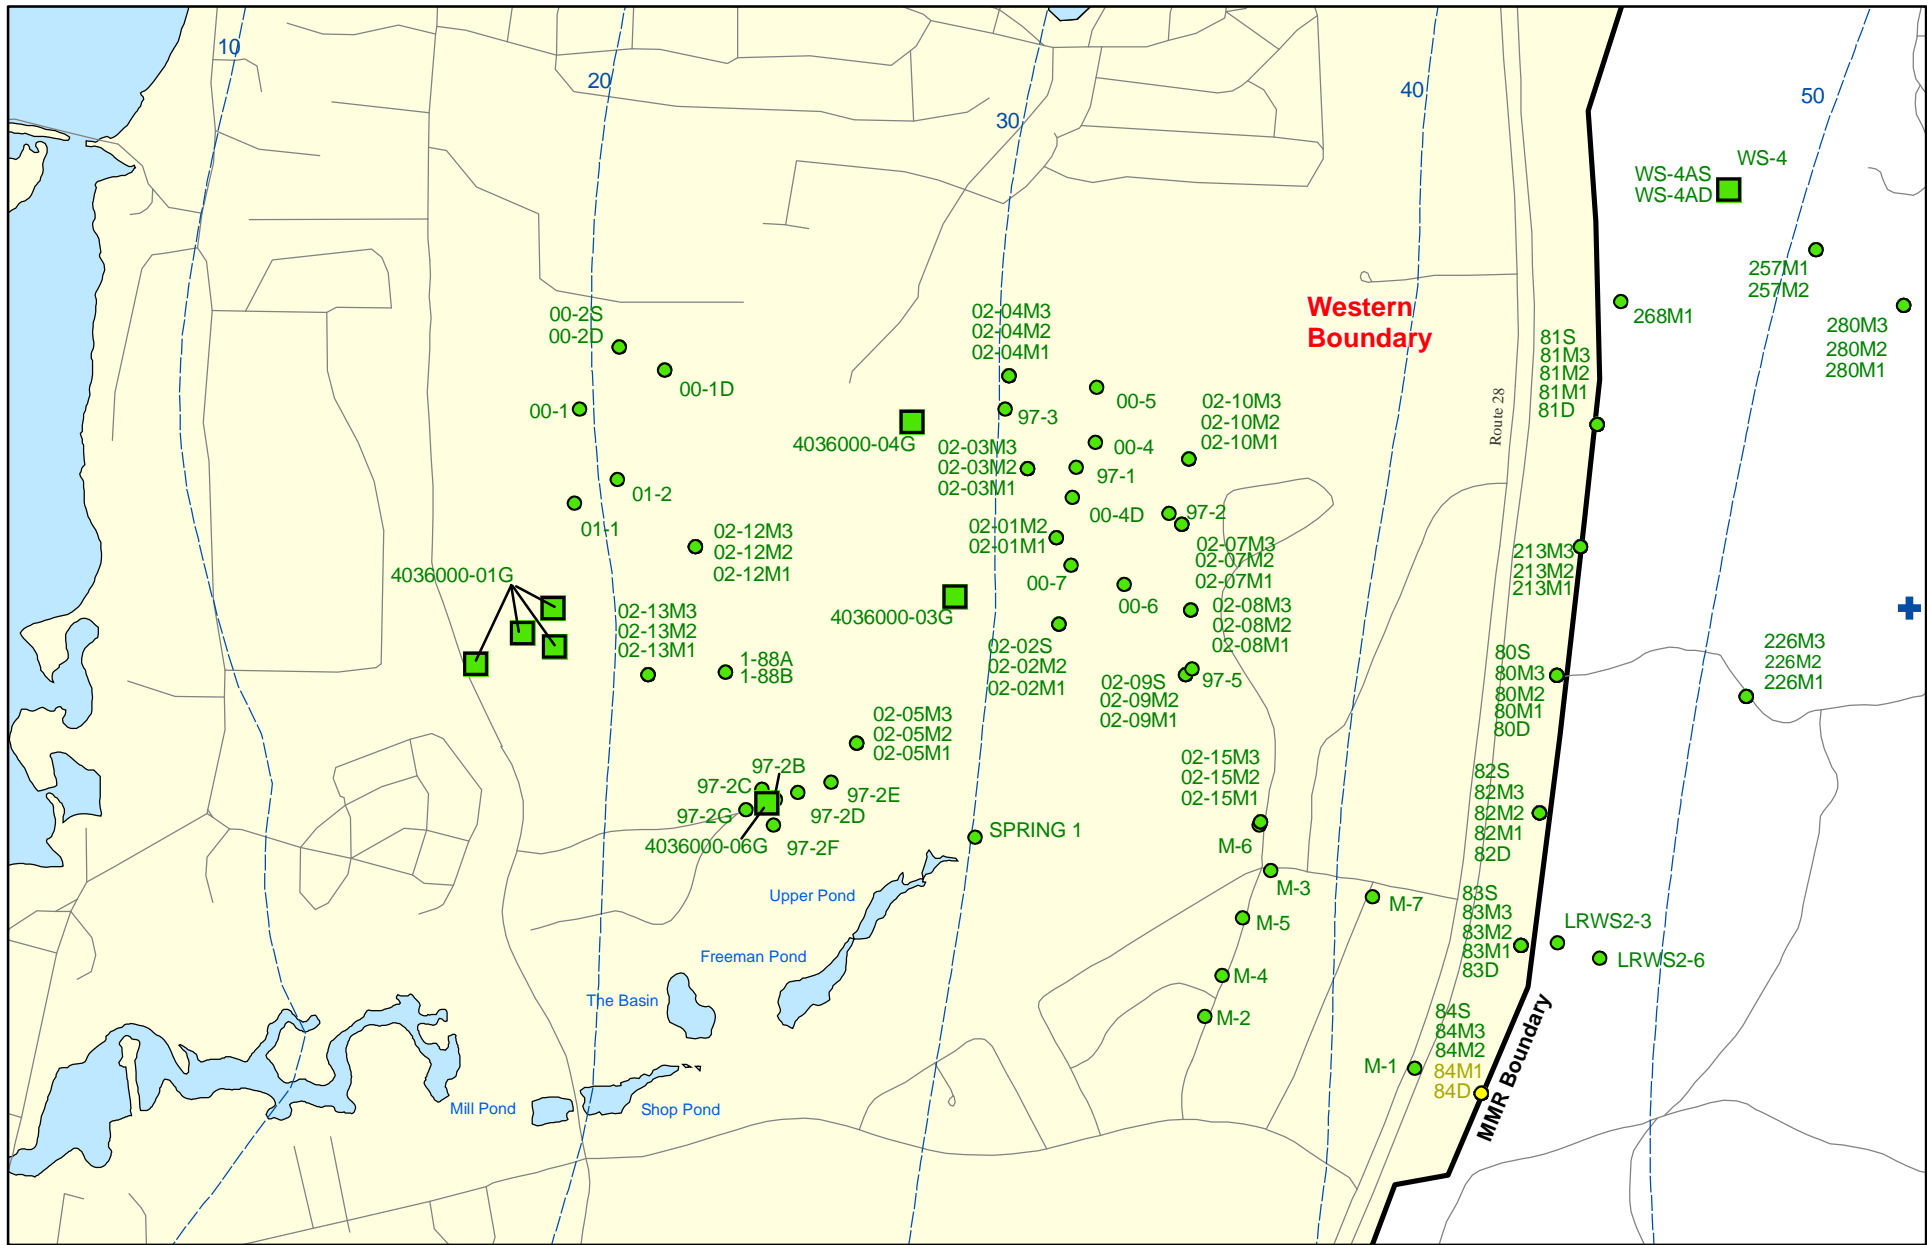


Sources & Notes:
 Base map data from US Geological Survey
 7 1/2 minute Topographic maps
 Source: Office of Geographic and
 Environmental Information (MassGIS)
 Commonwealth of Massachusetts
 Executive Office of Environmental Affairs

AMEC Earth & Environmental, Inc.
 Westford, Massachusetts

- Validated Detection Less than Maximum Contaminant Level/Health Advisories
- Validated Non-Detect
- + Current Gun Position
- Validated Non-Detect Water Supply Well
- Proposed Water Supply Well
- Water Table Contour (Feet NGVD)
AMEC, September 2003


Note: Map dot colors are representative of the highest historical concentration at each well and not the current concentration level. Historical data presented on this figure range from November 1996 through 2007.

Explosives in Groundwater Compared to Maximum Contaminant Level/Health Advisories Validated Data as of 11/28/07



Inset Map B

FIGURE
1

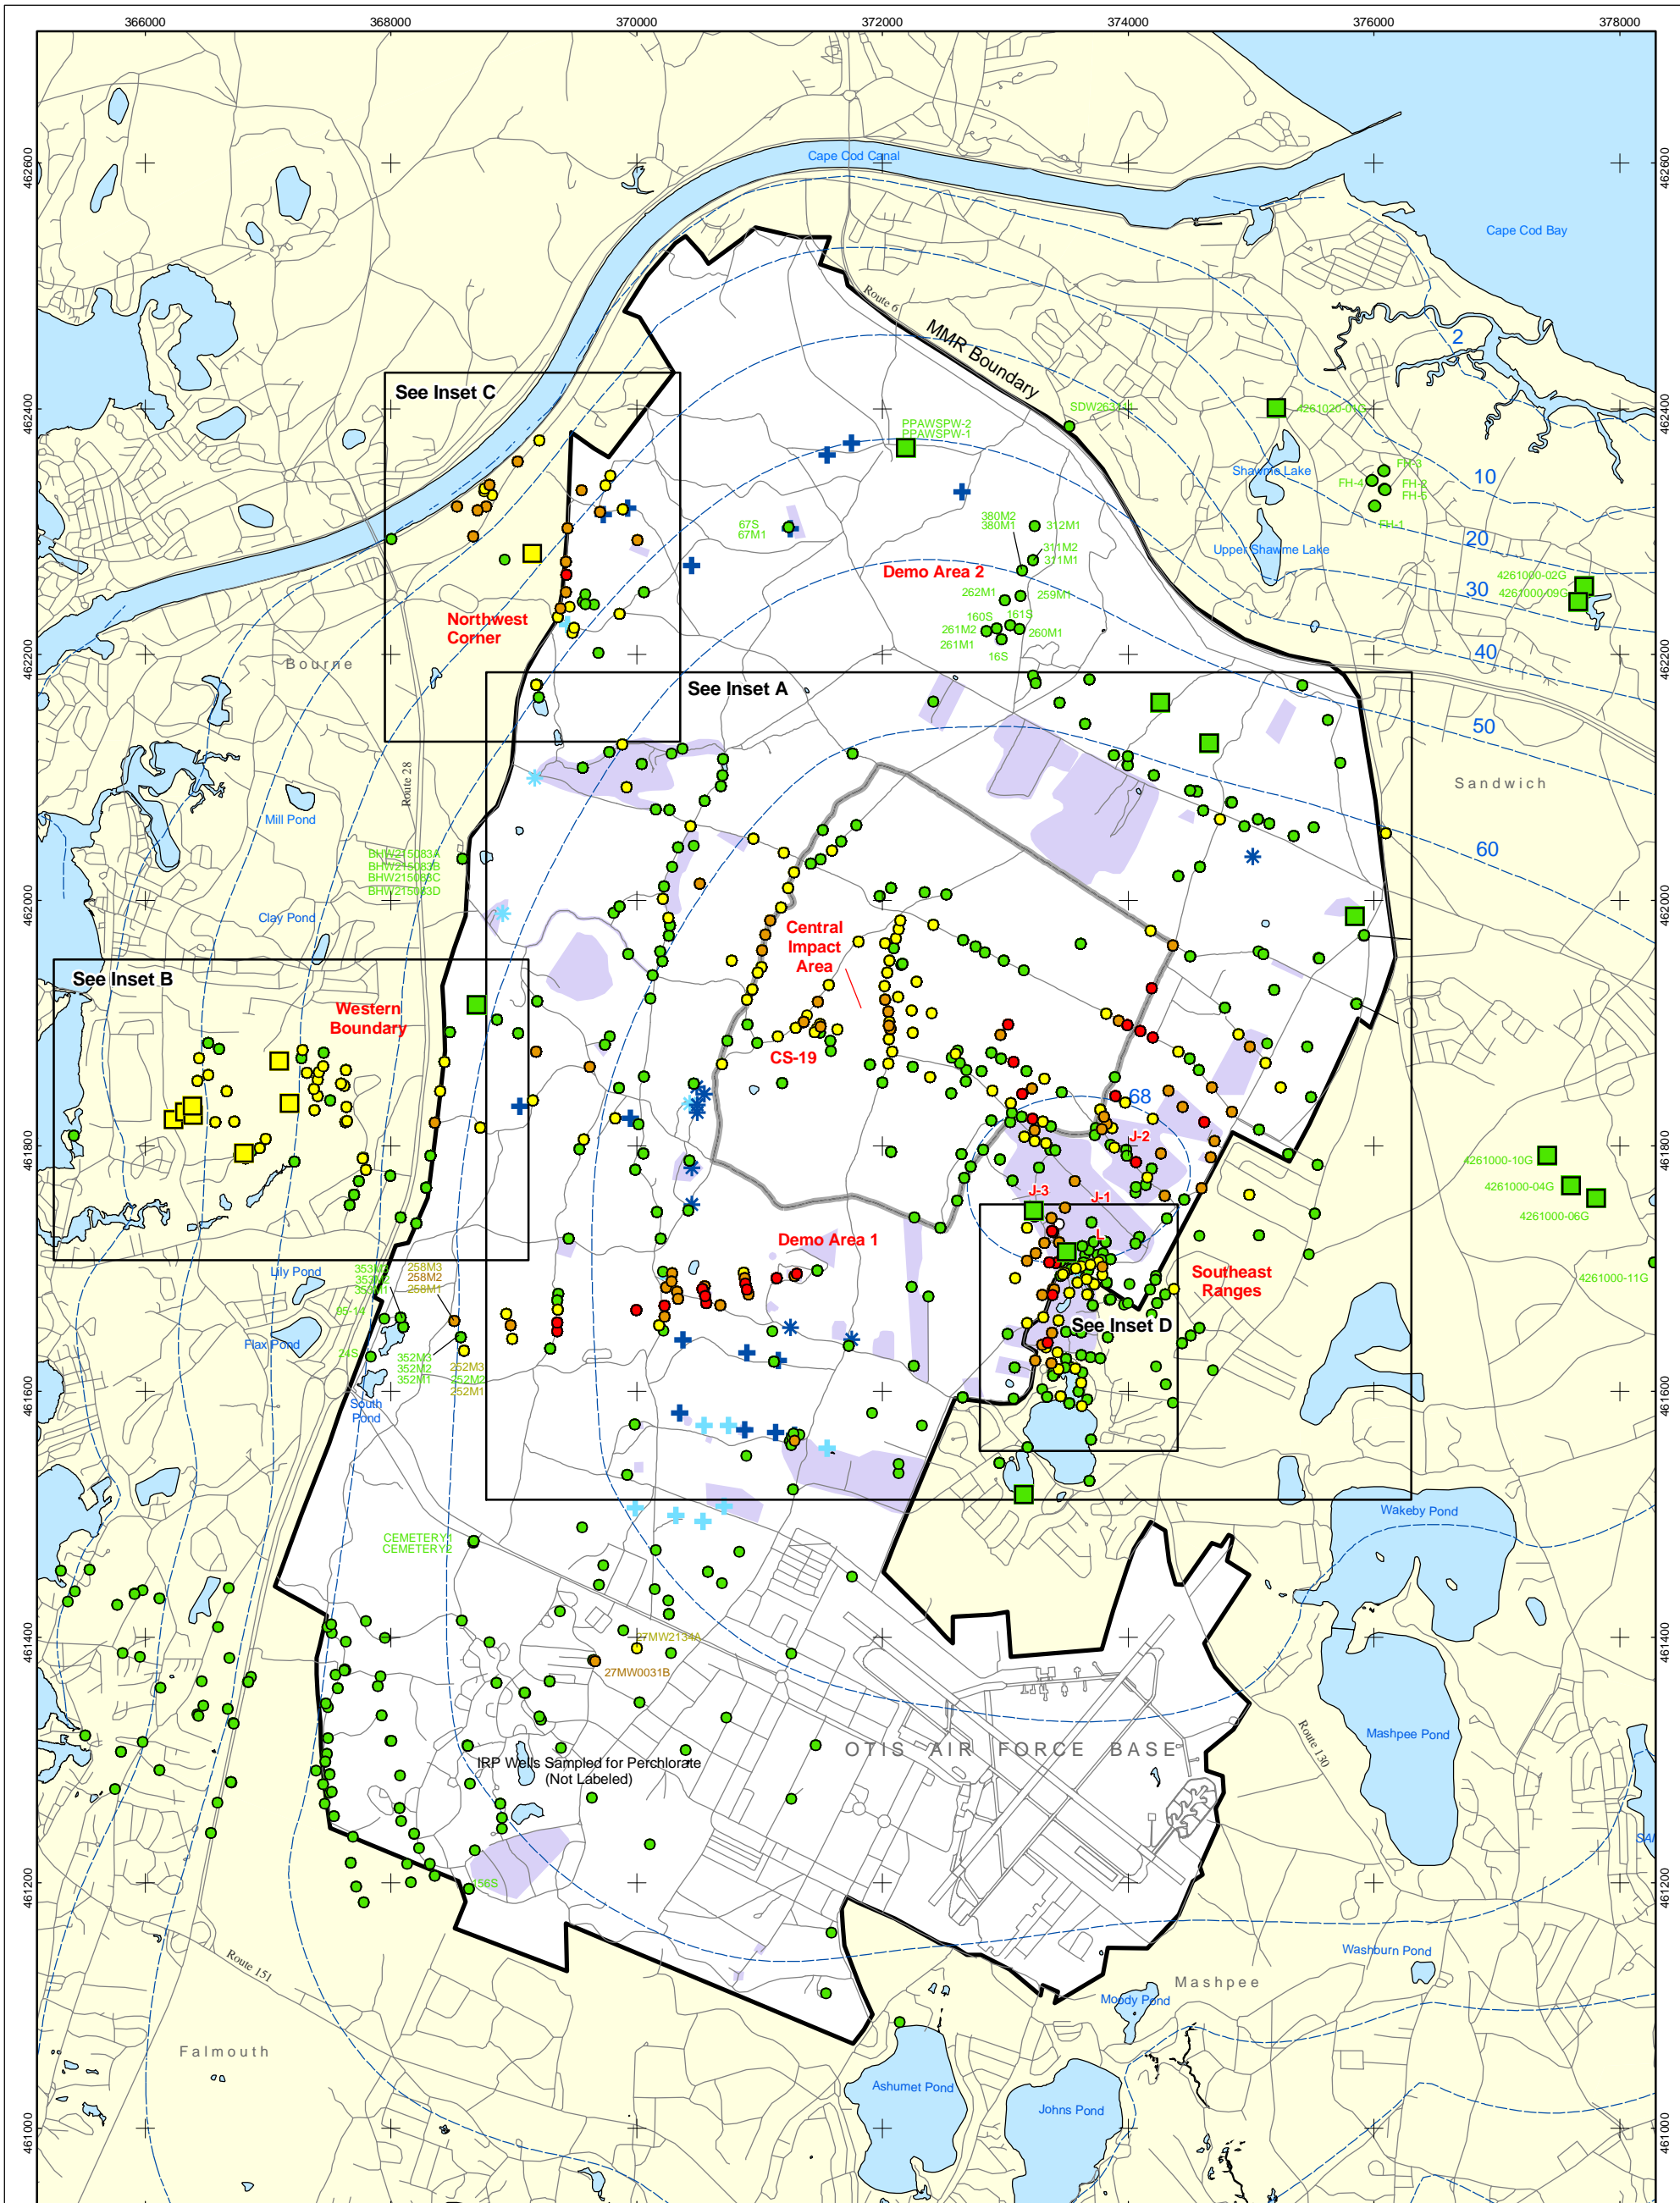


- Validated Detection Greater than or Equal to 24 ppb
- Validated Detection Greater than or Equal to 2 and Less than 24 ppb
- Validated Detection Greater than Non-Detect and Less than 2 ppb
- Validated Non-Detect




- Data Pending
- Proposed Monitoring Well
- Current Gun Position
- Current Mortar Position
- Old Gun Position
- Old Mortar Position

- Validated Non-Detect Water Supply Well
- Validated Detection Less than 2 ppb Water Supply Well
- Proposed Water Supply Well
- Water Table Contour (Feet NGVD) AMEC, September 2003
- Military Range Areas

Note: Map dot colors are representative of the highest historical concentration at each well and not the current concentration level. Historical data presented on this figure range from November 1996 through 2007.


 0 2,000 4,000
 Feet

Sources & Notes
 Base map data from US Geological Survey 7 1/2 minute Topographic Maps.
 Source: Office of Geographic and Environmental Information (MassGIS) Commonwealth of Massachusetts Executive Office of Environmental Affairs

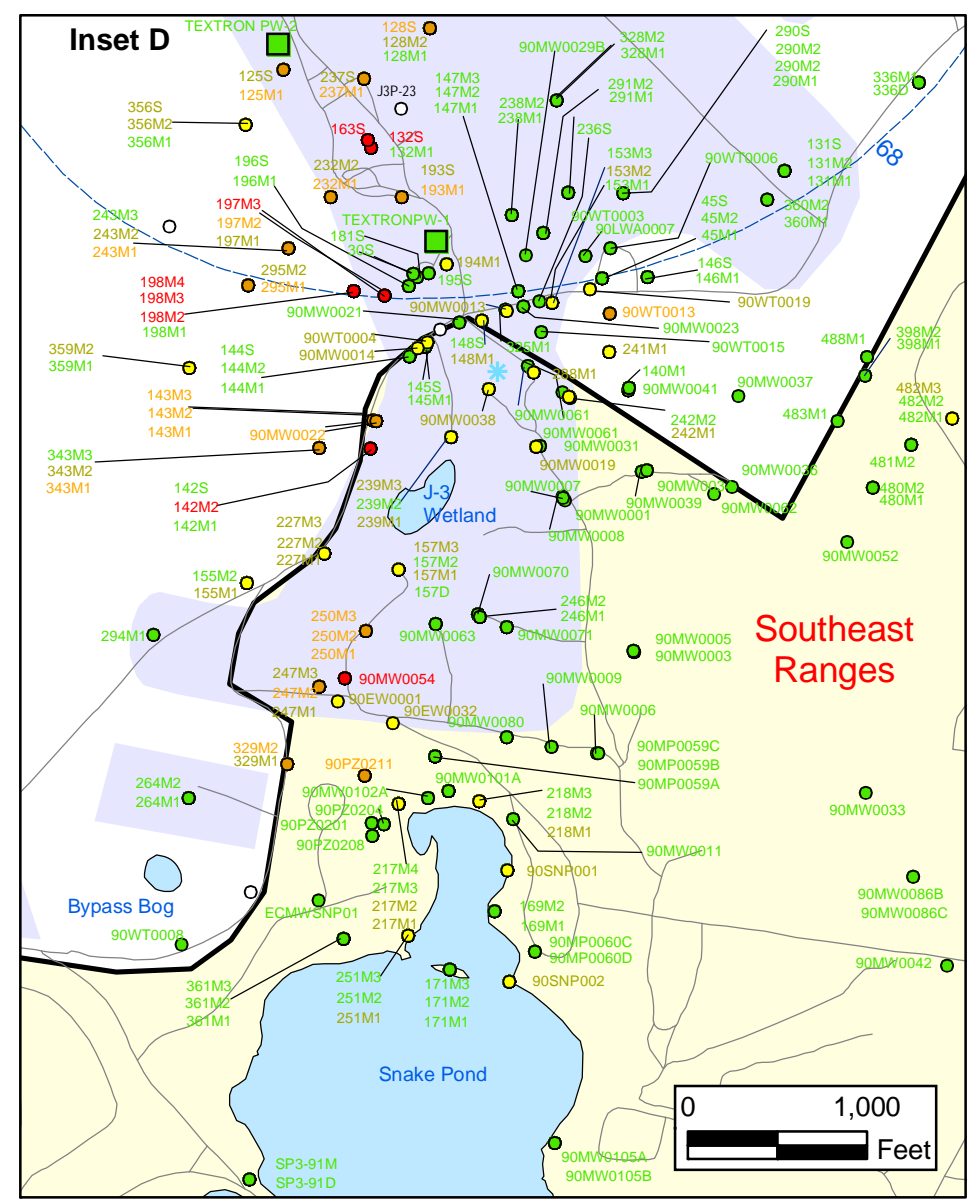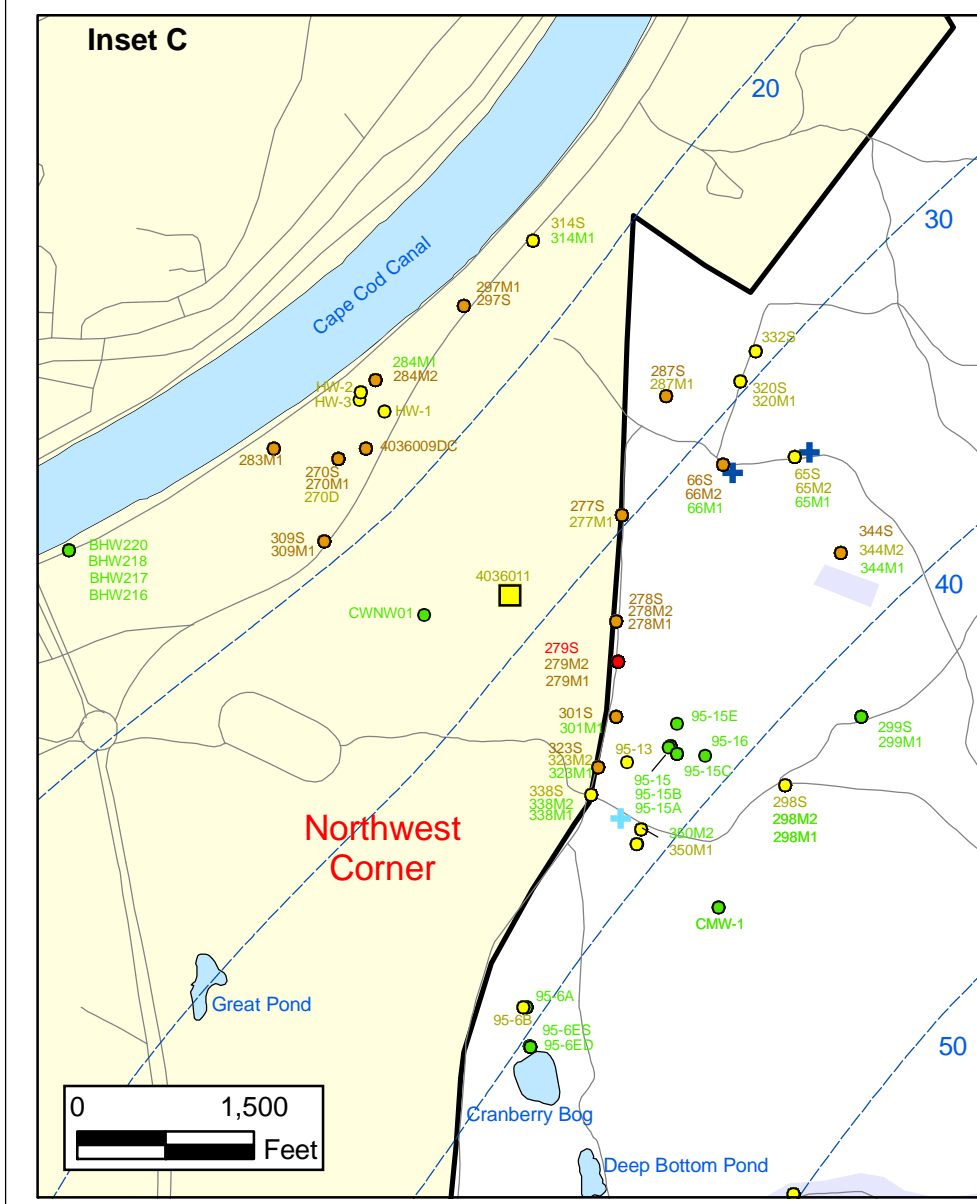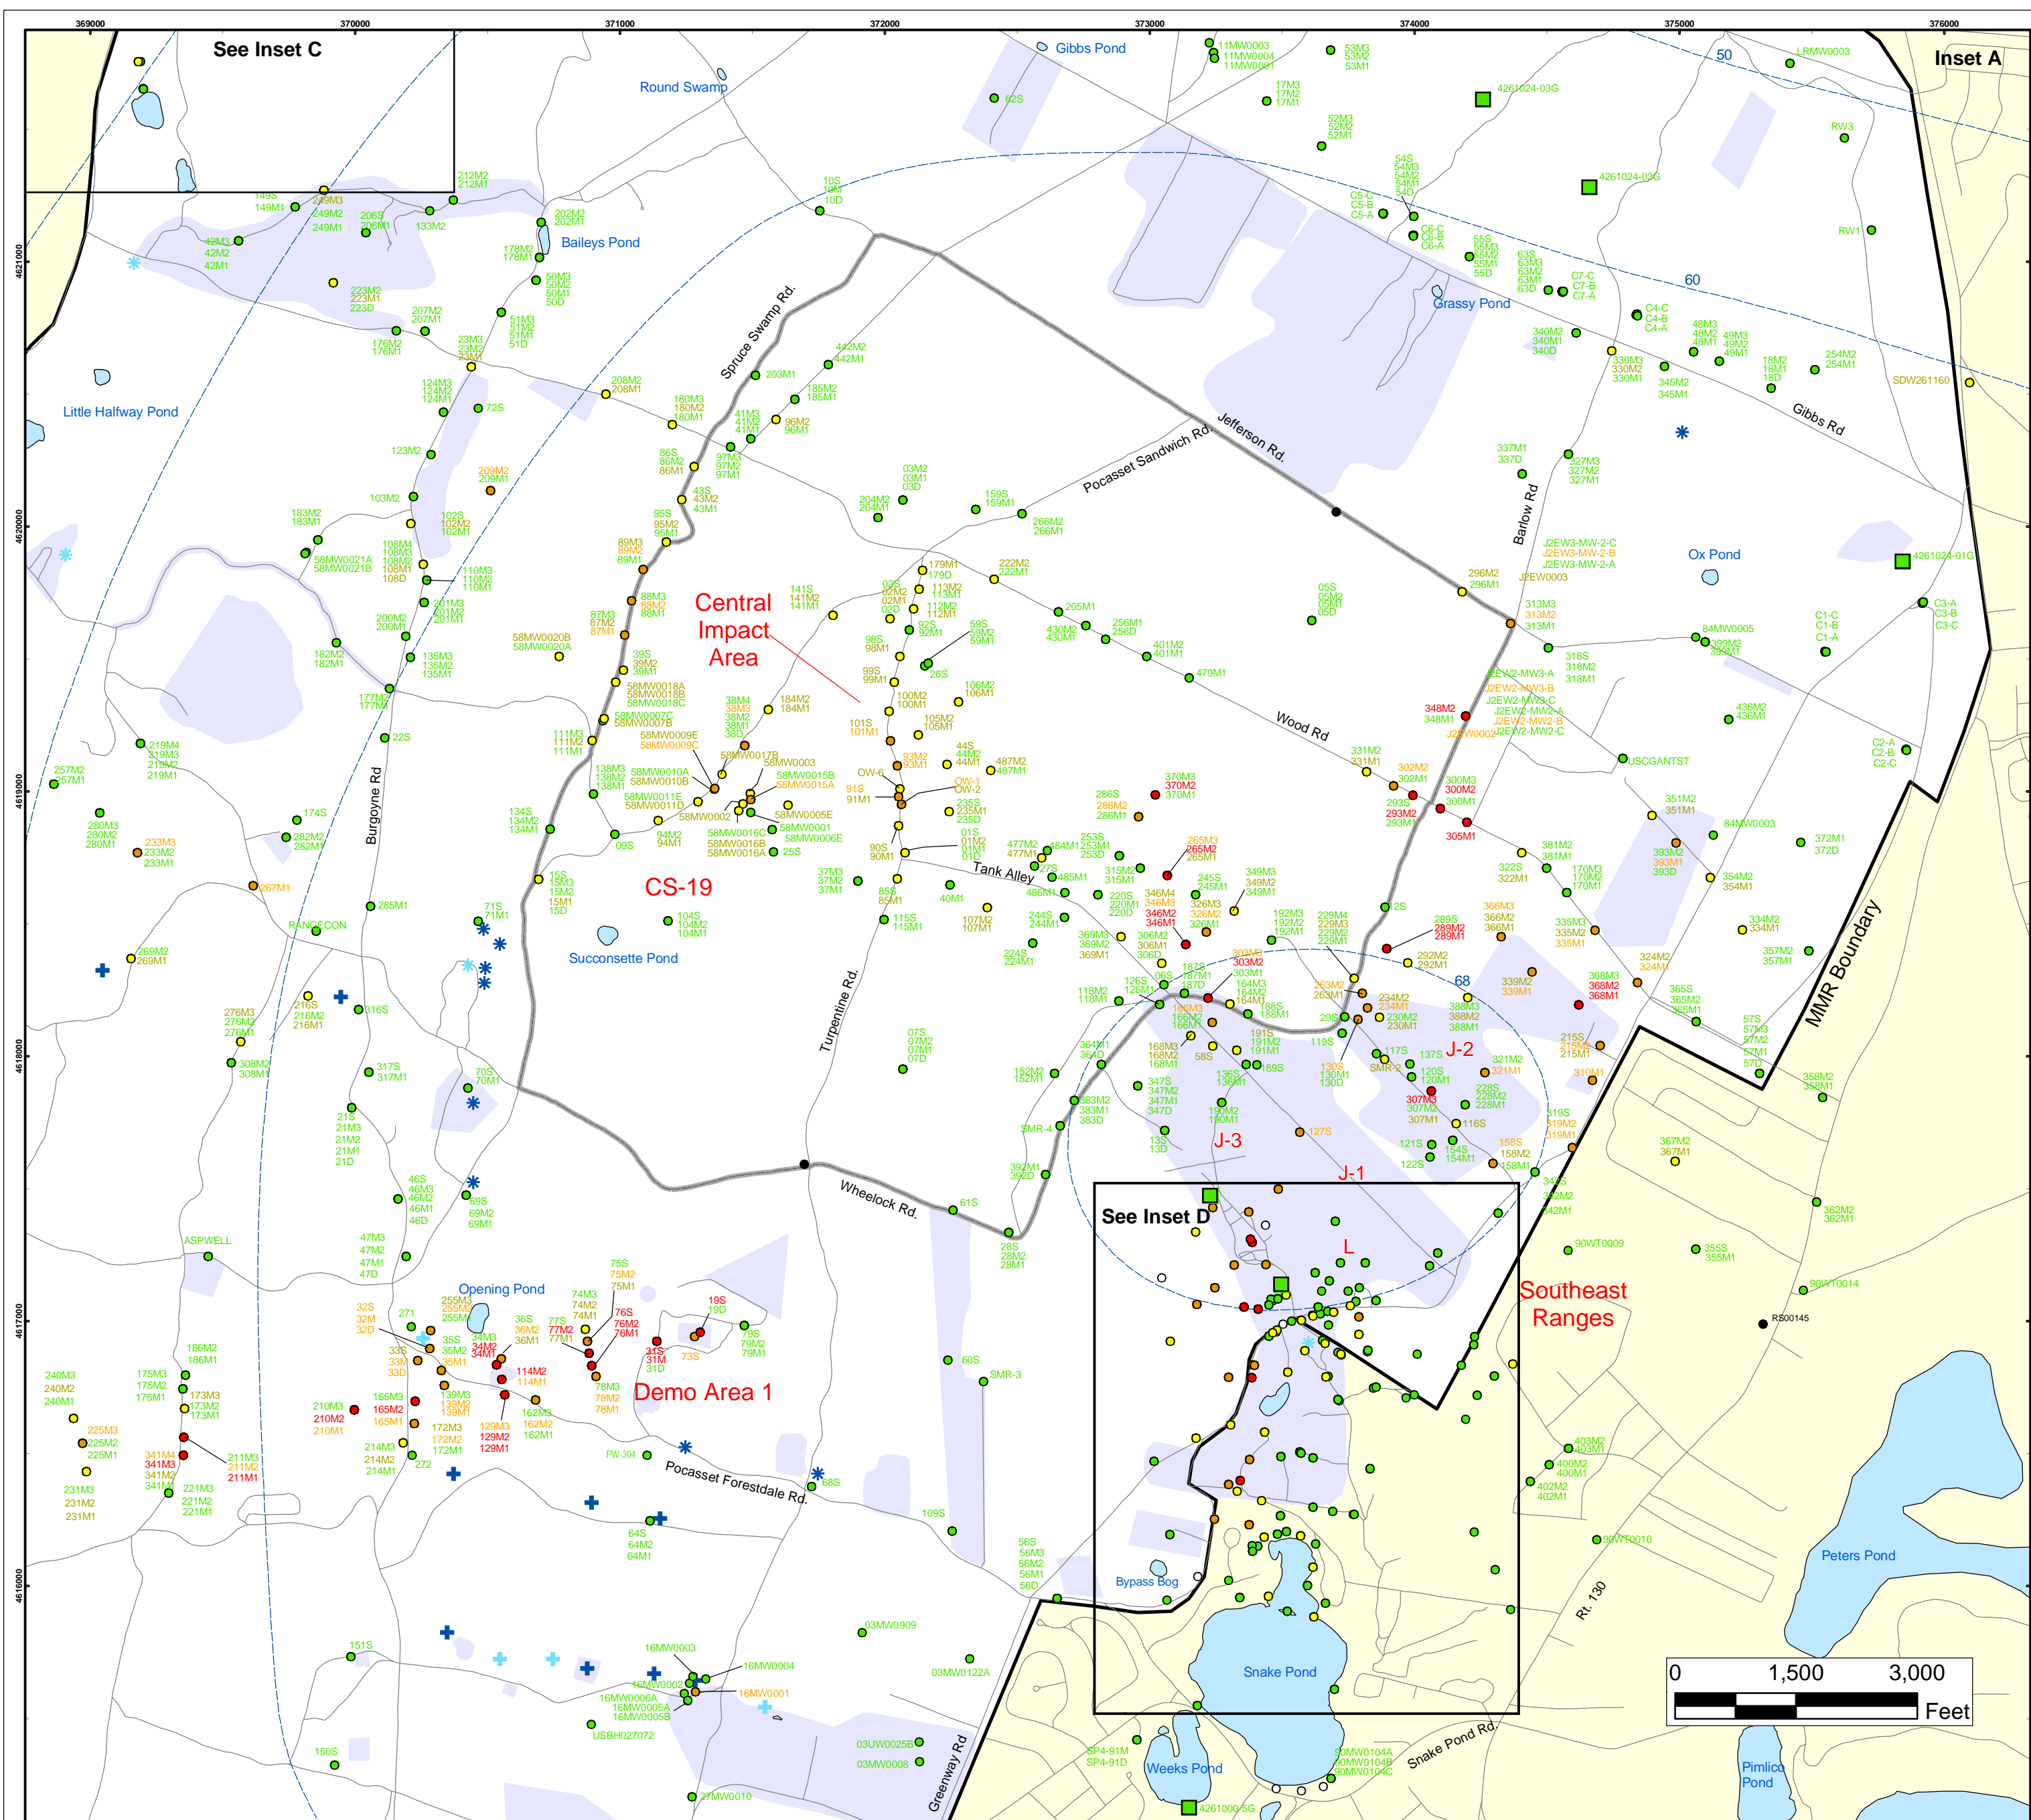

Perchlorate in Groundwater Compared to a 2 PPB Concentration Validated Data as of 11/28/07

- Validated Detection Greater than or Equal to 24 ppb
- Validated Detection Greater than or Equal to 2 and Less than 24 ppb
- Validated Detection Less than 2 ppb
- Validated Non-Detect
- Data Pending
- Proposed Monitoring Well
- Military Range Areas
- + Current Gun Position
- * Current Mortar Position
- + Old Gun Position
- * Old Mortar Position
- Validated Non-Detect Water Supply Well
- Validated Detection Less Than 2 ppb Water Supply Well
- Water Table Contour (Feet NGVD), AMEC, September 2003

Note: Map dot colors are representative of the highest historical concentration at each well and not the current concentration level. Historical data presented on this figure range from November 1996 through 2007.


Impact Area
Groundwater Study Program

Sources & Notes
Base map data from US Geological Survey
7 1/2 minute Topographic Maps
Source: Office of Geographic and
Environmental Information (MassGIS)
Commonwealth of Massachusetts
Executive Office of Environmental Affairs

AMEC Earth & Environmental, Inc.
Westford, Massachusetts

FIGURE
8

Inset Map

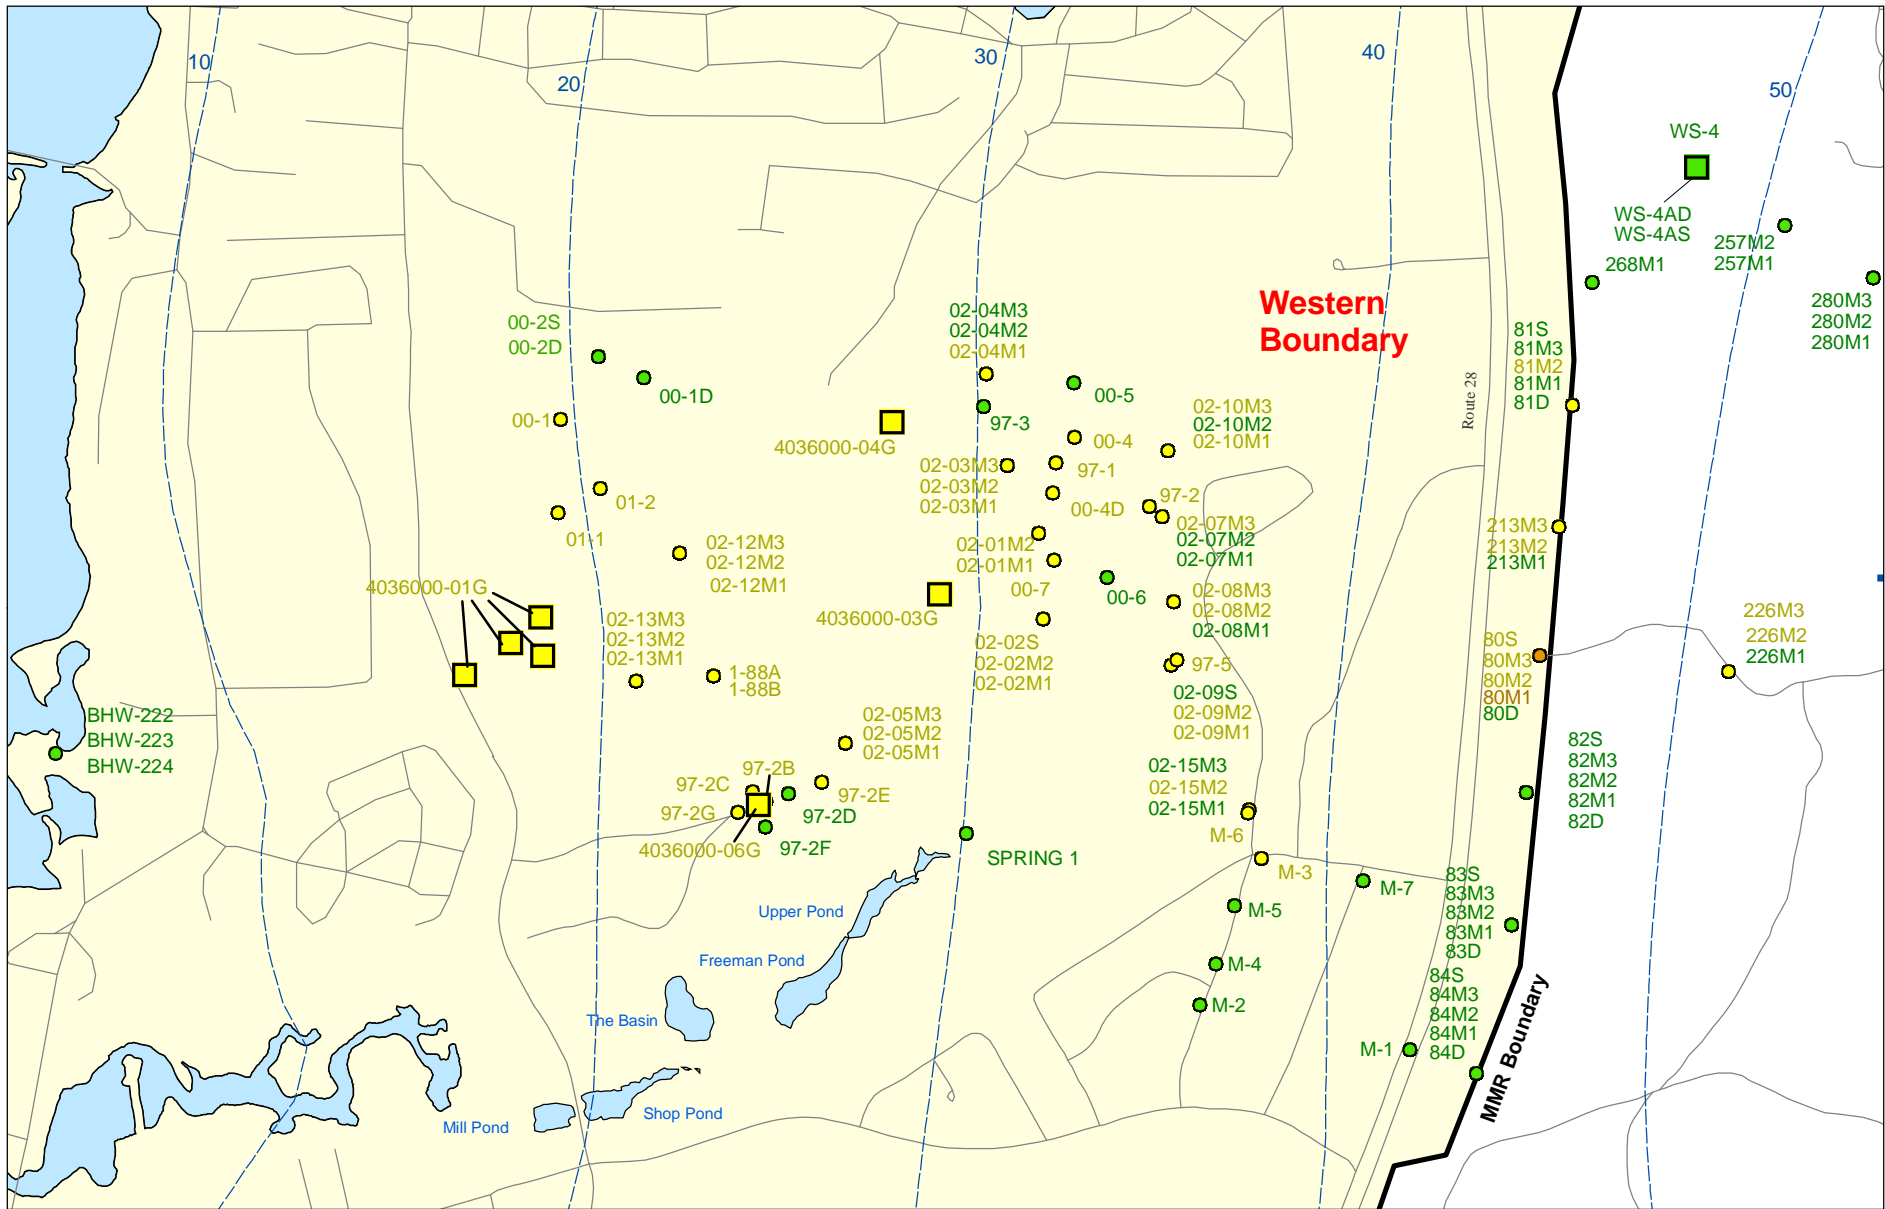


Sources & Notes:
 Base map data from US Geological Survey
 7 1/2 minute Topographic maps.
 Source: Office of Geographic and
 Environmental Information (MassGIS)
 Commonwealth of Massachusetts
 Executive Office of Environmental Affairs

- Validated Detection Greater than or Equal to 2 and Less than 24 ppb
- Validated Detection Greater than Non-Detect and Less than 2 ppb
- Validated Non-Detect

Note: Map dot colors are representative of the highest historical concentration at each well and not the current concentration level. Historical data presented on this figure range from November 1996 through 2007.

- Validated Detection Less than 2 ppb Water Supply Well
- Validated Non-Detect Water Supply Well
- + Current Gun Position
- Water Table Contour (Feet NGVD)
AMEC, September 2003

Perchlorate in Groundwater Compared to a 2 ppb Concentration Validated Data as of 11/28/07



AMEC Earth & Environmental, Inc.
Westford, Massachusetts

Inset Map B 8

Activity ID	Activity Description	Orig Dur	Rem Dur	Anticipated /Actual Start	Anticipated /Actual Finish	FY07				FY08				FY09				FY10				FY11				FY12																					
						J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J
Demo 1																																															
Demolition Area 1 Soil																																															
00145	Agency Review/Approve Draft Demo 1 RRA Soil COWR	313*	52*	22DEC05A	21MAR07	Agency Review/Approve Draft Demo 1 RRA Soil COWR preparing RCL																																									
DM0920	Prepare/Submit Final Demo 1 RRA Soil COWR	20	20	22MAR07	18APR07	Prepare/Submit Final Demo 1 RRA Soil COWR																																									
DL0000	Prepare/Submit Draft Demo 1 Soil NFA DD	45	45	19APR07	21JUN07	Prepare/Submit Draft Demo 1 Soil NFA DD																																									
DL0080	Agency Review/Approve Draft Demo 1 Soil NFA DD	55*	55*	22JUN07	10SEP07	Agency Review/Approve Draft Demo 1 Soil NFA DD																																									
DL0085	Formal Public Comment Demo 1 Soil NFA DD	30	30	09JUL07	07AUG07	Formal Public Comment Demo 1 Soil NFA DD																																									
DL0100	Prepare/Submit Final Demo 1 Soil NFA DD	20	20	11SEP07	09OCT07	Prepare/Submit Final Demo 1 Soil NFA DD																																									
DL0110	EPA Issue Demo 1 Soil NFA DD	15	15	10OCT07	30OCT07	EPA Issue Demo 1 Soil NFA DD																																									
Demolition Area 1 Groundwater																																															
31575	Construct/Startup Demo 1 GW Treatment System	211*	102*	01AUG06A	31MAY07	Construct/Startup Demo 1 GW Treatment System																																									
CL0010	Prepare/Submit Draft Demo 1 SPM Plan	60	26	02JAN07A	12FEB07	Prepare/Submit Draft Demo 1 SPM Plan																																									
CL0100	Agency Review/Approve Draft Demo 1 SPM Plan	55*	55*	13FEB07	01MAY07	Agency Review/Approve Draft Demo 1 SPM Plan																																									
CL0130	Prepare/Submit Final Demo 1 SPM Plan	20	20	02MAY07	30MAY07	Prepare/Submit Final Demo 1 SPM Plan																																									
CL0140	Prepare/Submit Dr Demo 1 GW Int RA & Close-Out Rt	60	60	05APR07	28JUN07	Prepare/Submit Dr Demo 1 GW Int RA & Close-Out Rt																																									
CL0220	Agency Revw/Approv Dr Demo 1 GW Int RA & Close-Out	55*	55*	29JUN07	17SEP07	Agency Revw/Approv Dr Demo 1 GW Int RA & Close-Out																																									
CL0240	Prep/Sub Final Demo 1 GW Interim RA&Close-Out Rt	20	20	18SEP07	16OCT07	Prep/Sub Final Demo 1 GW Interim RA&Close-Out Rt																																									
CL0245	EPA Approve Demo 1 GW Interim RA & Close-Out Rt	15	15	17OCT07	06NOV07	EPA Approve Demo 1 GW Interim RA & Close-Out Rt																																									
J-1 Range																																															
J-1 Range Soil & Groundwater																																															
02185	Prepare/Submit Draft J-1 GW RRA Pln Project Note	66*	0*	02OCT06A	05JAN07A	Prepare/Submit Draft J-1 GW RRA Pln Project Note																																									
02189	Agency Review/Approve Draft J-1 GW RRA Pjct Note	31*	31*	08JAN07A	20FEB07	Agency Review/Approve Draft J-1 GW RRA Pjct Note																																									
02192	Informal Public Comment J-1 GW RRA Project Note	15	15	20JAN07	03FEB07	Informal Public Comment J-1 GW RRA Project Note																																									
0920	Prepare/Submit Final J-1 GW RRA Pln Project Note	10	10	21FEB07	06MAR07	Prepare/Submit Final J-1 GW RRA Pln Project Note																																									
02187	Design J-1 GW RRA Treatment System	120*	121*	09JAN07A	27JUN07	Design J-1 GW RRA Treatment System Assumes: design starts with agency commitments.																																									
02191	Construct/Startup J-1 GW RRA Treatment System	66	66	17SEP07	20DEC07	Construct/Startup J-1 GW RRA Treatment System Assumes: 66 days for procurement under PBC																																									
CL0250	Prepare/Submit Draft J-1 RRA GW SPM Plan	45	45	25APR07	27JUN07	Prepare/Submit Draft J-1 RRA GW SPM Plan																																									
CL0330	Agency Review/Approve Draft J-1 RRA GW SPM Plan	55*	55*	28JUN07	14SEP07	Agency Review/Approve Draft J-1 RRA GW SPM Plan																																									

General Notes:

A. 55 day - Agency Review/Approve Activity Includes:

15 days: Agency Review/Comment
15 days: Prepare/Submit RCL
5 days: Agency Review RCL
5 days: Agency Conduct CRM
10 days: Prepare/Submit MOR
5 days: Agency Approve MOR

B. FY07 Priorities

- Demolition Area 1 GW
- J-2 Range GW
- J-1 Range GW
- J-3 Range GW
- Small Arms Ranges
- Gun & Mortar
- Demolition Area Soil
- Western Boundary
- Ammunition Supply Point

Start Date: 01JAN06
Finish Date: 20DEC69
Data Date: 07JAN07
Run Date: 18JAN07 17:08

U197
RCS - Revised Format
as of 07JAN07


Sheet 1 of 14

Activity Colors

- IAGWSP Activities
- Agency Activities
- Formal/Informal Public Comment Activities

Activity ID	Activity Description	Orig Dur	Rem Dur	Anticipated /Actual Start	Anticipated /Actual Finish	FY07				FY08				FY09				FY10				FY11				FY12																																							
						J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D
												Hatched Area						Hatched Area						Hatched Area						Hatched Area																																			
CL0350	Prepare/Submit J-1 Final RRA GW SPM Plan	20	20	17SEP07	15OCT07																																																												
CL0360	Prepare/Submit Draft J-1 RRA GW COWR	45	45	21DEC07	26FEB08																																																												
CL0440	Agency Review/Approve Draft J-1 RRA GW COWR	55*	55*	27FEB08	13MAY08																																																												
CL0460	Prepare/Submit Final J-1 RRA GW COWR	20	20	14MAY08	11JUN08																																																												
02165	Implement Field Program/Validate J-1 SE GW Data	744*	61*	30APR04A	03APR07																																																												
10066	Prepare/Submit Draft J-1 South Soil/GW RI/FS Rpt	110	110	04APR07	07SEP07																																																												
10071	Agency Review/Approve Drft J-1 Sth Soil/GW RI/FS	55*	55*	10SEP07	28NOV07																																																												
10088	Prepare/Submit Final J-1 South Soil/GW RI/FS Rpt	20	20	29NOV07	27DEC07																																																												
SL0010	Prepare/Submit Draft J-1 South RSP	15	15	28DEC07	18JAN08																																																												
SL0020	Agency Review/Approve Draft J-1 South RSP	55*	55*	21JAN08	07APR08																																																												
SL0030	Prepare/Submit Final J-1 South RSP	10	10	08APR08	21APR08																																																												
SL0040	Formal Public Comment J-1 South RSP	30	30	22APR08	21MAY08																																																												
SL0050	Prepare/Submit Draft J-1 South DD	20	20	22MAY08	19JUN08																																																												
SL0060	Agency Review/Approve Draft J-1 South DD	55	55	20JUN08	08SEP08																																																												
SL0070	Prepare/Submit Final J-1 South DD	20	20	09SEP08	06OCT08																																																												
SL0080	EPA Issue J-1 South DD	15	15	07OCT08	28OCT08																																																												
10089	Design J-1 South GW Treatment System	120	120	01OCT07	24MAR08																																																												
10091	Construct/Startup J-1 South GW Treatment System	150	150	09SEP08	14APR09																																																												
SL0082	Prepare/Submit Draft J-1 South SPM Plan	60	60	28DEC07	24MAR08																																																												
SL0084	Agency Review/Approve Draft J-1 South SPM Plan	55*	55*	25MAR08	10JUN08																																																												
SL0086	Prepare/Submit Final J-1 South SPM Plan	20	20	11JUN08	09JUL08																																																												
SL0088	Prepare/Subm Draft J-1 South RA & Close-Out Rpts	60	60	18FEB09	12MAY09																																																												
SL0092	Agency Revw/Appr Dr J-1 South RA & Close-Out Rpts	55	55	13MAY09	30JUL09																																																												
SL0094	Prepare/Submit J-1 South RA & Close-Out Rpts	20	20	31JUL09	27AUG09																																																												
SL0096	EPA Approve J-1 South RA & Close-Out Rpts	15	15	28AUG09	18SEP09																																																												
10116	Prepare/Submit Draft J-1 North Soil/GW RI/FS Rpt	184	114	13MAR06A	21AUG07																																																												
10121	Agency Review/Approve Drft J-1 Nth Soil/GW RI/FS	55*	55*	22AUG07	08NOV07																																																												
10138	Prepare/Submit Final J-1 North Soil/GW RI/FS Rpt	20	20	09NOV07	10DEC07																																																												
SL0090	Prepare/Submit Draft J-1 North RSP	15	15	11DEC07	02JAN08																																																												


Activity ID	Activity Description	Orig Dur	Rem Dur	Anticipated /Actual Start	Anticipated /Actual Finish	FY07												FY08												FY09												FY10												FY11												FY12																																																																													
						J F M A M J J A S				O N D J F M A M J J A S				O N D J F M A M J J A S				O N D J F M A M J J A S				O N D J F M A M J J A S				O N D J F M A M J J A S				O N D J F M A M J J A S				O N D J F M A M J J A S																																																																																																													
						J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J
L Range																																																																																																																																															
L Range Soil & Groundwater																																																																																																																																															
02316	Resolve Comments on Draft L Soil RI Report	315*	48*	14DEC05A	15MAR07	Resolve Comments on Draft L Soil RI Report Note: excludes UXO																																																																																																																																									
0622	Resolve Comments on L GW Risk Assessment Rpt	210*	48*	16MAY06A	15MAR07	Resolve Comments on L GW Risk Assessment Rpt																																																																																																																																									
0703	Prepare/Submit Draft L Soil/GW RI/FS Rpt	121*	121*	06APR07	26SEP07	Prepare/Submit Draft L Soil/GW RI/FS Rpt																																																																																																																																									
0724	Agency Review/Approve Draft L Soil/GW RI/FS Rpt	55*	55*	27SEP07	17DEC07	Agency Review/Approve Draft L Soil/GW RI/FS Rpt																																																																																																																																									
0722	Prepare/Submit Final L Soil/GW RI/FS Rpt	20	20	18DEC07	16JAN08	Prepare/Submit Final L Soil/GW RI/FS Rpt																																																																																																																																									
SL0382	Prepare/Submit Draft L RSP	15	15	17JAN08	06FEB08	Prepare/Submit Draft L RSP																																																																																																																																									
SL0383	Agency Review/Approve Draft L RSP	55	55	07FEB08	24APR08	Agency Review/Approve Draft L RSP																																																																																																																																									
SL0384	Prepare/Submit Final L RSP	10	10	25APR08	08MAY08	Prepare/Submit Final L RSP																																																																																																																																									
SL0386	Formal Public Comment L RSP	30	30	09MAY08	08JUN08	Formal Public Comment L RSP																																																																																																																																									
SL0388	Prepare/Submit Draft L DD	20	20	09JUN08	07JUL08	Prepare/Submit Draft L DD																																																																																																																																									
SL0391	Agency Review/Approve Draft L DD	55*	55*	08JUL08	23SEP08	Agency Review/Approve Draft L DD																																																																																																																																									
SL0392	Prepare/Submit Final L DD	20	20	24SEP08	22OCT08	Prepare/Submit Final L DD																																																																																																																																									
SL0394	EPA Issue L DD	15	15	23OCT08	13NOV08	EPA Issue L DD																																																																																																																																									
SL0400	Prepare/Submit Draft L LTM Plan	60	60	14NOV08	10FEB09	Prepare/Submit Draft L LTM Plan																																																																																																																																									
SL0410	Agency Review/Approve Draft L LTM Plan	55*	55*	11FEB09	29APR09	Agency Review/Approve Draft L LTM Plan																																																																																																																																									
SL0420	Prepare/Submit Final L LTM Plan	20	20	30APR09	28MAY09	Prepare/Submit Final L LTM Plan																																																																																																																																									
SL0430	Prepare/Submit Draft L Interim RA & Close-Out Rpt	60	60	02APR09	25JUN09	Prepare/Submit Draft L Interim RA & Close-Out Rpt																																																																																																																																									
SL0440	Agency Review/Approve Draft L Interim RA & Close-Out	55*	55*	26JUN09	14SEP09	Agency Review/Approve Draft L Interim RA & Close-Out																																																																																																																																									
SL0450	Prepare/Submit Final L Interim RA & Close-Out Rpt	20	20	15SEP09	13OCT09	Prepare/Submit Final L Interim RA & Close-Out Rpt																																																																																																																																									
SL0460	EPA Approve L Interim RA & Close-Out Rpt	15	15	14OCT09	03NOV09	EPA Approve L Interim RA & Close-Out Rpt																																																																																																																																									
Central Impact Area																																																																																																																																															
CIA Soil & Groundwater																																																																																																																																															
03122	Agency Review/Approve Draft CIA Soil RRA COWR	364*	18*	19AUG05A	31JAN07	Agency Review/Approve Draft CIA Soil RRA COWR																																																																																																																																									
CIA2770	Prepare/Submit Final CIA Soil RRA COWR	20	20	01FEB07	01MAR07	Prepare/Submit Final CIA Soil RRA COWR																																																																																																																																									
00261	Prepare/Submit Draft CIA Soil Investigation Rpt	846*	144*	04APR04A	31JUL07	Prepare/Submit Draft CIA Soil Investigation Rpt																																																																																																																																									
00263	Agency Review/Approve Draft CIA Soil Investigatn	55	55	01AUG07	18OCT07	Agency Review/Approve Draft CIA Soil Investigatn																																																																																																																																									
00299	Prepare/Submit Final CIA Soil Investigation Rpt	20	20	19OCT07	16NOV07	Prepare/Submit Final CIA Soil Investigation Rpt																																																																																																																																									
02030	Agency Review/Approve Draft CIA GW Report	719*	6*	19MAR04A	15JAN07	Agency Review/Approve Draft CIA GW Report																																																																																																																																									
22110	Prepare/Submit Draft CIA Soil/GW FS Screening Rpt	504*	6*	14APR05A	13APR07	Prepare/Submit Draft CIA Soil/GW FS Screening Rpt																																																																																																																																									

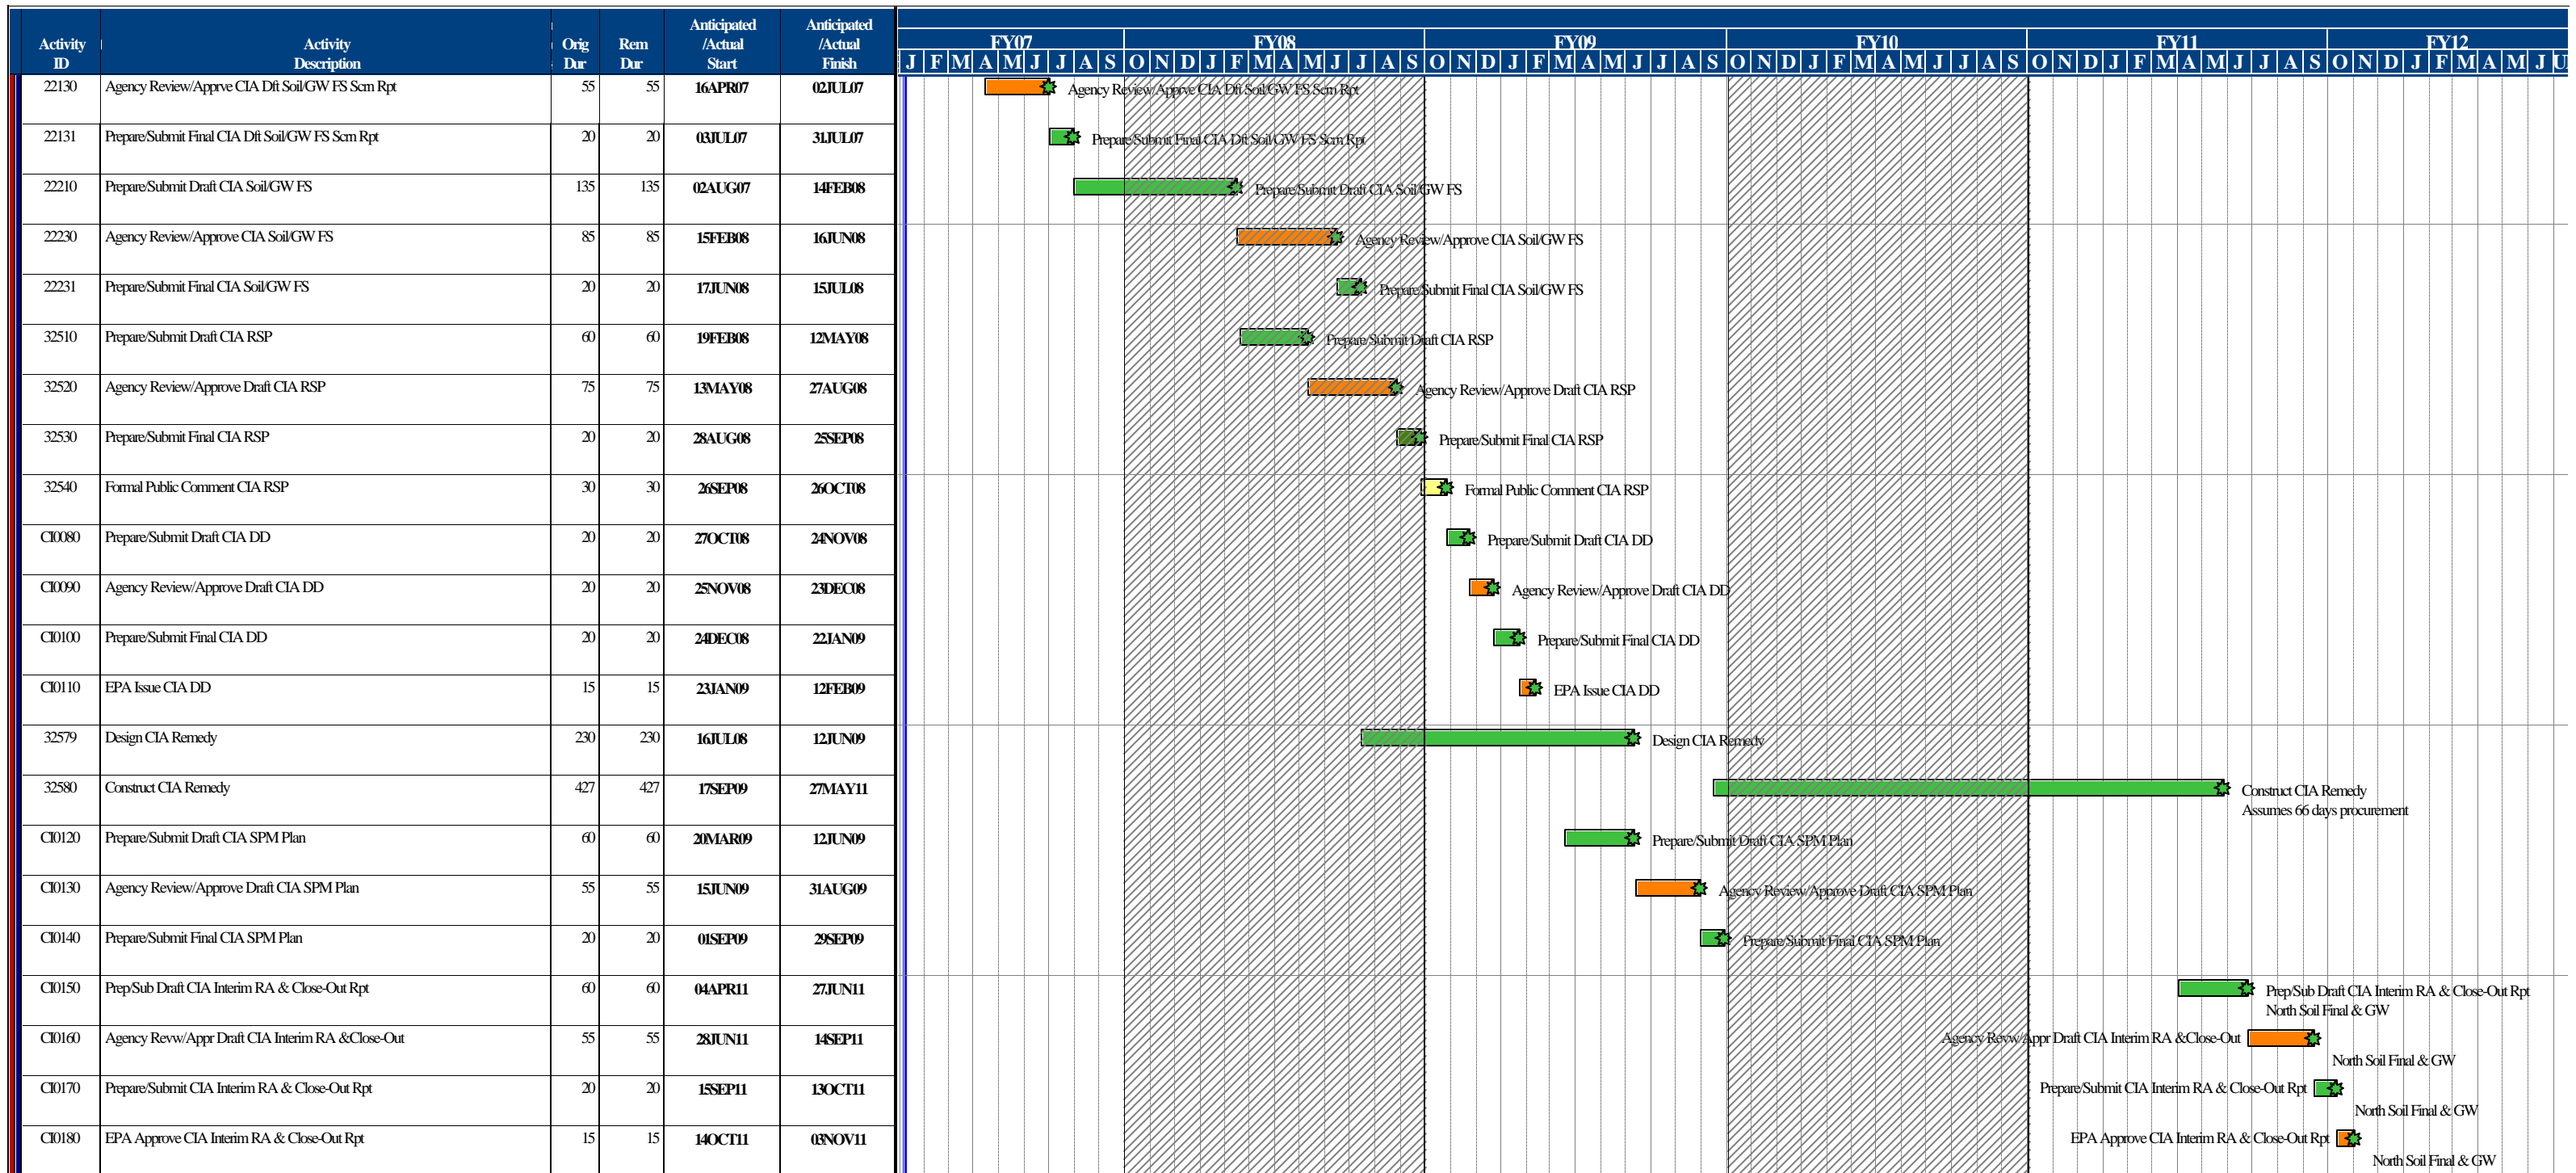

Northwest Corner

Northwest Corner Soil & Groundwater

03451	Prepare/Submit Draft Northwest Corner RI/FS	135	134	09NOV06A	19SEP07
03453	Agency Review/Approve Draft Northwest Corner RI/FS	55*	55*	20SEP07	10DEC07
03454	Prepare/Submit Final Northwest Corner RI/FS	20	20	11DEC07	09JAN08
SL0600	Prepare/Submit Draft Northwest Corner RSP	15	15	10JAN08	30JAN08
SL0610	Agency Review/Approve Draft Northwest Corner RSP	55*	55*	31JAN08	17APR08
SL0620	Prepare/Submit Final Northwest Corner RSP	10	10	18APR08	01MAY08

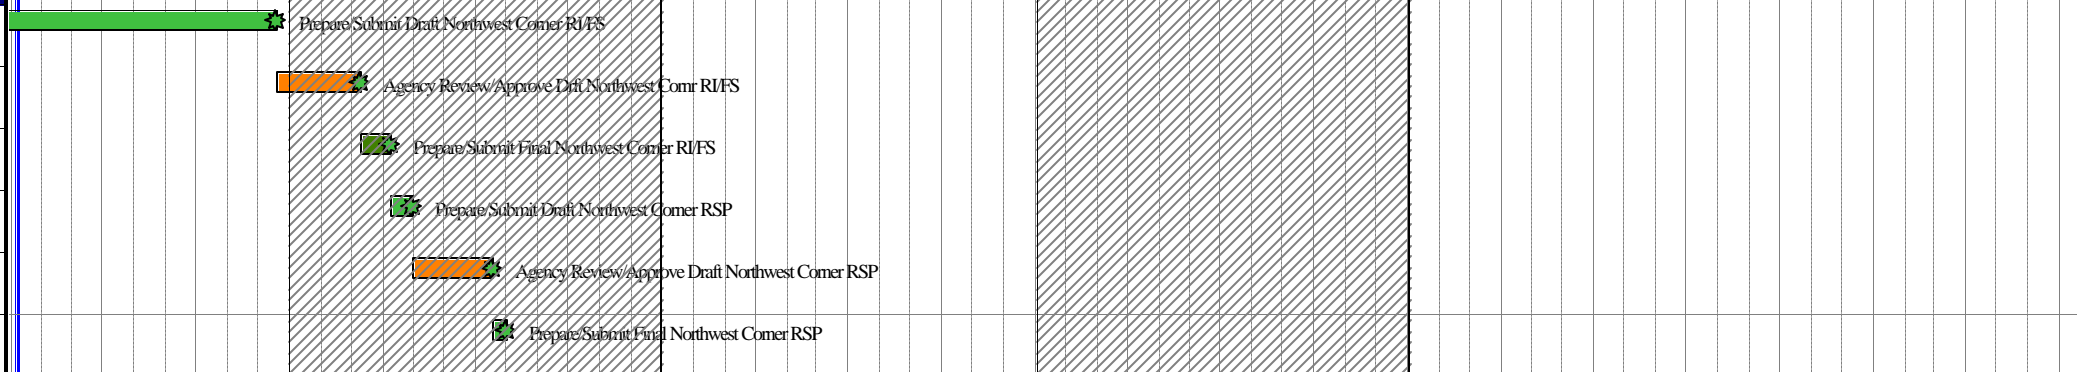

Activity ID	Activity Description	Orig Dur	Rem Dur	Anticipated /Actual Start	Anticipated /Actual Finish	FY07				FY08				FY09				FY10				FY11				FY12																					
						J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J
WB4210	EPA Approve WB Interim RA & Close-Out Rpt	15	15	18DEC08	09JAN09																																										
Demo 2																																															
Demo 2 Soil & Groundwater																																															
01574	Prepare/Submit Draft Demo 2 Soil/GW Investig Rpt	93	45	30JUN06A	10SEP07																																										
01578	Agency Review/Approve Draft Demo 2 Soil/GW Invest	55*	55*	11SEP07	29NOV07																																										
01579	Prepare/Submit Final Demo 2 Soil/GW Investig Rpt	20	20	30NOV07	28DEC07																																										
01608	Prepare/Submit Draft Demo 2 RSP	30	30	31DEC07	11FEB08																																										
01609	Agency Review/Approve Draft Demo 2 RSP	55*	55*	12FEB08	29APR08																																										
01611	Prepare/Submit Final Demo 2 RSP	20	20	30APR08	28MAY08																																										
01613	Formal Public Comment Demo 2 RSP	30	30	29MAY08	27JUN08																																										
01615	Prepare/Submit Draft Demo 2 DD	20	20	30JUN08	28JUL08																																										
01623	Agency Review/Approve Demo 2 DD	55*	55*	29JUL08	15OCT08																																										
01624	Prepare/Submit Final Demo 2 DD	20	20	16OCT08	13NOV08																																										
01625	EPA Issue Demo 2 DD	15	15	14NOV08	05DEC08																																										
2D0100	Prepare/Submit Draft Demo 2 LTM Plan	45	45	08DEC08	10FEB09																																										
2D0110	Agency Review/Approve Draft Demo 2 LTM Plan	55*	55*	11FEB09	29APR09																																										
2D0120	Prepare/Submit Final Demo 2 LTM Plan	20	20	30APR09	28MAY09																																										
2D0130	Prepare/Submit Drft Demo2 Interim RA & Close-Out	60	60	02APR09	25JUN09																																										
2D0140	Agency Revw/Appro Dr Demo2 Interim RA & Close-Out	55*	55*	26JUN09	14SEP09																																										
2D0150	Prep/Sub Final Demo 2 Interim RA & Close-Out Rpt	20	20	15SEP09	13OCT09																																										
2D0160	EPA Approve Demo 2 Interim RA & Close-Out Rpt	15	15	14OCT09	03NOV09																																										
Gun & Mortar																																															
Gun & Mortar Soil & Groundwater																																															
00606	Prepare/Submit Draft G&M Soil/GW Investigatn WP	286*	15*	08DEC05A	26JAN07																																										
00608	Agency Review/Approve Dr G&M Soil/GW Investig WP	55*	55*	29JAN07	16APR07																																										
00619	Prepare Final G&M Soil/GW Investig. Plan	20	20	17APR07	14MAY07																																										
CL2116	Conduct G&M Soil/GW Investigation	95*	95*	17JAN07	31MAY07																																										
00601	Agency Monitor G&M Soil/GW Investigation	95*	95*	17JAN07	31MAY07																																										
CL1760	Prepare/Submit Draft G&M Soil RRA Plan	41	41	17APR07	13JUN07																																										
CL1840	Agency Review/Approve Draft G&M Soil RRA Plan	55*	55*	14JUN07	30AUG07																																										
CL1845	Infomal Public Comment G&M Soil RRA Plan	15	15	06JUL07	20JUL07																																										

