
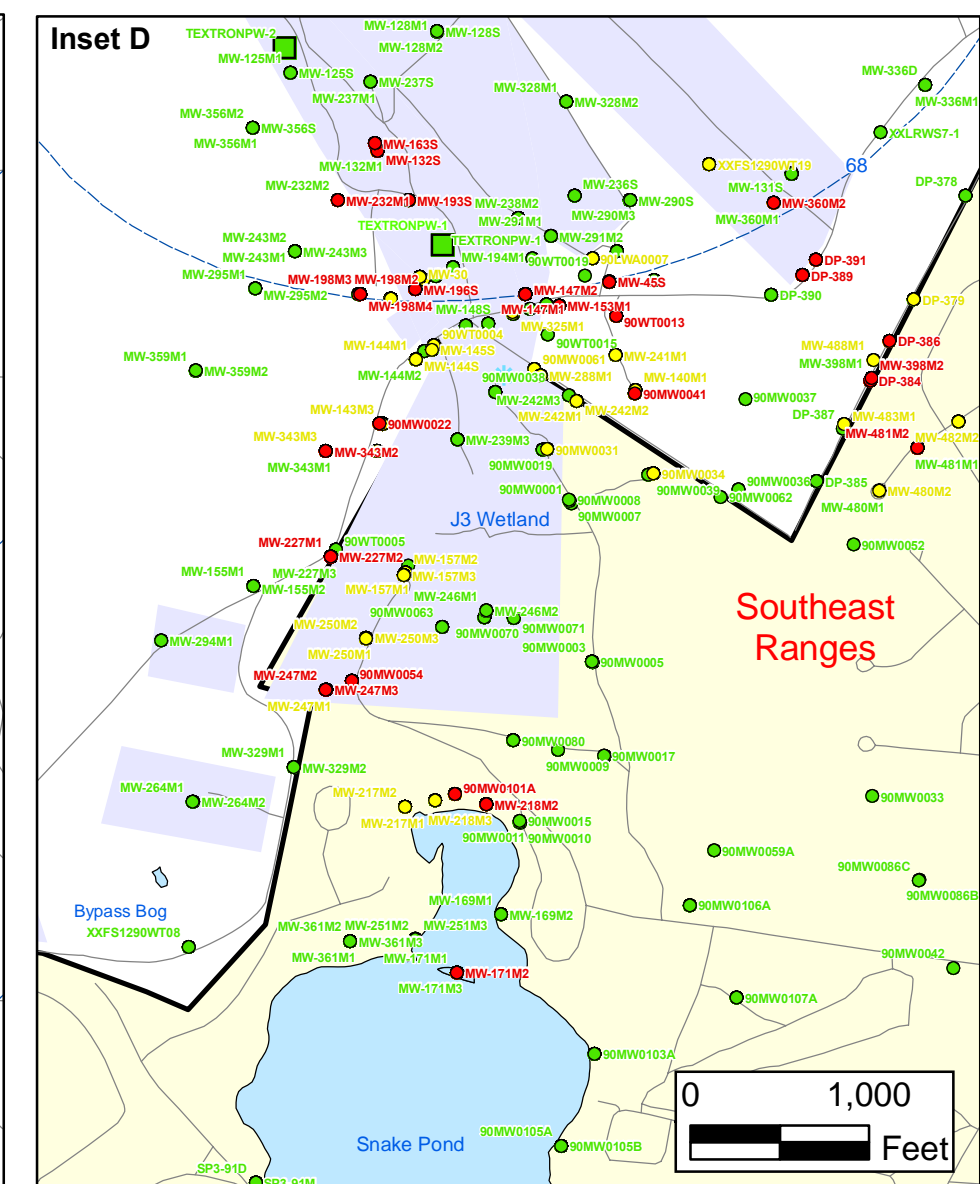
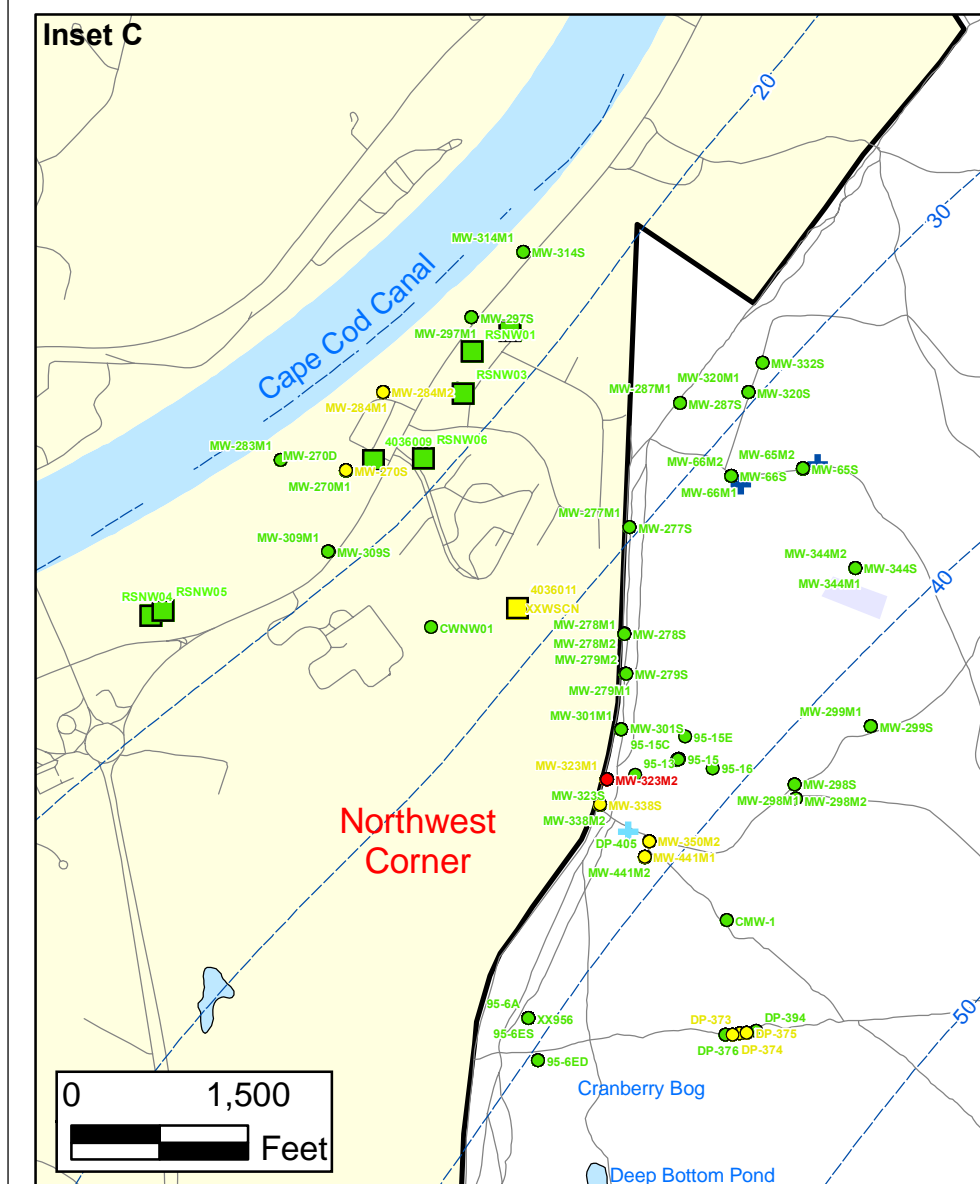


Explosives in Groundwater Compared to Maximum Contaminant Level/Health Advisories Validated Data as of 2008

FIGURE 1

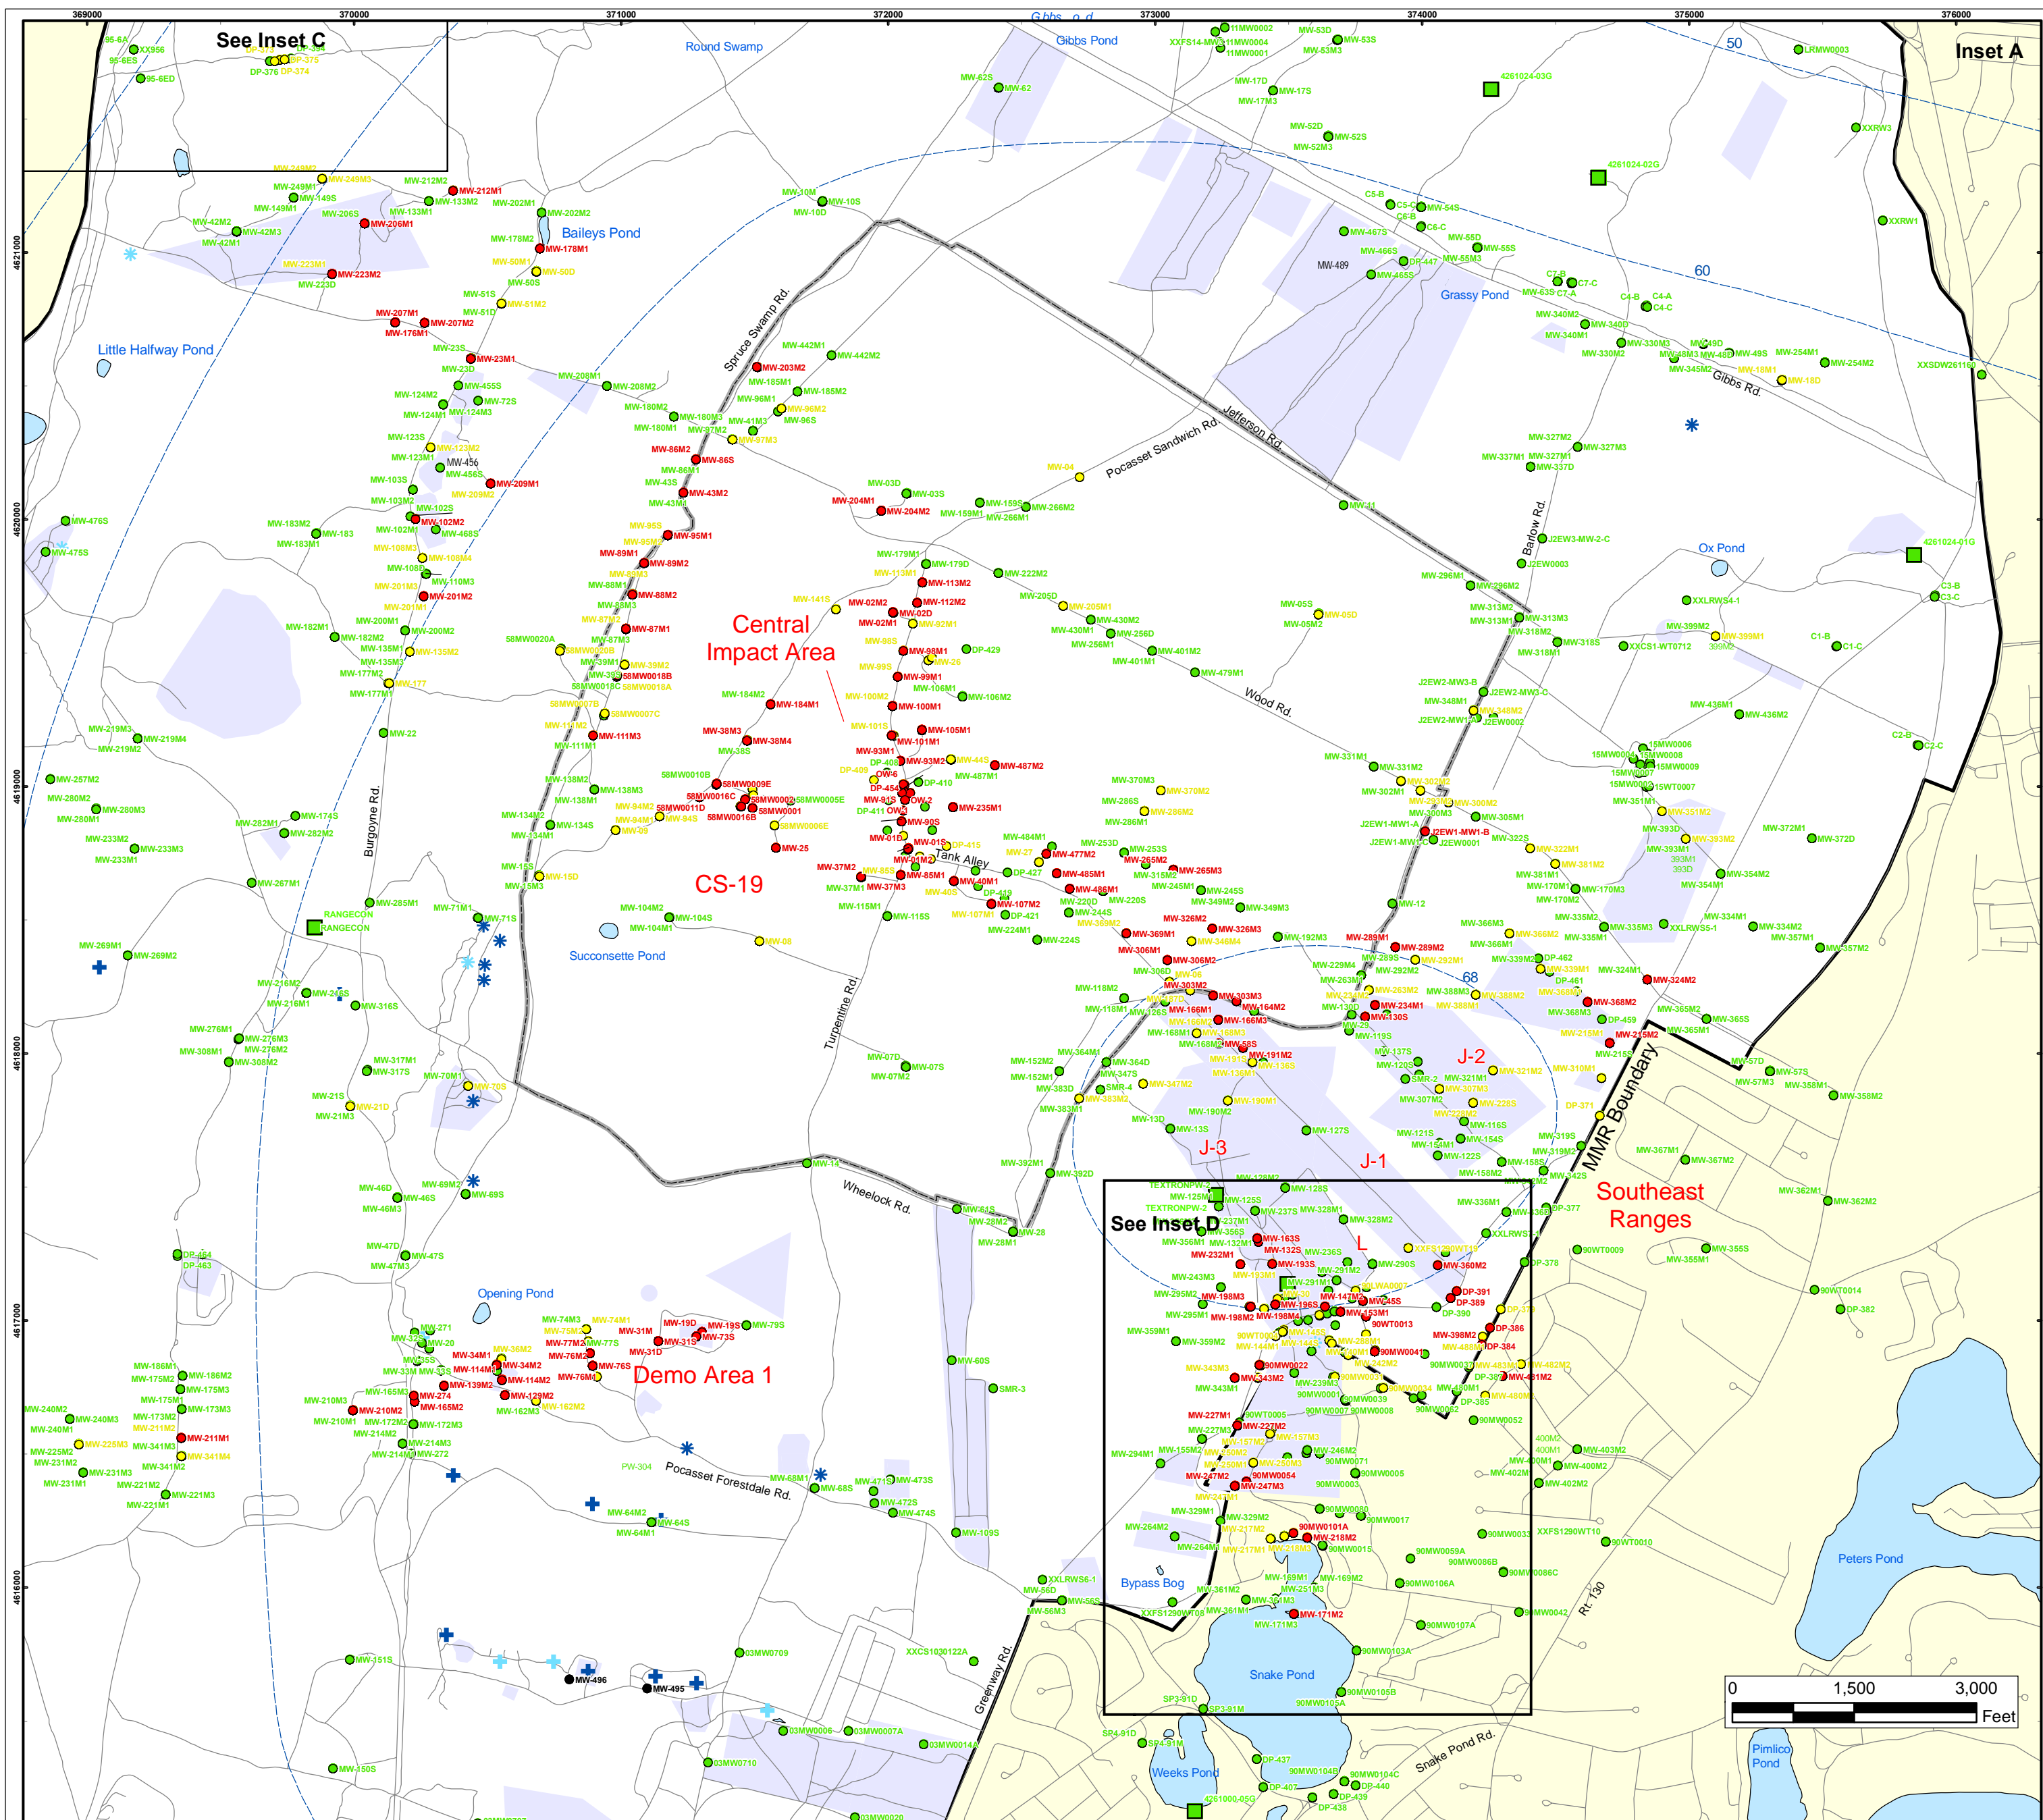

Explosives in Groundwater Compared to Maximum Contaminant Level/Health Advisories

Validated Data as of 2008

- Validated Detection Greater than or Equal to Maximum Contaminant Level/Health Advisories
- Validated Detection Less than Maximum Contaminant Level/Health Advisories
- Validated Non-Detect
- Data Pending
- Military Range Areas
- + Current Gun Position
- * Current Mortar Position
- + Old Gun Position
- * Old Mortar Position
- Validated Non-Detect Water Supply Well
- Validated Detection Less than Maximum Contaminant Level/Health Advisories Water Supply Well
- Water Table Contour (Feet NGVD), AMEC, September 2003

Note: Map dot colors are representative of the highest historical concentration at each well and not the current concentration level. Historical data presented on this figure range from November 1996 through 2007.


**Impact Area
Groundwater Study Program**

ECC-MMR
Cape Cod, Massachusetts

Sources & Notes
Base map data from US Geological Survey
7 1/2 minute Topographic Maps
Source: Office of Geographic and
Environmental Information (MassGIS)
Commonwealth of Massachusetts
Executive Office of Environmental Affairs

FIGURE 1

Inset Map

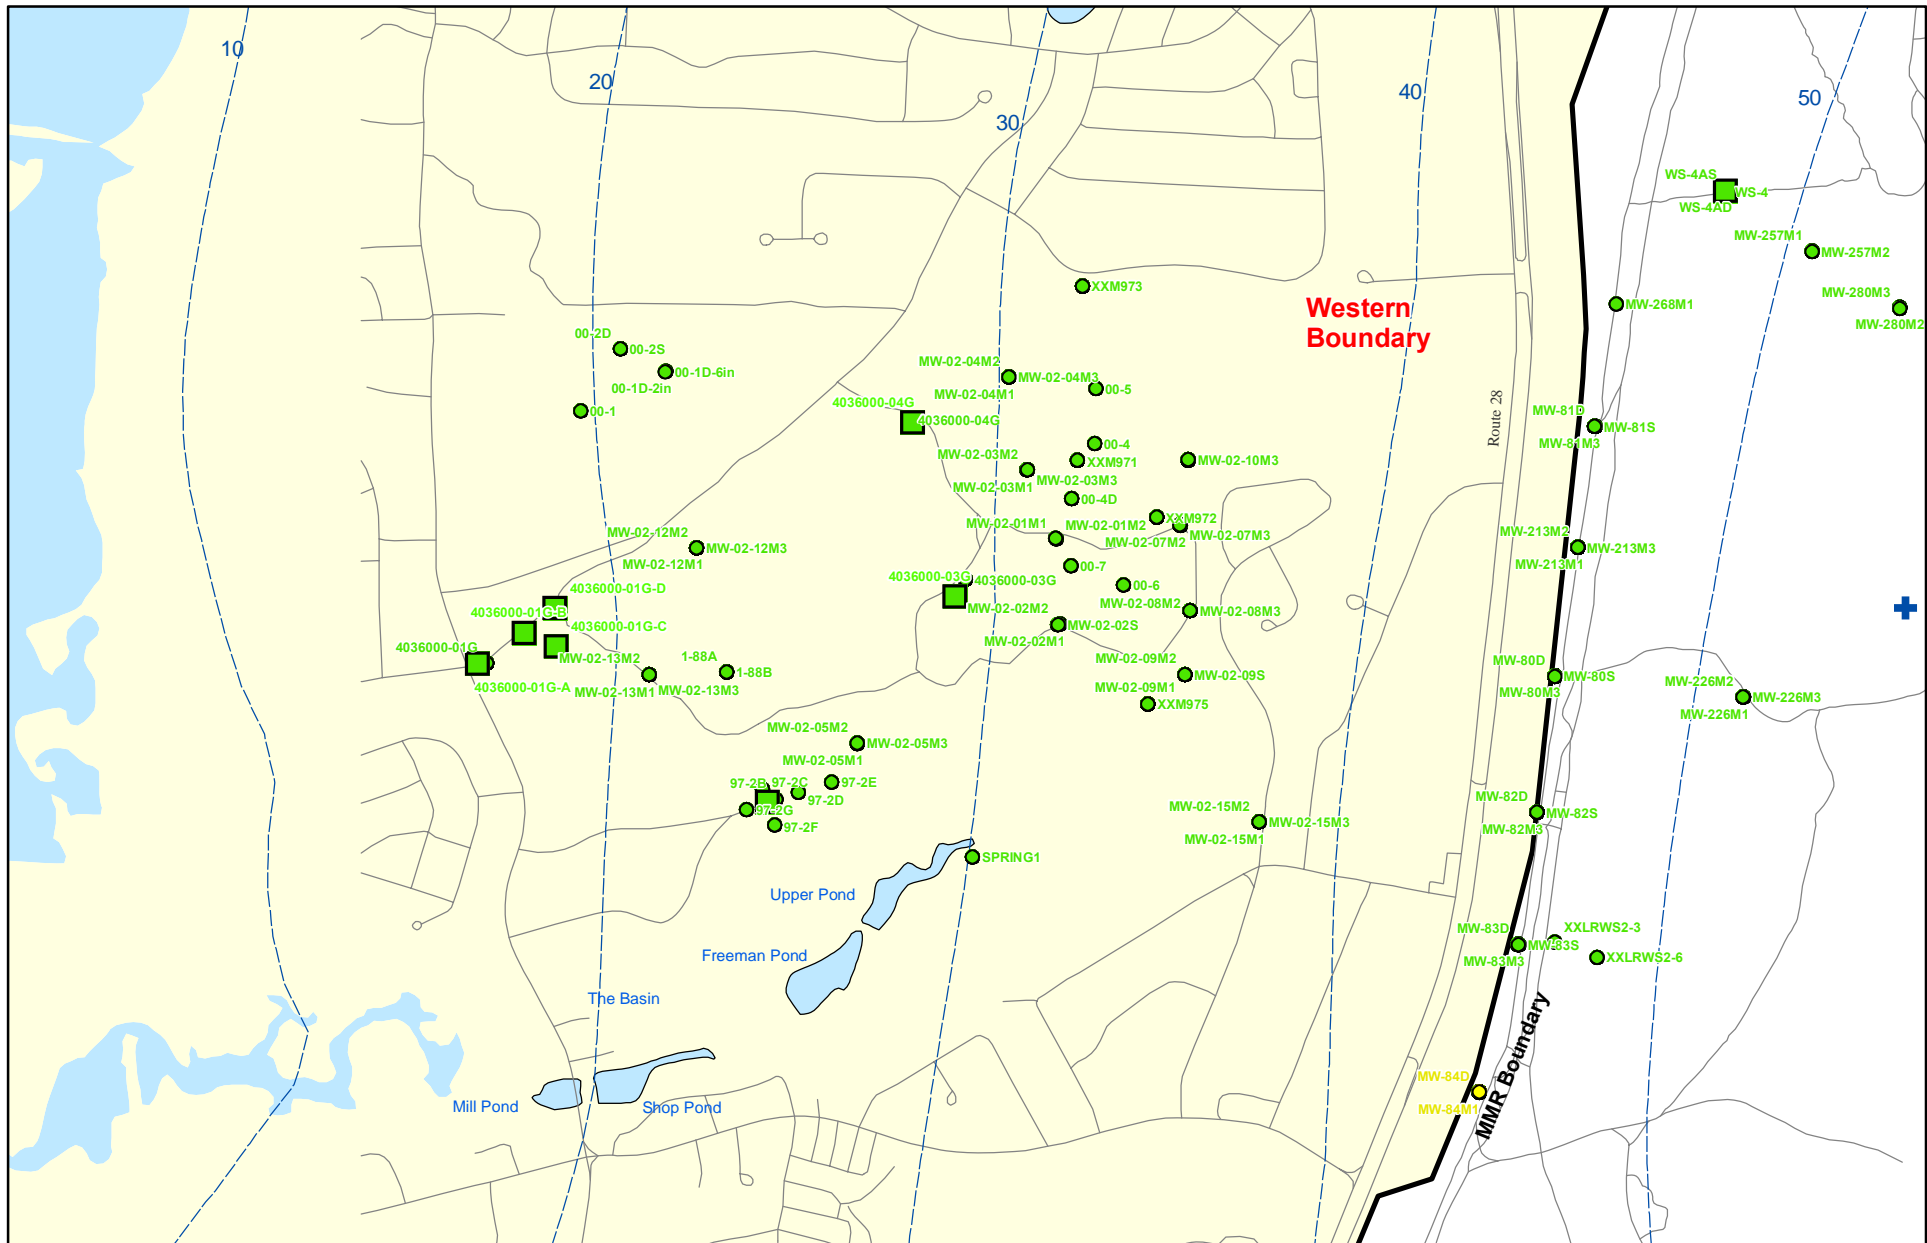

Sources & Notes:
 Base map data from US Geological Survey
 7 1/2 minute Topographic maps.
 Source: Office of Geographic and
 Environmental Information (MassGIS)
 Commonwealth of Massachusetts
 Executive Office of Environmental Affairs

- Validated Detection Less than Maximum Contaminant Level/Health Advisories
- Validated Non-Detect
- Validated Non-Detect Water Supply Well
- Proposed Water Supply Well
- + Current Gun Position
- Water Table Contour (Feet NGVD)
AMEC, September 2003


**Explosives in Groundwater Compared to
 Maximum Contaminant Level/Health Advisories
 Validated Data as of 2008**

**Impact Area
 Groundwater Study Program**

Note: Map dot colors are representative of the highest historical concentration at each well and not the current concentration level.
 Historical data presented on this figure range from November 1996 through 2007.

ECC-MMR
 Cape Cod, Massachusetts

FIGURE
Inset Map B 1

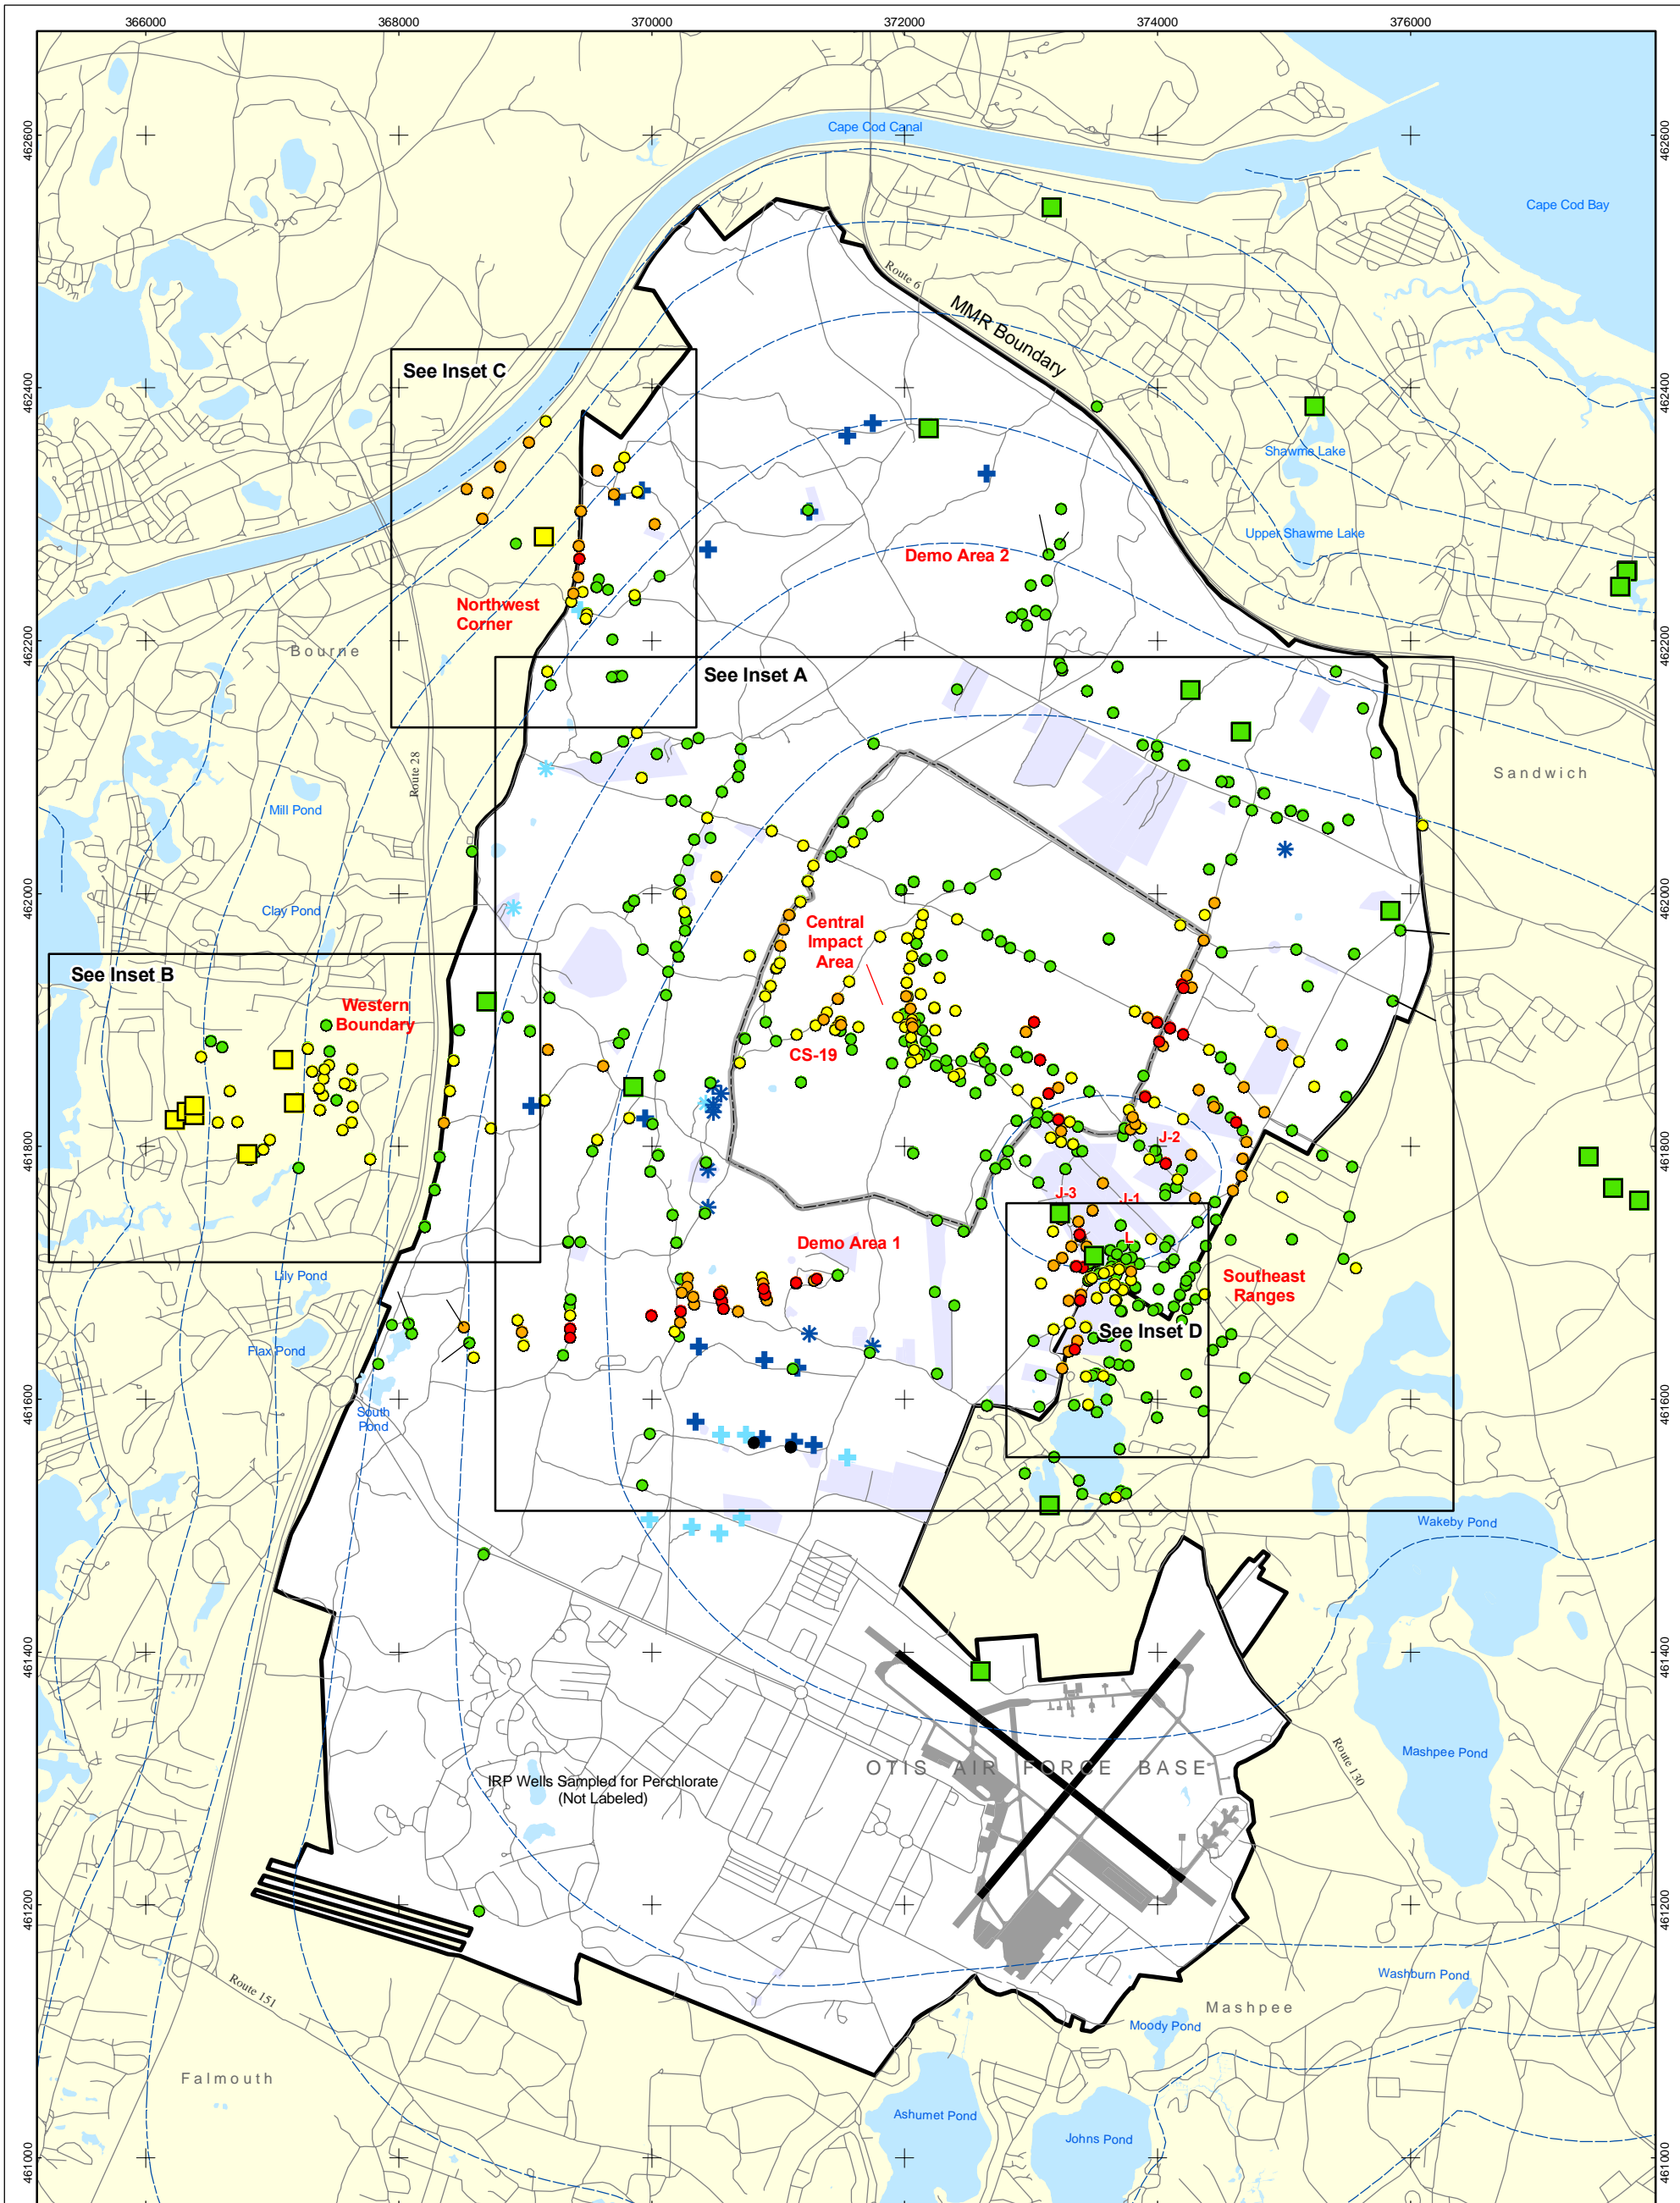


- Validated Detection Greater than or Equal to 24 ppb
- Validated Detection Greater than or Equal to 2 and Less than 24 ppb
- Validated Detection Greater than Non-Detect and Less than 2 ppb
- Validated Non-Detect

Note: Map dot colors are representative of the highest historical concentration at each well and not the current concentration level. Historical data presented on this figure range from November 1996 through 2007.




- Data Pending
- Proposed Monitoring Well
- ⊕ Current Gun Position
- ⊛ Current Mortar Position
- ⊕ Old Gun Position
- ⊛ Old Mortar Position

- Validated Non-Detect Water Supply Well
- Validated Detection Less than 2 ppb Water Supply Well
- Proposed Water Supply Well
- - - Water Table Contour (Feet NGVD) AMEC, September 2003
- Military Range Areas



Sources & Notes
 Base map data from US Geological Survey
 7 1/2 minute Topographic Maps
 Source: Office of Geographic and
 Environmental Information (MassGIS)
 Commonwealth of Massachusetts
 Executive Office of Environmental Affairs

**Perchlorate in Groundwater
 Compared to a 2 ppb Concentration
 Validated Data as of 2008**

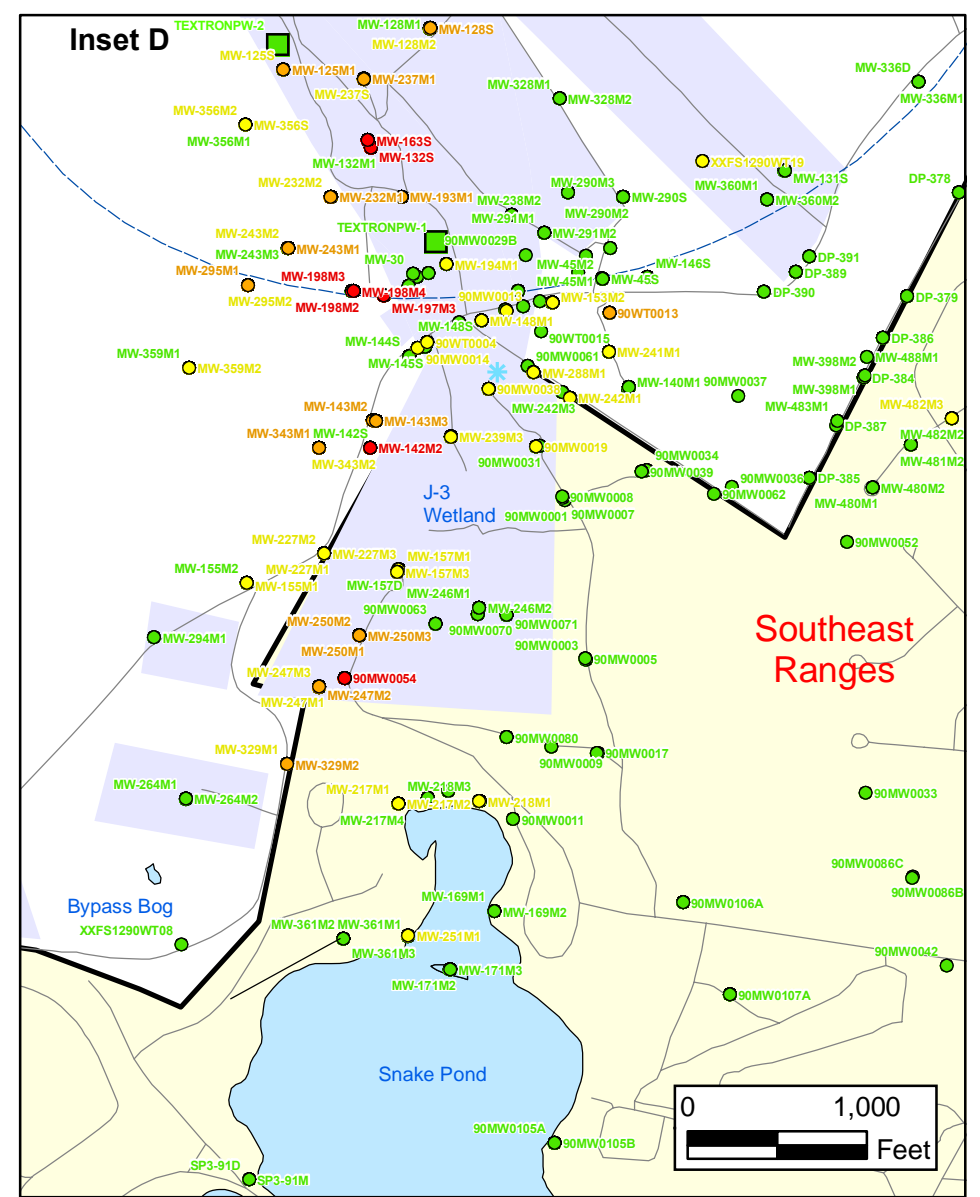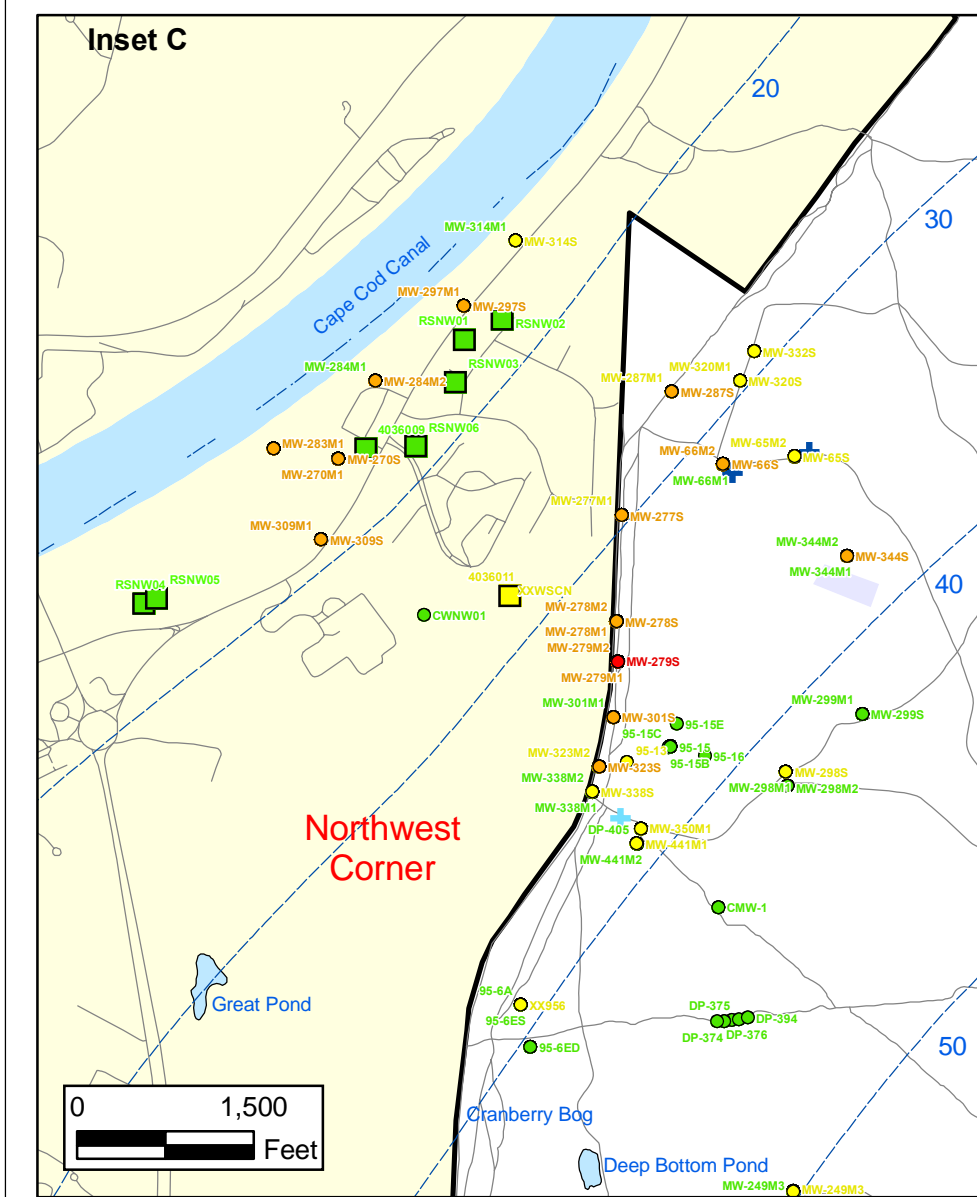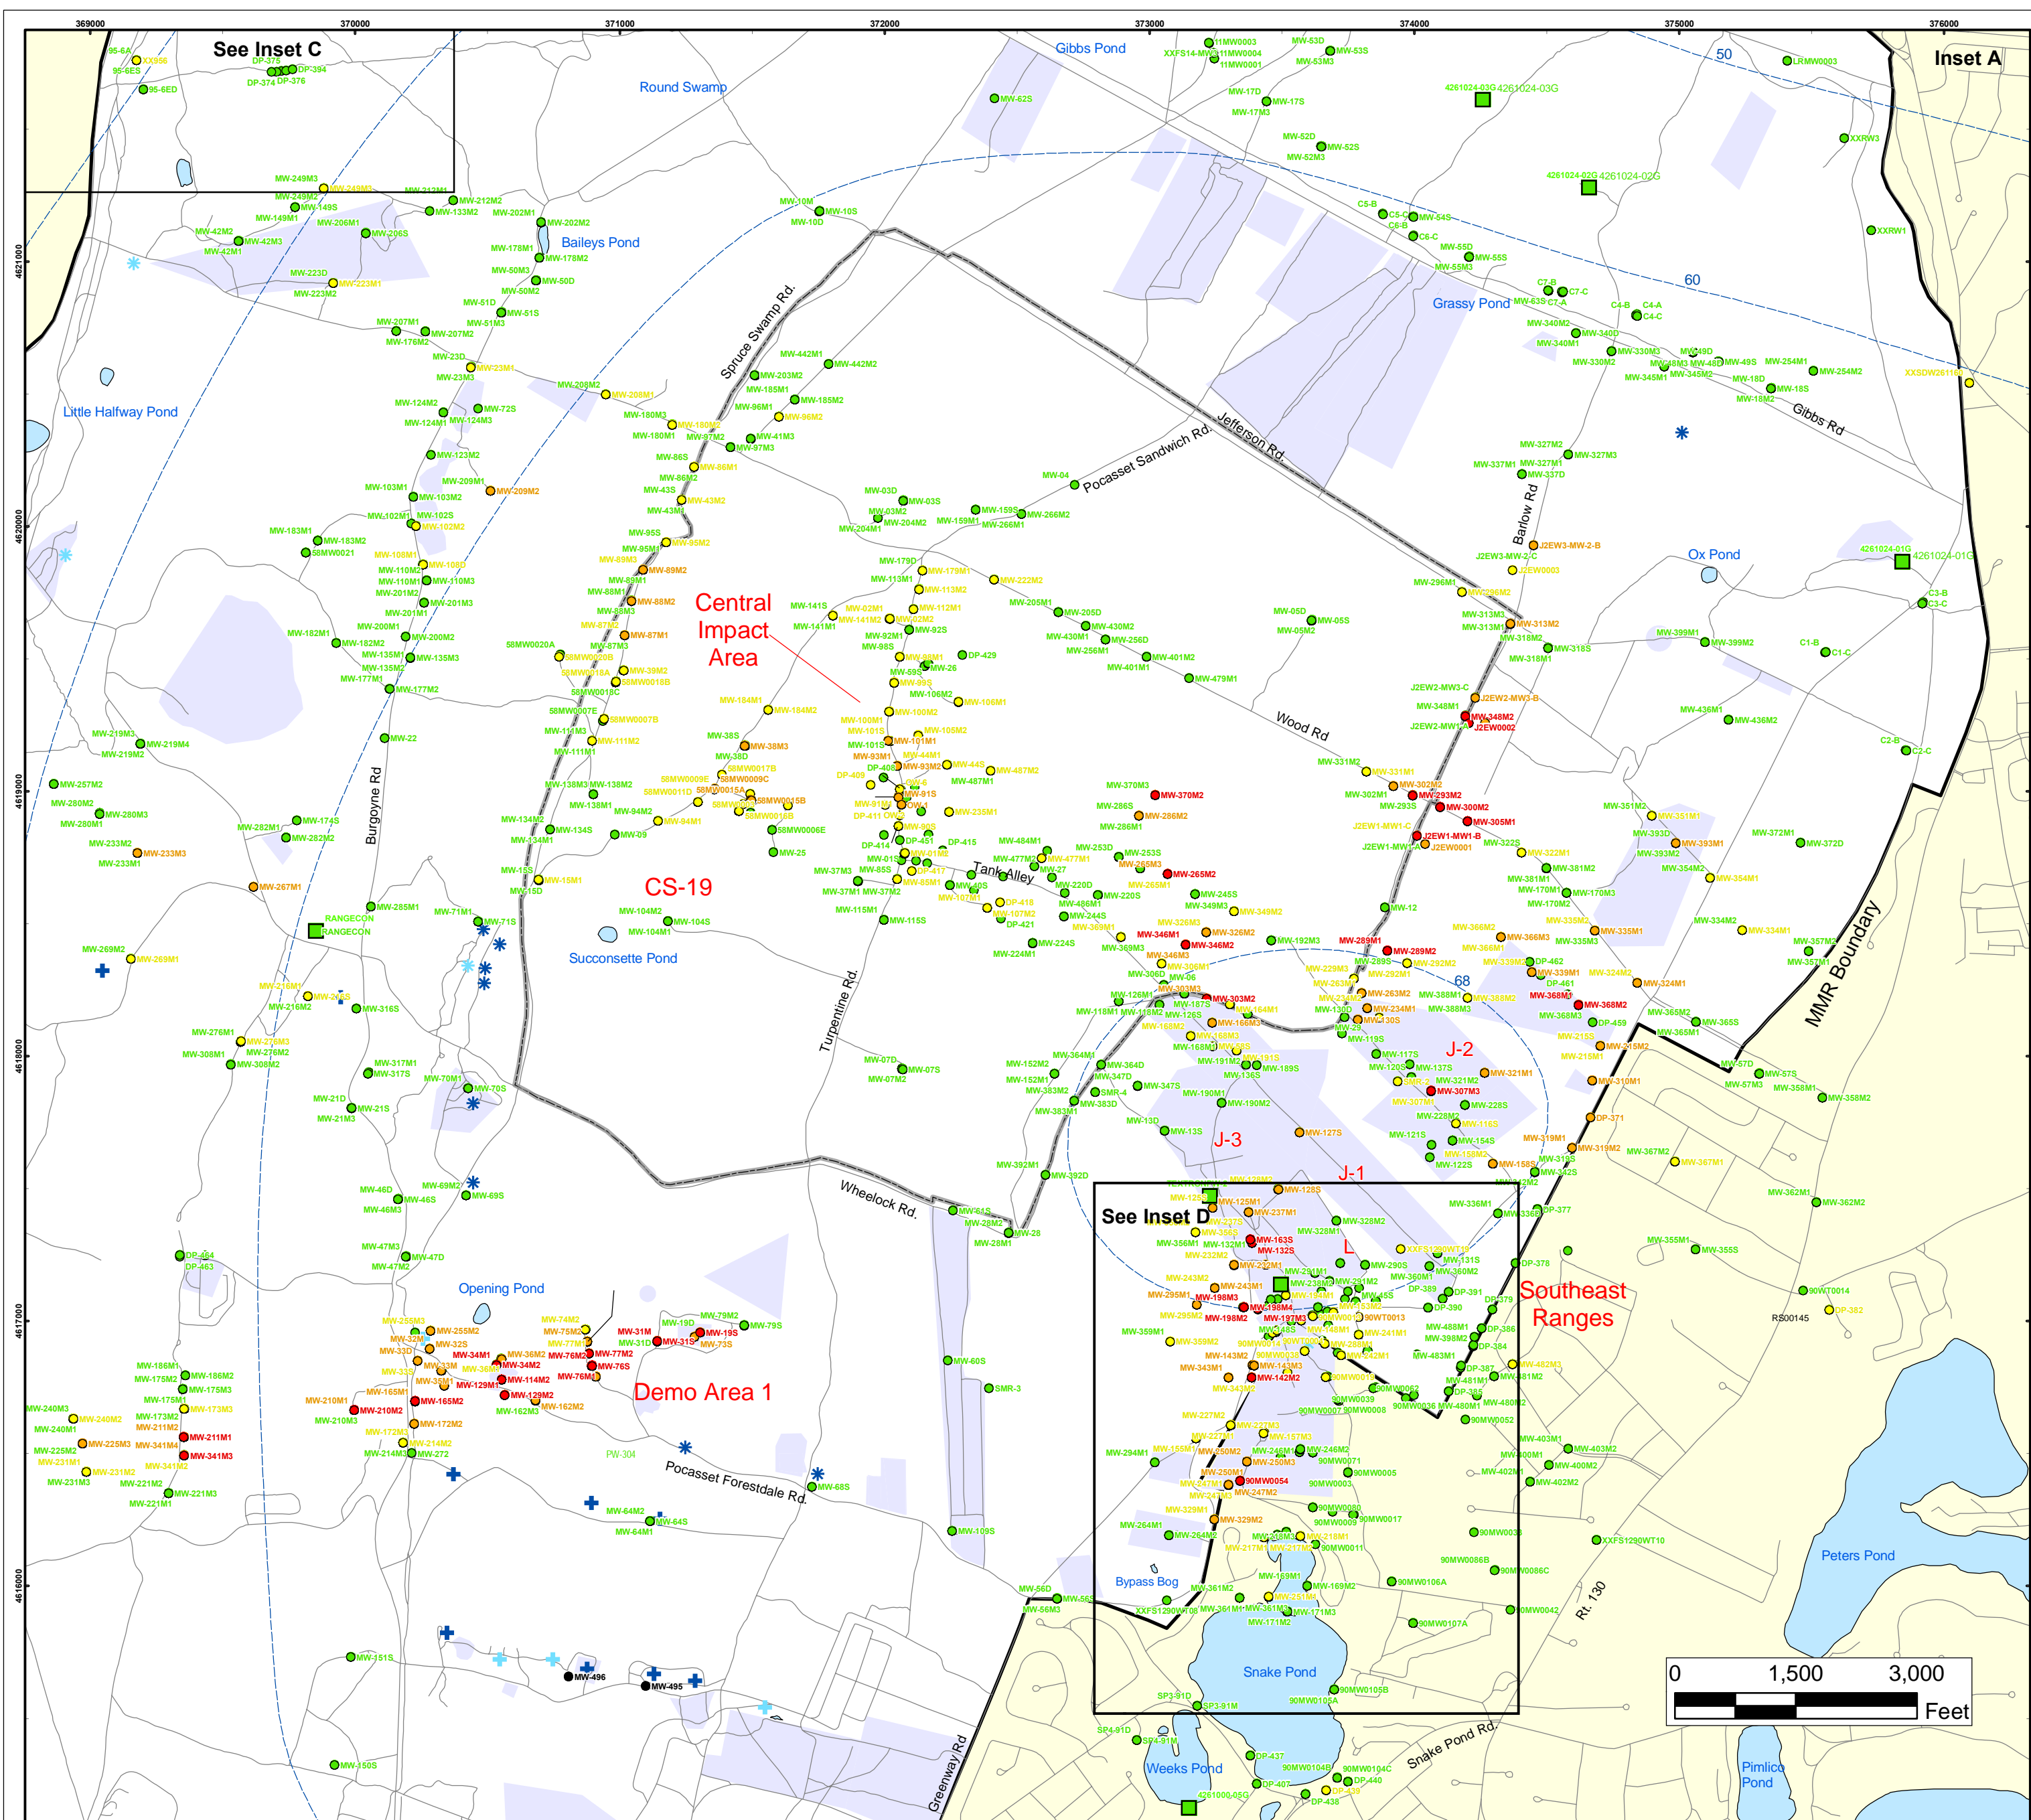



Perchlorate in Groundwater Compared to a 2 PPB Concentration Validated Data as of 2008

- Validated Detection Greater than or Equal to 24 ppb
- Validated Detection Greater than or Equal to 2 and Less than 24 ppb
- Validated Detection Less than 2 ppb
- Validated Non-Detect
- Data Pending
- Military Range Areas
- + Current Gun Position
- * Current Mortar Position
- + Old Gun Position
- * Old Mortar Position
- Validated Non-Detect Water Supply Well
- Validated Detection Less Than 2 ppb Water Supply Well
- Water Table Contour (Feet NGVD), AMEC, September 2003

Note: Map dot colors are representative of the highest historical concentration at each well and not the current concentration level. Historical data presented on this figure range from November 1996 through 2007.

ECC-MMR
Cape Cod, Massachusetts

FIGURE
8

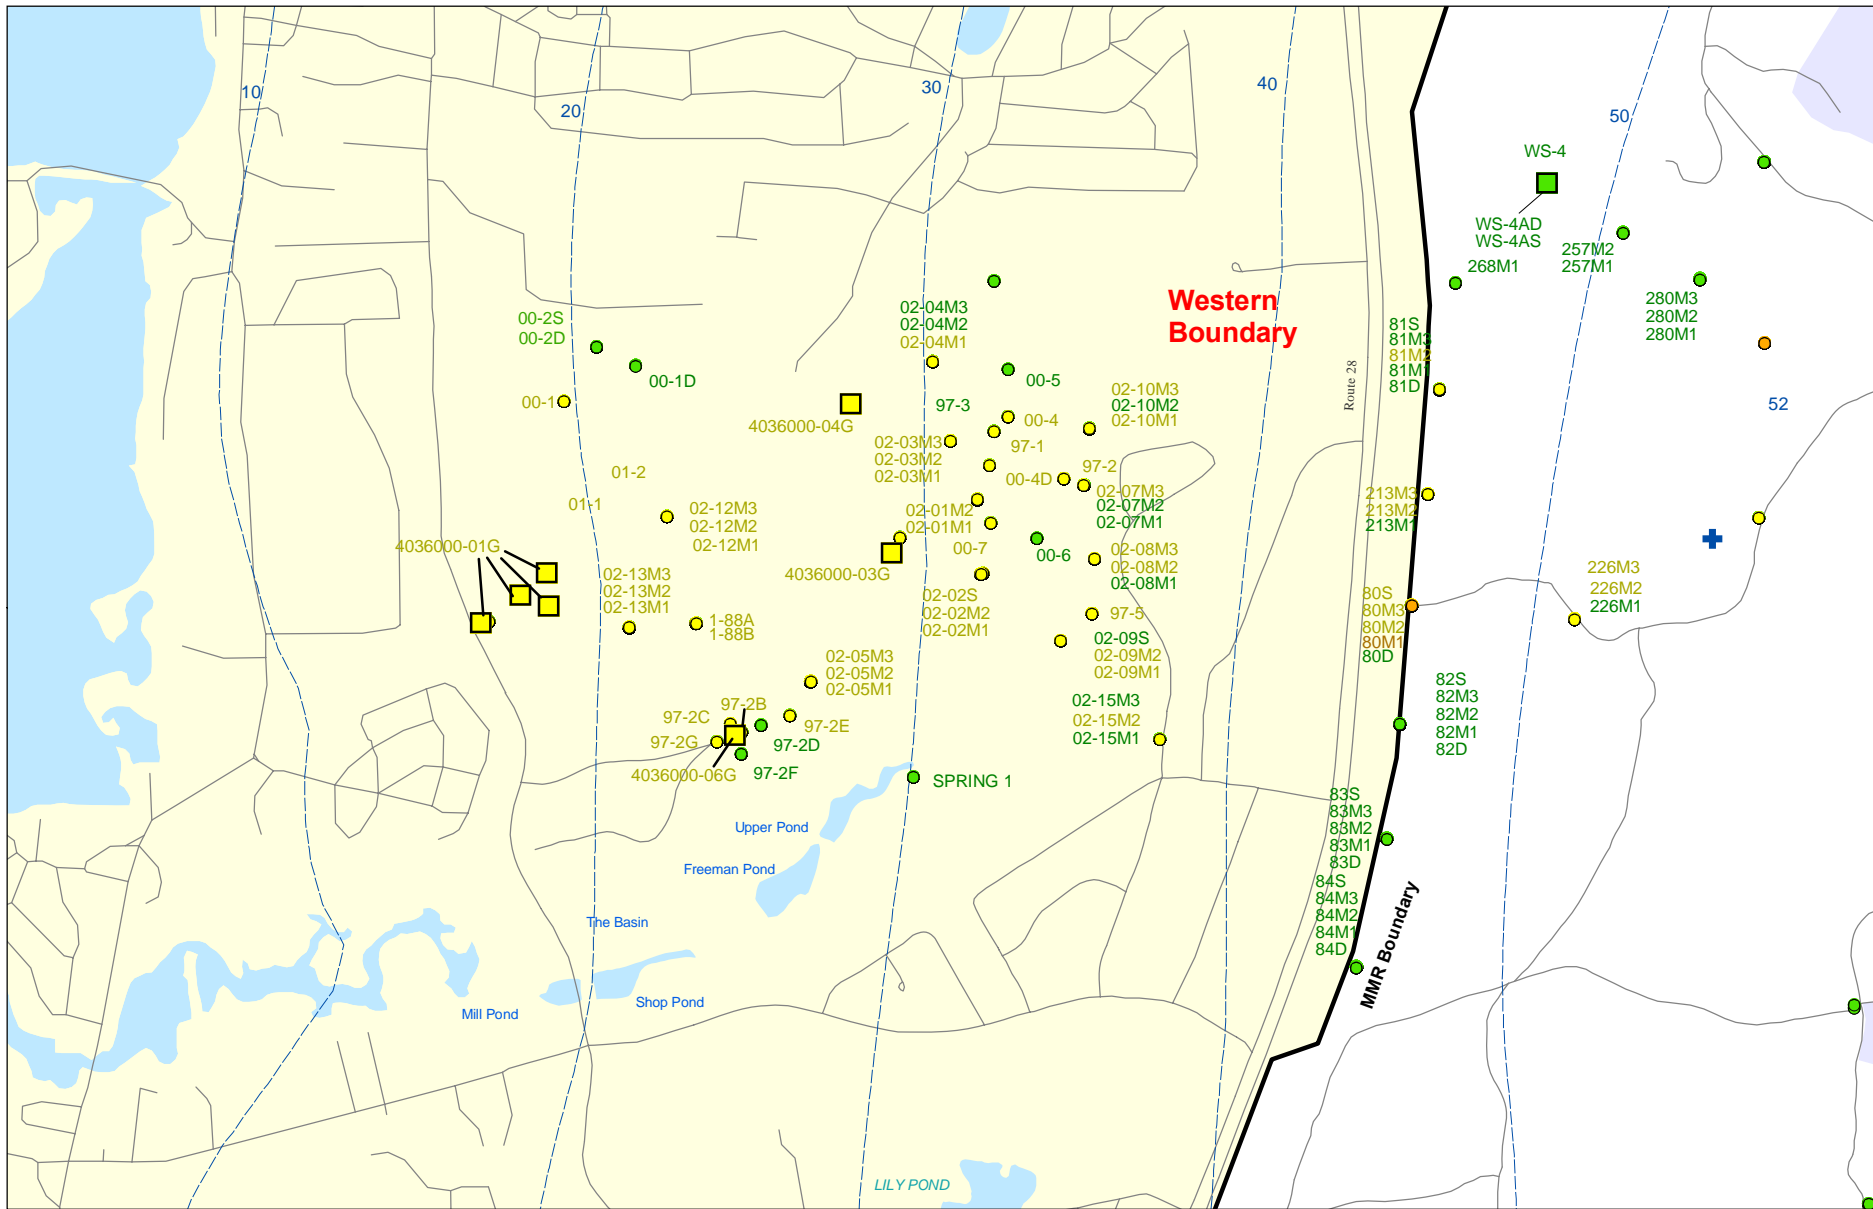

Sources & Notes:
 Base map data from US Geological Survey
 7 1/2 minute Topographic maps.
 Source: Office of Geographic and
 Environmental Information (MassGIS)
 Commonwealth of Massachusetts
 Executive Office of Environmental Affairs

- Validated Detection Greater than or Equal to 2 and Less than 24 ppb
- Validated Detection Greater than Non-Detect and Less than 2 ppb
- Validated Non-Detect

Note: Map dot colors are representative of the highest historical concentration at each well and not the current concentration level.
 Historical data presented on this figure range from November 1996 through 2007.

- Validated Detection Less than 2 ppb Water Supply Well
- Validated Non-Detect Water Supply Well
- + Current Gun Position
- Water Table Contour (Feet NGVD)
AMEC, September 2003

Perchlorate in Groundwater Compared to a 2 ppb Concentration Validated Data as of 2008



Impact Area
Groundwater Study Program

ECC-MMR
Cape Cod, Massachusetts

Inset Map B

Activity ID	Activity Description	Orig Dur	Rem Dur	Anticipated /Actual Start	Anticipated /Actual Finish	FY08					FY09					FY10					FY11					FY12																													
						F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S						
Demolition Area 1																															General Notes: A. 55-65 day - Agency Review/Approve Activity Includes: 15-25 days: Agency Review/Comment 15 days: Prepare/Submit RCL 5 days: Agency Review RCL 5 days: Agency Conduct CRM 10 days: Prepare/Submit MOR 5 days: Agency Approve MOR																								
Demolition Area 1 Soil																																																							
DM1782	Prepare Demo 1 Supplemental Post Screening Rpt	345	35	06SEP06A	21MAR08	Prepare Demo 1 Supplemental Post Screening Rpt																																																	
00145	Agency Review/Approve Draft Demo 1 RRA Soil COWR	599*	68*	22DEC05A	07MAY08	Agency Review/Approve Draft Demo 1 RRA Soil COWR																																																	
DM0920	Prepare/Submit Final Demo 1 RRA Soil COWR	20	20	08MAY08	05JUN08	Prepare/Submit Final Demo 1 RRA Soil COWR																																																	
Demolition Area 1 Groundwater																																																							
CL0100	Agency Review/Approve Draft Demo 1 ESPM Plan	251*	11*	20FEB07A	15FEB08	Agency Review/Approve Draft Demo 1 ESPM Plan																																																	
CL0130	Prepare/Submit Final Demo 1 ESPM Plan	20	20	19FEB08	17MAR08	Prepare/Submit Final Demo 1 ESPM Plan																																																	
CL0140	Prepare/Submit Dr Demo1 GW Remedial Const Rpt	40	0	26JUN07A	05NOV07A																																																		
CL0220	Agency Revw/Appr Dr Demo1 GW Remedial Const Rpt	104*	45*	06NOV07A	04APR08	Agency Revw/Appr Dr Demo1 GW Remedial Const Rpt																																																	
CL0240	Prep/Sub Final Demo1 GW Remedial Const Rpt	20	20	07APR08	02MAY08	Prep/Sub Final Demo1 GW Remedial Const Rpt																																																	
CL0245	EPA Approve Demo1 GW Remedial Construction Rpt	15	15	05MAY08	23MAY08	EPA Approve Demo1 GW Remedial Construction Rpt																																																	
Demolition Area 1																																																							
DL0000	Prepare/Submit Draft Demo 1 DD Amendment	45	45	31MAR08	02JUN08	Prepare/Submit Draft Demo 1 DD Amendment																																																	
DL0080	Agency Review/Approve Draft Demo1 DD Amendment	55*	55*	03JUN08	19AUG08	Agency Review/Approve Draft Demo1 DD Amendment																																																	
DL0100	Prepare/Submit Final Demo 1 DD Amendment	20	20	20AUG08	17SEP08	Prepare/Submit Final Demo 1 DD Amendment																																																	
DL0110	EPA Issue Demo 1 DD Amendment	15	15	18SEP08	08OCT08	EPA Issue Demo 1 DD Amendment																																																	
J-1 Range																																																							
CL0360	Prepare/Submit Draft J-1 South RRA GW COWR	66	21	15OCT07A	03MAR08	Prepare/Submit Draft J-1 South RRA GW COWR																																																	
CL0440	Agency Review/Approve Draft J-1 Sth RRA GW COWR	55*	55*	04MAR08	19MAY08	Agency Review/Approve Draft J-1 Sth RRA GW COWR																																																	
CL0460	Prepare/Submit Final J-1 South RRA GW COWR	20	20	20MAY08	17JUN08	Prepare/Submit Final J-1 South RRA GW COWR																																																	
U1100	Scoping MtgDraft J-1 Sth/Nth UXO SourceAssess WP	1	1	09JUN08*	09JUN08	Scoping MtgDraft J-1 Sth/Nth UXO SourceAssess WP																																																	
U1105	Prp/Sbmt Draft J-1 Sth/Nth UXO SourceAssess WP	30	30	10JUN08	22JUL08	Prp/Sbmt Draft J-1 Sth/Nth UXO SourceAssess WP																																																	
U1110	Agency Rev/Appr Drft J-1Sth/Nth UXO Source As WP	65	65	23JUL08	23OCT08	Agency Rev/Appr Drft J-1Sth/Nth UXO Source As WP																																																	
U1120	Prep/Sbmt Final J-1 Sth/Nth UXO SourceAssess WP	20	20	24OCT08	21NOV08	Prep/Sbmt Final J-1 Sth/Nth UXO SourceAssess WP																																																	
U1130	Incorporate J-1 Sth/Nth UXO Source Assessment WP	60	60	22NOV08	23JAN09	Incorporate J-1 Sth/Nth UXO Source Assessment WP																																																	
10066	Prepare/Submit Draft J-1 South RI/FS Rpt	373	235	16JUL07A	23JAN09	Prepare/Submit Draft J-1 South RI/FS Rpt																																																	
10071	Agency Review/Approve Drft J-1 South RI/FS	65*	65*	26JAN09	27APR09	Agency Review/Approve Drft J-1 South RI/FS																																																	
10088	Prepare/Submit Final J-1 South RI/FS Rpt	20	20	28APR09	26MAY09	Prepare/Submit Final J-1 South RI/FS Rpt																																																	

Activity ID	Activity Description	Orig Dur	Rem Dur	Anticipated /Actual Start	Anticipated /Actual Finish	FY08					FY09					FY10					FY11					FY12											
						F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S
10116	Prepare/Submit Draft J-1 North RI/FS Rpt	326	235	20SEP07A	23JAN09	██████████						* Prepare/Submit Draft J-1 North RI/FS Rpt																									
10121	Agency Review/Approve Draft J-1 North RI/FS	65*	65*	26JAN09	27APR09	██████████						* Agency Review/Approve Draft J-1 North RI/FS																									
10138	Prepare/Submit Final J-1 North RI/FS Rpt	20	20	28APR09	26MAY09	██████████						* Prepare/Submit Final J-1 North RI/FS Rpt																									
R1065	Prep/Subm Near Term Plume Migration Assess J-1N	41	41	01FEB08*	31MAR08	██████████						* Prep/Subm Near Term Plume Migration Assess J-1N																									
R1000	Prepare/Submit Draft J-1 North GW RRA	132	132	01AUG08*	10FEB09	██████████						* Prepare/Submit Draft J-1 North GW RRA																									
R1010	Agency Review/Approve Draft J-1 North GW RRA	65	65	11FEB09	13MAY09	██████████						* Agency Review/Approve Draft J-1 North GW RRA																									
R1040	Design J-1 North GW RRA	88	88	05MAR09	08JUL09	██████████						* Design J-1 North GW RRA																									
R1020	Prepare/Submit Final J-1 North GW RRA	20	20	14MAY09	11JUN09	██████████						* Prepare/Submit Final J-1 North GW RRA																									
R1060	Prepare/Submit Draft J-1 North GW RRA SPM Plan	60	60	26JUN09	21SEP09	██████████						* Prepare/Submit Draft J-1 North GW RRA SPM Plan																									
R1070	Agency Review/Approve Draft J-1N GW RRA SPM Plan	65	65	22SEP09	24DEC09	██████████						* Agency Review/Approve Draft J-1N GW RRA SPM Plan																									
R1050	Construct/Startup J-1 North GW RRA	243	243	28DEC09	13DEC10	██████████						* Construct/Startup J-1 North GW RRA Assumes 66 days for procurement under PBC																									
R1080	Prepare/Submit Final J-1 North GW RRA SPM Plan	20	20	28DEC09	25JAN10	██████████						* Prepare/Submit Final J-1 North GW RRA SPM Plan																									
R1090	Prep/Sub Draft J-1 North GW RRA COWR	60	60	15OCT10	12JAN11	██████████						* Prep/Sub Draft J-1 North GW RRA COWR																									
R1100	Agency Revw/Appr Draft J-1 North GW RRA COWR	65	65	13JAN11	14APR11	██████████						* Agency Revw/Appr Draft J-1 North GW RRA COWR																									
R1110	Prep/Sbmt Final J-1 North GW RRA COWR	20	20	15APR11	12MAY11	██████████						* Prep/Sbmt Final J-1 North GW RRA COWR																									
SL0090	Prepare/Submit Draft J-1 RSP	15	15	13MAY11	03JUN11	██████████						* Prepare/Submit Draft J-1 RSP Groundwater/UXO/Source																									
SL0100	Agency Review/Approve Draft J-1 RSP	55*	55*	06JUN11	22AUG11	██████████						* Agency Review/Approve Draft J-1 RSP																									
SL0110	Prepare/Submit Final J-1 RSP	10	10	23AUG11	06SEP11	██████████						* Prepare/Submit Final J-1 RSP																									
SL0120	Formal Public Comment J-1 RSP	30	30	07SEP11	06OCT11	██████████						* Formal Public Comment J-1 RSP																									
SL0130	Prepare/Submit Draft J-1 DD	20	20	07OCT11	04NOV11	██████████						* Prepare/Submit Draft J-1 DD																									
SL0140	Agency Review/Approve Draft J-1 DD	65*	65*	07NOV11	09FEB12	██████████						* Agency Review/Approve Draft J-1 DD																									
SL0150	Prepare/Submit Final J-1 DD	20	20	10FEB12	09MAR12	██████████						* Prepare/Submit Final J-1 DD																									
SL0160	EPA Issue J-1 DD	15	15	12MAR12	30MAR12	██████████						* EPA Issue J-1 DD																									

J-2 Range

J-2 Range Soil

PW1614	Conduct J-2 Supplemental Soil Investigation	386*	98*	11DEC06A	19JUN08	██████████						* Conduct J-2 Supplemental Soil Investigation														
U1200	Scoping Meeting Draft J-2 UXO Source AssessWP	1	1	22JUL08*	22JUL08	██████████						* Scoping Meeting Draft J-2 UXO Source AssessWP														
U1205	Prepare/Submit Draft J-2 UXO Source AssessWP	30	30	23JUL08	03SEP08	██████████						* Prepare/Submit Draft J-2 UXO Source AssessWP														
U1210	Agency Review/Appr Draft J-2 UXO SourceAssess.WP	65	65	04SEP08	08DEC08	██████████						* Agency Review/Appr Draft J-2 UXO SourceAssess.WP														
U1220	Prepare/Submit Final J-2 UXO Source Assess. WP	20	20	09DEC08	07JAN09	██████████						* Prepare/Submit Final J-2 UXO Source Assess. WP														
U1230	Incorporate J-2 UXO Source Assesment Work Plan	60	60	08JAN09	09MAR09	██████████						* Incorporate J-2 UXO Source Assesment Work Plan														

Activity ID	Activity Description	Orig Dur	Rem Dur	Anticipated /Actual Start	Anticipated /Actual Finish	FY08				FY09				FY10				FY11				FY12									
						F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M
00325	Prepare/Submit Draft J-2 UXO/Source RI/FS Rpt	179	179	20JUN08	09MAR09																										
00329	Agency Rvw/Approve Draft J-2 UXO/Source RI/FS Rt	65*	65*	10MAR09	09JUN09																										
J20038	Prepare/Submit Final J-2 UXO/Source RI/FS Rpt	20	20	10JUN09	08JUL09																										
J-2 Range Groundwater																															
00353	Agency Review/Approve J-2 GW RI/FS Rpt	267*	5*	18JAN07A	07FEB08																										
0698	Prepare/Submit Interim Final J-2 GW RI/FS Rpt	20	20	08FEB08	07MAR08																										
00369	Construct/Startup J-2 Range GW Treatment System	254*	153*	06SEP07A	08SEP08																										
CL0580	Agency Review/Approve Draft J-2E SPM Plan	137*	0*	29JUN07A	16JAN08A																										
CL0600	Prepare/Submit Final J-2E SPM Plan	20	10	17JAN08A	14FEB08																										
CL0605	Prep/Sub Draft J-2 Remedial Construction Rpt	60	60	14JUL08	06OCT08																										
CL0615	Agency Revw/Appr Draft J-2 Remedial Const Rpt	55	55	07OCT08	26DEC08																										
CL0625	Prepare/Submit Final J-2 Remedial Const Rpt	20	20	29DEC08	26JAN09																										
CL0635	EPA Approve Final J-2 Remedial Construction Rpt	15	15	27JAN09	17FEB09																										
J-2 Range																															
CL1200	Prepare/Submit Draft J-2 RSP	10	10	09JUL09	22JUL09																										
CL1280	Agency Review/Approve Draft J-2 RSP	50*	50*	23JUL09	01OCT09																										
CL1300	Prepare/Submit Final J-2 RSP	10	10	02OCT09	16OCT09																										
CL1305	Formal Public Comment J-2 RSP	30	30	17OCT09	16NOV09																										
SL0300	Prepare/Submit Draft J-2 DD	45	45	17NOV09	21JAN10																										
SL0310	Agency Review/Approve Draft J-2 DD	65*	65*	22JAN10	23APR10																										
SL0330	Prepare/Submit Final J-2 DD	20	20	26APR10	21MAY10																										
SL0340	EPA Issue J-2 DD	15	15	24MAY10	14JUN10																										
J-3 Range																															
J-3 Range Soil																															
U1300	Scoping Mtg Draft J-3 UXO Source Assess WP	1	1	25APR08*	25APR08																										
U1305	Prepare/Submit Draft J-3 UXO Source Assess WP	30	30	28APR08	09JUN08																										
U1310	Agency Review/Appr Draft J-3 UXO SourceAssess.WP	65	65	10JUN08	10SEP08																										
U1320	Prepare/Submit Final J-3 UXO Source Assess WP	20	20	11SEP08	08OCT08																										
U1330	Incorporate J-3 UXO Source Assessment Work Plan	60	60	09OCT08	10DEC08																										
U1340	Prepare/Submit Draft J-3 UXO/Source RI	60	60	09OCT08	10DEC08																										
U1350	Agency Review/Appr Draft J-3 UXO/Source RI	65	65	11DEC08	16MAR09																										
U1360	Prepare/Submit Final J-3 UXO/Source RI	20	20	17MAR09	13APR09																										

Activity ID	Activity Description	Orig Dur	Rem Dur	Anticipated /Actual Start	Anticipated /Actual Finish	FY08												FY09												FY10												FY11												FY12											
						F M A M J J J A S O N D												F M A M J J J A S O N D												F M A M J J J A S O N D												F M A M J J J A S O N D												F M A M J J J A S O N D											
						F	M	A	M	J	J	A	S	O	N	D	F	M	A	M	J	J	A	S	O	N	D	F	M	A	M	J	J	A	S	O	N	D	F	M	A	M	J	J	A	S	O	N	D	F	M	A	M	J	J	A	S	O	N	D					
U1370	Prepare/Submit Draft J-3 UXO/Source FS	60	60	14APR09	08JUL09	Prepare/Submit Draft J-3 UXO/Source FS																																																											
U1380	Agency Review/Apr Draft J-3 UXO/Source FS	65	65	09JUL09	08OCT09	Agency Review/Apr Draft J-3 UXO/Source FS																																																											
U1390	Prepare/Submit Final J-3 UXO/Source FS	20	20	09OCT09	06NOV09	Prepare/Submit Final J-3 UXO/Source FS																																																											
J-3 Range Groundwater																																																																	
10009	Agency Review/Approve Draft J-3 GW RI/FS Report	295*	5*	07DEC06A	07FEB08	Agency Review/Approve Draft J-3 GW RI/FS Report																																																											
10020	Prepare/Submit Interim Final J-3 GW RI/FS Report	20	20	08FEB08	07MAR08	Prepare/Submit Interim Final J-3 GW RI/FS Report (interim pending UXO/Source RI results)																																																											
J-3 Range																																																																	
DL0500	Prepare/Submit Draft J-3 RSP	10	10	09NOV09	23NOV09	Prepare/Submit Draft J-3 RSP																																																											
DL0530	Agency Review/Approve Draft J-3 RSP	55*	55*	24NOV09	11FEB10	Agency Review/Approve Draft J-3 RSP																																																											
DL0550	Prepare/Submit Final J-3 RSP	10	10	12FEB10	26FEB10	Prepare/Submit Final J-3 RSP																																																											
DL0560	Formal Public Comment J-3 RSP	30	30	27FEB10	28MAR10	Formal Public Comment J-3 RSP																																																											
DL0570	Prepare/Submit Draft J-3 DD	20	20	29MAR10	23APR10	Prepare/Submit Draft J-3 DD																																																											
DL0620	Agency Review/Approve Draft J-3 DD	65*	65*	26APR10	27JUL10	Agency Review/Approve Draft J-3 DD																																																											
DL0640	Prepare/Submit Final J-3 DD	20	20	28JUL10	24AUG10	Prepare/Submit Final J-3 DD																																																											
DL0650	EPA Issue J-3 DD	15	15	25AUG10	15SEP10	EPA Issue J-3 DD																																																											
L Range																																																																	
U1400	Prepare/Submit Draft L UXO Source Assess. WP	86*	11*	15OCT07A	15FEB08	Prepare/Submit Draft L UXO Source Assess. WP																																																											
U1410	Agency Review/Apr Draft L UXO Source Assess. WP	65	65	19FEB08	19MAY08	Agency Review/Apr Draft L UXO Source Assess. WP																																																											
U1420	Prepare/Submit Final L UXO Source Assessment WP	20	20	20MAY08	17JUN08	Prepare/Submit Final L UXO Source Assessment WP																																																											
U1430	Incorporate L UXO Source Assessment Work Plan	60	60	18JUN08	11SEP08	Incorporate L UXO Source Assessment Work Plan																																																											
0703	Prepare/Submit Draft L RI/FS Rpt	260	80	15MAY07A	11SEP08	Prepare/Submit Draft L RI/FS Rpt Groundwater, UXO, Source																																																											
0724	Agency Review/Approve Draft L RI/FS Rpt	65*	65*	12SEP08	16DEC08	Agency Review/Approve Draft L RI/FS Rpt																																																											
0722	Prepare/Submit Final L RI/FS Rpt	20	20	17DEC08	15JAN09	Prepare/Submit Final L RI/FS Rpt																																																											
SL0382	Prepare/Submit Draft L RSP	15	15	16JAN09	05FEB09	Prepare/Submit Draft L RSP																																																											
SL0383	Agency Review/Approve Draft L RSP	55	55	06FEB09	24APR09	Agency Review/Approve Draft L RSP																																																											
SL0384	Prepare/Submit Final L RSP	10	10	27APR09	08MAY09	Prepare/Submit Final L RSP																																																											
SL0386	Formal Public Comment L RSP	30	30	09MAY09	08JUN09	Formal Public Comment L RSP																																																											
SL0388	Prepare/Submit Draft L DD	20	20	09JUN09	07JUL09	Prepare/Submit Draft L DD																																																											
SL0391	Agency Review/Approve Draft L DD	65*	65*	08JUL09	07OCT09	Agency Review/Approve Draft L DD																																																											
SL0392	Prepare/Submit Final L DD	20	20	08OCT09	05NOV09	Prepare/Submit Final L DD																																																											
SL0394	EPA Issue L DD	15	15	06NOV09	30NOV09	EPA Issue L DD																																																											

Activity ID	Activity Description	Orig Dur	Rem Dur	Anticipated /Actual Start	Anticipated /Actual Finish	FY08				FY09				FY10				FY11				FY12															
						F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S
SL0400	Prepare/Submit Draft L LTM Plan	60	60	01DEC09	25FEB10																																
SL0410	Agency Review/Approve Draft L LTM Plan	55*	55*	26FEB10	13MAY10																																
SL0420	Prepare/Submit Final L LTM Plan	20	20	14MAY10	11JUN10																																
Central Impact Area																																					
00261	Prepare/Submit Draft CIA UXO/Source Investig Rt	920	0	04APR04A	08JAN08A																																
00263	Agency Rvw/Approve Draft CIA UXO/Source Investig	65	50	09JAN08A	11APR08																																
00299	Prepare/Submit Final CIA UXO/Source Investig Rpt	20	20	14APR08	09MAY08																																
22130	Agency Review/Approve CIA Dft FS Scrn Rpt	85	44	16APR07A	03APR08																																
22135	Prep/Sbmt Near Term Plume Migration Assess CIA	41	41	01FEB08*	31MAR08																																
22131	Prepare/Submit Final CIA Dft FS Scrn Rpt	20	20	04APR08	01MAY08																																
22210	Prepare/Submit Draft CIA FS	206*	206*	05MAY08	27FEB09																																
22230	Agency Review/Approve Draft CIA FS	85	85	02MAR09	29JUN09																																
22231	Prepare/Submit Final CIA FS	20	20	30JUN09	28JUL09																																
R2000	Prepare/Submit Draft CIA RRA	110*	110*	27AUG08*	04FEB09																																
R2010	Agency Review/Approve Draft CIA RRA	65	65	05FEB09	07MAY09																																
R2020	Prepare/Submit Final CIA RRA	20	20	08MAY09	05JUN09																																
R2030	Design CIA RRA	120	120	08JUN09	27NOV09																																
R2050	Prepare/Submit Draft CIA GW RRA SPM Plan	60	60	07DEC09	03MAR10																																
R2060	Agency Review/Approve Draft CIA GW RRA SPM Plan	65	65	04MAR10	03JUN10																																
R2070	Prepare/Submit Final CIA GW RRA SPM Plan	20	20	04JUN10	01JUL10																																
R2040	Construct/Startup CIA RRA	121	121	02JUL10	27DEC10																																
R2080	Prep/Sub Draft CIA COWR	60	60	28OCT10	25JAN11																																
R2090	Agency Revw/Appr Draft CIA COWR	65	65	26JAN11	27APR11																																
R2100	Prep/Sbmt Final CIA COWR	20	20	28APR11	25MAY11																																
32510	Prepare/Submit Draft CIA RSP	30	30	30JUN09	11AUG09																																
32520	Agency Review/Approve Draft CIA RSP	55	55	12AUG09	29OCT09																																
32530	Prepare/Submit Final CIA RSP	20	20	30OCT09	30NOV09																																
32540	Formal Public Comment CIA RSP	30	30	01DEC09	31DEC09																																
CI0080	Prepare/Submit Draft CIA DD	40	40	01DEC09	27JAN10																																
CI0090	Agency Review/Approve Draft CIA DD	65	65	28JAN10	29APR10																																

Activity ID	Activity Description	Orig Dur	Rem Dur	Anticipated /Actual Start	Anticipated /Actual Finish	FY08			FY09			FY10			FY11			FY12														
						F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A
WB1022	Prepare/Submit Draft Western Boundary RSP	30	30	04MAR08	14APR08	Prepare/Submit Draft Western Boundary RSP																										
WB1024	Agency Review/Approve Draft Western Boundary RSP	55*	55*	15APR08	01JUL08	Agency Review/Approve Draft Western Boundary RSP																										
WB1026	Prepare/Submit Final Western Boundary RSP	10	10	02JUL08	16JUL08	Prepare/Submit Final Western Boundary RSP																										
WB1028	Formal Public Comment Western Boundary RSP	30	30	17JUL08	15AUG08	Formal Public Comment Western Boundary RSP																										
WB4010	Prepare/Submit Draft Western Boundary DD	20	20	18AUG08	15SEP08	Prepare/Submit Draft Western Boundary DD																										
WB4060	Agency Review/Approve Draft Western Boundary DD	65*	65*	16SEP08	18DEC08	Agency Review/Approve Draft Western Boundary DD																										
WB4080	Prepare/Submit Final Western Boundary DD	20	20	19DEC08	19JAN09	Prepare/Submit Final Western Boundary DD																										
WB4090	EPA Issue Western Boundary DD	15	15	20JAN09	09FEB09	EPA Issue Western Boundary DD																										
WB4220	Prepare/Submit Draft Western Boundary LTM Plan	45	45	10FEB09	14APR09	Prepare/Submit Draft Western Boundary LTM Plan																										
WB4300	Agency Review/Approve Draft Western Bnd LTM Plan	55*	55*	15APR09	01JUL09	Agency Review/Approve Draft Western Bnd LTM Plan																										
WB4320	Prepare/Submit Final Western Boundary LTM Plan	20	20	02JUL09	30JUL09	Prepare/Submit Final Western Boundary LTM Plan																										
Demo 2																																
01574	Prepare/Submit Draft Demo 2 RI/FS Rpt	268*	56*	30MAR07A	21APR08	Prepare/Submit Draft Demo 2 RI/FS Rpt																										
01578	Agency Review/Approve Draft Demo 2 RI/FS Rpt	65*	65*	22APR08	23JUL08	Agency Review/Approve Draft Demo 2 RI/FS Rpt																										
01579	Prepare/Submit Final Demo 2 RI/FS Rpt	20	20	24JUL08	20AUG08	Prepare/Submit Final Demo 2 RI/FS Rpt																										
01608	Prepare/Submit Draft Demo 2 RSP	30	30	21AUG08	02OCT08	Prepare/Submit Draft Demo 2 RSP																										
01609	Agency Review/Approve Draft Demo 2 RSP	55*	55*	03OCT08	23DEC08	Agency Review/Approve Draft Demo 2 RSP																										
01611	Prepare/Submit Final Demo 2 RSP	20	20	24DEC08	22JAN09	Prepare/Submit Final Demo 2 RSP																										
01613	Formal Public Comment Demo 2 RSP	30	30	23JAN09	22FEB09	Formal Public Comment Demo 2 RSP																										
01615	Prepare/Submit Draft Demo 2 DD	20	20	23FEB09	20MAR09	Prepare/Submit Draft Demo 2 DD																										
01623	Agency Review/Approve Demo 2 DD	65*	65*	23MAR09	22JUN09	Agency Review/Approve Demo 2 DD																										
01624	Prepare/Submit Final Demo 2 DD	20	20	23JUN09	21JUL09	Prepare/Submit Final Demo 2 DD																										
01625	EPA Issue Demo 2 DD	15	15	22JUL09	11AUG09	EPA Issue Demo 2 DD																										
2D0100	Prepare/Submit Draft Demo 2 LTM Plan	45	45	12AUG09	15OCT09	Prepare/Submit Draft Demo 2 LTM Plan																										
2D0110	Agency Review/Approve Draft Demo 2 LTM Plan	55*	55*	16OCT09	06JAN10	Agency Review/Approve Draft Demo 2 LTM Plan																										
2D0120	Prepare/Submit Final Demo 2 LTM Plan	20	20	07JAN10	03FEB10	Prepare/Submit Final Demo 2 LTM Plan																										
Gun & Mortar																																
00608	Agency Review/Approve Draft G&M Invest Workplan	272*	27*	12FEB07A	11MAR08	Agency Review/Approve Draft G&M Invest Workplan																										
00619	Prepare Final G&M Investigation Workplan	20	20	12MAR08	08APR08	Prepare Final G&M Investigation Workplan																										
CL2116	Conduct G&M Investigation	269	111	19MAR07A	11JUL08	Conduct G&M Investigation																										

Activity ID	Activity Description	Orig Dur	Rem Dur	Anticipated /Actual Start	Anticipated /Actual Finish	FY08												FY09												FY10												FY11												FY12																							
						J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D												
00601	Prepare Draft Investigation Report	130	130	14JUL08	19JAN09													Prepare Draft Investigation Report																																																											
CL1760	Prepare/Submit Draft G&M Soil RRA Plan	61	61	20JAN09	15APR09													Prepare/Submit Draft G&M Soil RRA Plan																																																											
CL1840	Agency Review/Approve Draft G&M Soil RRA Plan	65*	65*	16APR09	17JUL09													Agency Review/Approve Draft G&M Soil RRA Plan																																																											
CL1845	Informal Public Comment G&M Soil RRA Plan	15	15	21MAY09	05JUN09													Informal Public Comment G&M Soil RRA Plan																																																											
CL1860	Prepare/Submit Final G&M Soil RRA Plan	20	20	20JUL09	14AUG09													Prepare/Submit Final G&M Soil RRA Plan																																																											
00571	Conduct G&M Soil RRA	132	132	03AUG09	10FEB10													Conduct G&M Soil RRA																																																											
CL1900	Prepare/Submit Draft G&M Soil COWR	60	60	11FEB10	06MAY10													Prepare/Submit Draft G&M Soil COWR																																																											
CL1990	Agency Review/Approve Draft G&M Soil COWR	55*	55*	07MAY10	26JUL10													Agency Review/Approve Draft G&M Soil COWR																																																											
CL2000	Prepare/Submit G&M Final Soil COWR	20	20	27JUL10	23AUG10													Prepare/Submit G&M Final Soil COWR																																																											
00555	Prep/Submt Revised Draft G&M Investigation Rpt	110	110	11FEB10	19JUL10													Prep/Submt Revised Draft G&M Investigation Rpt																																																											
00557	Agency Review/Approve Draft G&M Investig Rpt	65*	65*	20JUL10	20OCT10													Agency Review/Approve Draft G&M Investig Rpt																																																											
00560	Prepare Final G&M Investigation Report	20	20	21OCT10	18NOV10													Prepare Final G&M Investigation Report																																																											
CL2230	Prepare/Submit Draft G&M DD	20	20	19NOV10	17DEC10													Prepare/Submit Draft G&M DD																																																											
CL2280	Agency Review/Approve Draft G&M DD	65*	65*	20DEC10	23MAR11													Agency Review/Approve Draft G&M DD																																																											
CL2310	Prepare/Submit Final G&M DD	20	20	24MAR11	20APR11													Prepare/Submit Final G&M DD																																																											
CL2320	EPA Issue G&M DD	15	15	21APR11	11MAY11													EPA Issue G&M DD																																																											
Former A Range																																																																													
U1600	Scoping Mtg Draft Former A UXO Source Assess WP	1	1	14MAR08*	14MAR08	Scoping Mtg Draft Former A UXO Source Assess WP																																																																							
U1605	Prep/Submit Draft Former A UXO Source Assess WP	30	30	17MAR08	25APR08	Prep/Submit Draft Former A UXO Source Assess WP																																																																							
U1610	Agency Rev/Appr Draft Fmr A UXO Source Assess.WP	65	65	28APR08	29JUL08	Agency Rev/Appr Draft Fmr A UXO Source Assess.WP																																																																							
U1620	Prep/Submit Final Former A UXO Source Assess WP	20	20	30JUL08	26AUG08	Prep/Submit Final Former A UXO Source Assess WP																																																																							
U1630	Incorporate Former A UXO Source Assess Work Plan	60	60	27AUG08	27OCT08	Incorporate Former A UXO Source Assess Work Plan																																																																							
01586	Prepare/Submit Draft Former A RI/FS Rpt	448	52	09MAR06A	27OCT08	Prepare/Submit Draft Former A RI/FS Rpt UXO/Source																																																																							
01588	Agency Review/Approve Former A RI/FS Rpt	65	65	28OCT08	30JAN09	Agency Review/Approve Former A RI/FS Rpt																																																																							
01562	Prepare/Submit Final Former A RI/FS Rpt	20	20	02FEB09	02MAR09	Prepare/Submit Final Former A RI/FS Rpt																																																																							
FA0400	Prepare/Submit Draft Former A RSP	15	15	03MAR09	23MAR09	Prepare/Submit Draft Former A RSP																																																																							
FA0410	Agency Review/Approve Draft Former A RSP	55	55	24MAR09	09JUN09	Agency Review/Approve Draft Former A RSP																																																																							
FA0420	Prepare/Submit Final Former A RSP	10	10	10JUN09	23JUN09	Prepare/Submit Final Former A RSP																																																																							
FA0430	Formal Public Comment Former A RSP	30	30	24JUN09	24JUL09	Formal Public Comment Former A RSP																																																																							
FA0500	Prepare/Submit Draft Former A DD	20	20	27JUL09	21AUG09	Prepare/Submit Draft Former A DD																																																																							

Activity ID	Activity Description	Orig Dur	Rem Dur	Anticipated /Actual Start	Anticipated /Actual Finish	FY08					FY09					FY10					FY11					FY12																	
						F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M
Wide Area Source Assessment																																											
02806	Agency Review/Approve Draft WASA Workplan	711*	68*	13JUL05A	07MAY08	* Agency Review/Approve Draft WASA Workplan																																					
TC00815	Prepare/Submit Final WASA Workplan	20	20	08MAY08	05JUN08	* Prepare/Submit Final WASA Workplan																																					
WA0002	Conduct WASA Investigation	85	85	06JUN08	06OCT08	* Conduct WASA Investigation																																					
WA0004	Prepare/Submit Draft WASA Investigation Rpt	135	135	07OCT08	21APR09	* Prepare/Submit Draft WASA Investigation Rpt																																					
WA0006	Agency Review/Approve Draft WASA Investigation	65	65	22APR09	23JUL09	* Agency Review/Approve Draft WASA Investigation																																					
WA0008	Prepare Final WASA Investigation Report	20	20	24JUL09	20AUG09	* Prepare Final WASA Investigation Report																																					
WA0000	Prepare/Submit Draft WASA Soil RRA Plan	60	60	07OCT08	05JAN09	* Prepare/Submit Draft WASA Soil RRA Plan																																					
WA0010	Agency Review/Approve Draft WASA Soil RRA Plan	55	55	06JAN09	24MAR09	* Agency Review/Approve Draft WASA Soil RRA Plan																																					
WA0020	Informal Public Comment WASA Soil RRA Plan	15	15	27JAN09	10FEB09	* Informal Public Comment WASA Soil RRA Plan																																					
WA0030	Prepare/Submit Final WASA Soil RRA Plan	20	20	25MAR09	21APR09	* Prepare/Submit Final WASA Soil RRA Plan																																					
WA0040	Conduct WASA Soil RRA	30	30	22APR09	03JUN09	* Conduct WASA Soil RRA																																					
WA0050	Prepare/Submit Draft WASA Soil COWR	60	60	04JUN09	27AUG09	* Prepare/Submit Draft WASA Soil COWR																																					
WA0060	Agency Review/Approve Draft WASA Soil COWR	55	55	28AUG09	17NOV09	* Agency Review/Approve Draft WASA Soil COWR																																					
WA0070	Prepare/Submit WASA Final Soil COWR	20	20	18NOV09	16DEC09	* Prepare/Submit WASA Final Soil COWR																																					
WA0080	Prepare/Submit Draft WASA NFA DD	45	45	17DEC09	22FEB10	* Prepare/Submit Draft WASA NFA DD																																					
WA0090	Agency Review/Approve Draft WASA NFA DD	65	65	23FEB10	24MAY10	* Agency Review/Approve Draft WASA NFA DD																																					
WA0110	Prepare/Submit Final WASA NFA DD	20	20	25MAY10	22JUN10	* Prepare/Submit Final WASA NFA DD																																					
WA0120	EPA Issue WASA NFA DD	15	15	23JUN10	14JUL10	* EPA Issue WASA NFA DD																																					
